# Project Overview Report
## July 15, 2011

A total of 329 projects are currently in the MSBA's Capital Pipeline. As of this report, 13 of the 37 Closeout/Audit Complete projects have been approved for final MSBA approved grants and thus, with the fiscal year end, will be removed from future reports. The following summary table provides the category (e.g., New Program, Green Repair) and the number of projects in each phase (e.g., Local Clearance, Construction):

| | Total | Local Clearance | Consultant Selection | Feasibility Study/ Schematic Design | Design Development | Construction |
|---|---|---|---|---|---|---|
| **Closeout/Audit Complete** | 37 | | | | | |
| **New Program** | 122 | 17 | 21 | 25 | 20 | 39 |
| **Waitlist** | 9 | 0 | 2 | 0 | 1 | 6 |
| **Green Repair** | 161 | 1 | 0 | 48 | 62 | 50 |
| **Total** | 329 | 18 | 23 | 73 | 83 | 95 |

The MSBA utilizes the Capital Pipeline Project Status chart (see attached) to account for the ongoing status of all District SOIs in the pipeline. Activity for some of the key milestones is summarized in the table below with the numbers reported indicative of the category requirements. For instance, enrollment certifications are not required for all projects (e.g., repairs) and Owner's Project Managers ("OPMs") are not always mandatory for construction projects under $1.5 million unless required by the MSBA.

Critical Prerequisites:

An agreed-upon enrollment is a key prerequisite for the MSBA to commence a Feasibility Study with a District. To begin the enrollment projection process, a District must file enrollment information utilizing the MSBA's online enrollment projection tool.

After the MSBA and the District have agreed upon an enrollment to be used as the design basis and executed a Feasibility Study Agreement, the District procures consultants, starting with an Owner's Project Manager. Currently, there are 17 Districts in the Capital Pipeline who still need to procure an OPM.

After a District has selected an OPM and executed a contract with that OPM, it is ready for the selection of a Designer utilizing either a local designer selection process for projects under $5 million or the MSBA's Designer Selection Panel for projects over $5 million. Currently, there are 31 Districts in the Capital Pipeline who still need to procure a Designer.

| | District Action to complete | MSBA/ District Collaboration | Completed Activity this Period | Total Completed to Date | Total |
|---|---|---|---|---|---|
| Enrollment | 10 | 21 | 3 | 111 | 71,355 |
| Owner's Project Manager | 17 | 14 | 7 | 104 | Over $84 million in OPM fees* |
| Designer | 31 | 9 | 2 | 132 | Over $207.6 million in Designer Fees* |

* Does not include OPM and Designer Fees associated with repair projects.

## Owner's Project Managers

Since the last report, the following 7 Districts have completed the OPM selection process:

- Chicopee – Chicopee Middle School
- Lynnfield – Lynnfield High School
- W. Bridgewater – W. Bridgewater High School
- Wakefield – Galvin Middle School
- Marshfield – Marshfield High School (Model School)
- Greater New Bedford – Greater New Bedford Vocational Technical High School
- Somerset-Berkley – Somerset-Berkley Regional High School (Model School)

The following Districts are tentatively scheduled for the upcoming OPM Review Panel meetings:

| Panel Date | District/School | Project Description Status | Estimated Project Cost |
|---|---|---|---|
| 8/1/11 | Lexington / Estabrook ES | Feasibility Study | $20-$30mil |
| 9/12/11 | Berkshire Hill RSD/ Monument Regional HS | Feasibility Study | $25-$30mil |
| 9/12/11 | Auburn/ Auburn Middle School | Feasibility Study | $20-$40mil |
| 9/12/11 | Andover / Bancroft ES | Design Development | $45mil |
| 9/12/11 | Newburyport / R.A. Nock MS | Feasibility Study | $12-$18mil |
| 9/12/11 | Newburyport/ F.T. Bresnahan ES | Model School | $25-$35mil |
| 10/3/11 | Greater Lowell / Greater Lowell RVT | Feasibility Study | $30-$40 mil |
| 10/3/11 | Whitman Hanson / Maquan ES | Feasibility Study | $20-$30mil |

## Designers

Since the last report, the DSP has met once resulting in two additional Districts completing the Designer selection process.

| Panel Date | District/School | Status | Estimated Project Cost | # of Proposals Received | Top 3-Ranked Firms | Interviews Requested | First-Ranked Selection |
|---|---|---|---|---|---|---|---|
| 7/19/2011 | Georgetown – Penn Brook IS | Designer Selection | $20m - $40m | 11 | - DRA<br>- Flansburgh<br>- Dore & Whittier | No | DRA |
| 7/19/2011 | Wakefield – Galvin Middle School | Designer Selection | TBD | 10 | - Tappe<br>- DRA<br>- Mount Vernon | No | Tappe |

The following Districts are tentatively scheduled for upcoming DSP meetings:

West Bridgewater PS – West Bridgewater J/SHS – August 2, 2011
Webster PS – Park Avenue Elementary School – August 23, 2011
Lexington PS – Estabrook Elementary School – August 23, 2011
Boston PS – Quincy Upper School – TBD
Chicopee PS – Chicopee MS – TBD
Lynnfield PS – Lynnfield HS – TBD
Winthrop PS – Winthrop Sr High School (R) – TBD

## Commissioning

Since the last report, the MSBA has assigned Commissioning Consultants to an additional 43 projects as presented in the table below. The MSBA has executed 128 Commissioning Consultant contracts to date, totaling $10.6 million.

| District | School | Estimated Const. Cost (millions) | Commissioning Consultant | Contract Amount |
|---|---|---|---|---|
| Framingham PS | Mary E Stapleton ES | $0.82 | CBI Consulting Inc. | $29,000 |
| Melrose PS | Melrose HS | $0.87 | Russo Barr Associates, Inc. | $28,500 |
| Needham PS | Pollard MS | $2.81 | CBI Consulting Inc. | $27,400 |
| Andover PS | Andover West MS | $1.32 | Simpson Gumpertz & Heger | $36,000 |
| Reading PS | Green Repair - Multiple Schools | $1.73 | Russo Barr Associates, Inc. | $37,650 |
| Amherst-Pelham PS | Amherst Reg MS | $1.32 | Russo Barr Associates, Inc. | $27,100 |
| Leverett PS | Leverett ES | $0.37 | Russo Barr Associates, Inc. | $21,000 |
| West Springfield PS | West Springfield HS | $73.30 | Turner Fac. Mgmnt Solutions | $193,143 |
| Springfield PS | Forest Park Middle School | $34.00 | Foreman Building Commissioning | $111,600 |
| Leicester PS | Leicester MS | $1.14 | Cannon Design | $22,900 |
| Billerica PS | Billerica Memorial HS | $0.63 | VP Consultants, LLC | $24,500 |
| Springfield PS | Green Repair - Multiple Schools | $12.82 | VP Consultants, LLC | $190,000 |
| Gloucester PS | Green Repair - Multiple Schools | $4.03 | Russo Barr Associates, Inc. | $39,650 |
| Brockton PS | Green Repair - Multiple Schools | $26.96 | Simpson Gumpertz & Heger | $241,000 |
| North Brookfield PS | North Brookfield ES | $0.36 | Simpson Gumpertz & Heger | $22,500 |
| Plymouth PS | Plymouth Community IS | $3.98 | VP Consultants, LLC | $29,500 |
| Brockton PS | Green Repair - Multiple Schools | $5.60 | RFS Engineering | $50,450 |
| Wachusett PS | Green Repair - Multiple Schools | $4.30 | RFS Engineering | $75,200 |
| Avon PS | Ralph D Butler ES | $0.76 | Cannon Design | $15,100 |
| Weymouth PS | Abigail Adams MS | $0.71 | Cannon Design | $17,700 |
| Boston PS | Green Repair - Multiple Schools | $2.88 | RFS Engineering | $10,500 |
| Grafton PS | South Grafton ES | $0.18 | Horizon Engineering Associates | $7,250 |
| Sharon PS | Sharon HS | $2.96 | Cannon Design | $47,600 |
| Canton PS | Green Repair - Multiple Schools | $0.56 | Cannon Design | $22,400 |
| Central Berkshire PS | Green Repair - Multiple Schools | $1.66 | Strategic Building Solutions | $28,743 |
| Upper Cape Cod Voc Tech PS | Upper Cape Cod Voc / Tech HS | $1.55 | Gale Associates, Inc. | $17,000 |
| Blackstone Valley Reg PS | Blackstone Valley HS | $0.61 | Cannon Design | $19,100 |
| Fitchburg PS | Fitchburg HS | $1.52 | RDK Engineering | $15,760 |
| Pentucket PS | Green Repair - Multiple Schools | $1.12 | RDK Engineering | $33,500 |
| Westfield PS | Green Repair - Multiple Schools | $10.22 | Strategic Building Solutions | $65,365 |
| Fitchburg PS | Green Repair - Multiple Schools | $4.92 | Simpson Gumpertz & Heger | $93,000 |
| Falmouth PS | Green Repair - Multiple Schools | $0.49 | Gale Associates, Inc. | $24,650 |
| Boston PS | Green Repair - Multiple Schools | $5.77 | Simpson Gumpertz & Heger | $96,500 |
| Abington PS | Woodsdale IS | $1.01 | Russo Barr Associates, Inc. | $25,950 |
| Pentucket PS | Green Repair - Multiple Schools | $6.17 | CBI Consulting Inc. | $97,300 |
| Dartmouth PS | James M. Quinn ES | $1.16 | Gale Associates, Inc. | $19,450 |

| District | School | Estimated Const. Cost (millions) | Commissioning Consultant | Contract Amount |
|---|---|---|---|---|
| Rockland PS | R Stewart Esten ES | $0.24 | Russo Barr Associates, Inc. | $14,300 |
| Greenfield PS | Four Corners ES | $1.53 | Strategic Building Solutions | $19,271 |
| Sandwich PS | Green Repair - Multiple Schools | $4.56 | Gale Associates, Inc. | $37,850 |
| Quincy PS | Central MS | $32.60 | Sebesta Blomberg & Associates | $94,132 |
| Brookline PS | Heath K-8 | $7.02 | Consulting Engineering Services | $45,898 |
| Southeastern Reg VoTech PS | Southeastern Regional VoTech HS | $26.58 | RDK Engineering | $151,605 |
| North Attleborough PS | Falls ES | $0.50 | Gale Associates, Inc. | $30,600 |
| | **Total** | **$293.60** | **Total** | **$2,257,617** |

Projects for which we are currently seeking proposals and/or negotiating Work Orders include:

| District | School | Responses Due |
|---|---|---|
| Norton PS | Norton HS | 7/22/11 |
| Fall River PS | Morton MS | 7/22/11 |

Projects that are currently in the queue for assignment of a Commissioning Consultant and for which contract documents are being drafted include:


| District | School |
|---|---|
| Marblehead PS | Glover Primary |
| Arlington PS | Thompson ES |
| Duxbury PS | Duxbury MS/HS |
| Fairhaven PS | Rogers ES |
| Narragansett PS | Templeton Center |
| Somerset Berkley | Somerset Berkley HS |
| Cape Cod Reg VoTech | Cape Cod Reg VTHS |
| Grafton | Grafton SHS |
| Haverhill | Green Repair - Multiple Schools |
| Lowell | Green Repair - Multiple Schools |
| Middleborough | Mary K. Goode Elementary School |
| Mohawk Trail | Green Repair - Multiple Schools |
| Nauset | Nauset Regional High |
| North Middlesex | Green Repair - Multiple Schools |
| Northborough | Robert E. Melican Middle School |
| Peabody | Green Repair - Multiple Schools |
| Salem | Green Repair - Multiple Schools |
| Westport | Green Repair - Multiple Schools |
| West Boylston | Green Repair - Multiple Schools |

Attached to the Project Overview Report are the following:

- Master District Status List
- Capital Pipeline Project Status Chart: As indicated in the attached chart, Districts continue to make progress with their projects. The narrow solid bar indicates the number of Districts in each category as reported at the June Board meeting.
- 2011 Estimated Bid Dates Schedule:
  - New Program
  - Green Repair Program
- Projects in Construction Report

**Status of Green Repair Program**

At the July 27, 2011 meeting of the Board of Directors, MSBA staff will be recommending Project Funding Agreements ("PFAs") for 12 districts, representing 23 projects totaling $87,021,917 in MSBA Total Facilities Grants. With the Board's approval, 158 projects will have received authorization to enter into a PFA, totaling $372,416,260 in Total Project Costs and $223,348,649 in MSBA Total Facilities Grant funding.

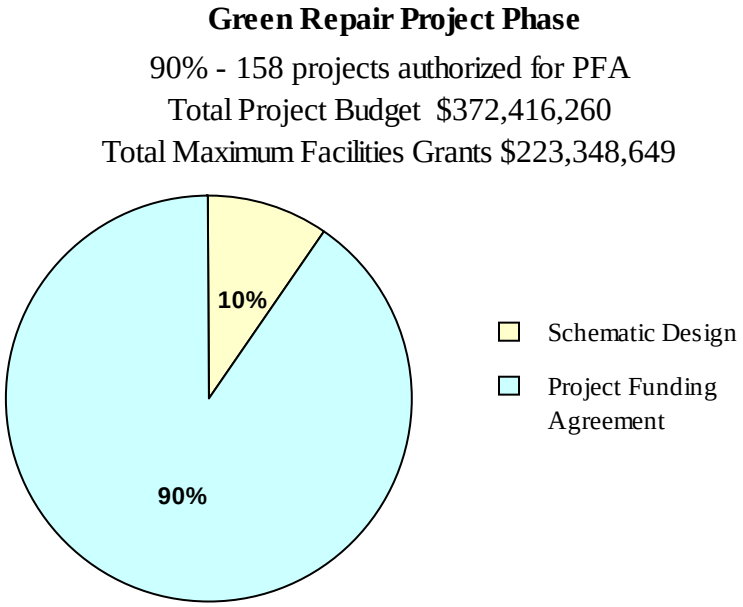


**Anticipated Construction Bids – Summer 2011**

Based on current schedule information, 38 roof projects, 18 window projects and 10 boiler projects will go out to bid this summer.

| | Roofs | Windows | Boilers |
|---|---|---|---|
| June | 20 | 13 | 5 |
| July | 18 | 5 | 5 |
| August | 0 | 0 | 0 |
| **Total** | **38** | **18** | **10** |

The following chart represents the bid results received by the MSBA as of July 21, 2011.

| | | Bids Received Prior to May 1, 2011 | | Bids Received Between May 1, 2011 & July 21, 2011 | |
|---|---|---|---|---|---|
| | **Total** | Under | Over | Under | Over |
| Roof | **48** | 9 | 3 | 31 | 5 |
| Windows | **24** | 3 | 6 | 12 | 3 |
| Boiler | **17** | 2 | 5 | 5 | 5 |
| **Total** | **89** | **14** | **14** | **48** | **13** |

**Districts remaining in Schematic Design:**

The following 9 districts, representing 17 projects, are currently in the schematic design phase and soon will be submitting the conclusion of their studies:

| District | School | Scope | Invite Date |
|---|---|---|---|
| Agawam | Agawam Junior High | Roof, Windows | November 17, 2010 |
| Hadley | Hopkins Academy | Roof | November 17, 2010 |
| Lowell | Lowell High School | Roof | February 9, 2011 |
| Lowell | Moody Elementary School | Roof, Windows, Boiler | February 9, 2011 |
| Lowell | Peter W. Reilly Elementary School | Roof, Windows | February 9, 2011 |
| Lowell | Washington Elementary School | Roof, Windows, Boilers | February 9, 2011 |
| Marlborough | Francis J. Kane Elementary School | Windows | November 17, 2010 |
| Marlborough | Marlborough High School | Roof, Windows, Boiler | November 17, 2010 |
| Natick | Johnson Elementary School | Windows, Boiler | February 9, 2011 |
| North Andover | Atkinson Elementary School | Windows | February 9, 2011 |
| North Andover | North Andover Middle School | Roof | February 9, 2011 |
| North Andover | Annie L. Sargent Elementary School | Roof | February 9, 2011 |
| Pioneer Valley | Bernardston Elementary School | Boiler | February 9, 2011 |
| Pioneer Valley | Pioneer Valley Regional | Boiler | February 9, 2011 |
| Pioneer Valley | Northfield Elementary School | Roof, Windows | February 9, 2011 |
| West Boylston | Major Edwards Elementary School | Windows | November 17, 2010 |
| Westport | Westport Middle School | Windows | November 17, 2010 |

# Massachusetts School Building Authority

No. of Projects: 318

## Master District Status List

Yellow = Wait List Project

Geen = Green Repair

Red = Changes in last 60 days

| District Name | School Name | Status | Preferred Schematic | OPM | Designer | Cx Authority | Procurement Status | CM/GC |
|---|---|---|---|---|---|---|---|---|
| Abington PS | Frolio JHS | Local Clearance - 07/08 | | | | | Undetermined | |
| Abington PS | Woodsdale IS | Design Development | Repair | RF Walsh Collaborative Partners | Gale Associates, Inc. | Russo Barr Associates, Inc. | | |
| Acton PS | Douglas ES | Closeout/Audit | Repair | N/A | CBI Consulting Inc. | | Undetermined | Gibson Roofs |
| Adams-Cheshire PS | Adams MS | Design Development | Addition/Renovation | URS Corporation | Tessier Associates | Strategic Building Solutions | Undetermined | |
| Agawam PS | Agawam Junior HS | Feasibility Study | Repair | Municipal Building Consultants, Inc. | CSS Architects Incorporated | | | |
| Amherst-Pelham PS | Amherst Reg MS | Design Development | Repair | Strategic Building Solutions, LLC | Bradley Architects, Inc. | Russo Barr Associates, Inc. | | |
| Andover PS | Bancroft ES | Design Development | New Construction | Town of Andover | Symmes Maini & McKee Associates, Inc. | Sebesta Blomberg & Associates | | |
| Andover PS | Andover West MS | Design Development | Repair | Skanska USA Building Inc. | Russo Barr Associates, Inc. | Simpson Gumpertz & Heger | | |
| Arlington PS | Thompson ES | Preferred Schematic | | PMA Consultants | HMFH Architects, Inc. | | | |
| Arlington PS | M Norcross Stratton ES | Construction | Repair | PMA Consultants | Turowski2 Architecture, Inc. | | Undetermined | Unicon, Inc. and Federal Construction Corp. |
| Ashburnham-West PS | Briggs ES | Design Development | New Construction | STV, Inc. | Lamoureux Pagano & Associates, Inc. | Foreman Building Commissioning, LP | | |
| Assabet Valley PS | Assabet Valley Voc HS | Preferred Schematic | Repair | Strategic Building Solutions, LLC | Design Partnership of Cambridge, Inc. | | | |
| Athol-Royalston PS | Riverbend ES | Local Clearance - 09/10 | | | | | | |
| Attleboro PS | Hyman Fine ES | Construction | Repair | Skanska USA Building, Inc. | Russo Barr Associates, Inc. | Gale Associates, Inc. | | |
| Attleboro PS | Hill-Roberts ES | Construction | Repair | Skanska USA Building, Inc. | Russo Barr Associates, Inc. | Gale Associates, Inc. | | |
| Attleboro PS | Attleboro HS | Construction | Repair | Skanska USA Building, Inc. | Russo Barr Associates, Inc. | Gale Associates, Inc. | | |
| Attleboro PS | A. Irvin Studley ES | Construction | Repair | Skanska USA Building, Inc. | Russo Barr Associates, Inc. | Gale Associates, Inc. | | |
| Auburn PS | Auburn MS | OPM Selection | | | | | | |
| Avon PS | Ralph D Butler ES | Design Development | Repair | Skanska USA Building Inc. | Knight, Bagge & Anderson, Inc. | Cannon Design | | |
| Ayer PS | Ayer HS | Local Clearance - 09/10 | | | | | | |
| Barnstable PS | West Barnstable ES | Construction | Repair | PMA Construction Services | Gale Associates, Inc. | CBI Consulting Inc. | | |
| Bellingham PS | Bellingham Memorial MS | Construction | Repair | Daedalus Projects Inc | Richard D. Kimball Company, Inc. | WSP Flack + Kurtz | Undetermined | General Air Conditioning & Heating, Inc. |
| Belmont PS | Roger E Wellington ES | Construction | New Construction | PMA Consultants | Jonathan Levi Architects LLC | Strategic Building Solutions | CMR - CM Selected | Skanska USA Building, Inc. |



DBB = Design-Bid-Build
CMR = Construction Manager at Risk

| Yellow = Wait List Project | |
|---|---|
| Geen = Green Repair | Red = Changes in last 60 days |

# Master District Status List

| District Name | School Name | Status | Preferred Schematic | OPM | Designer | Cx Authority | Procurement Status | CM/GC |
|---|---|---|---|---|---|---|---|---|
| Berkshire Hills PS | Monument Mt Reg HS | OPM Selection | | | | | | |
| Berlin-Boylston PS | Tahanto Reg HS | Construction | New Construction | PMA Consultants | HMFH Architects, Inc. | Strategic Building Solutions | | |
| Beverly PS | Beverly HS | Construction | Addition/Renovation | Heery International | Mount Vernon Group Architects, Inc. | | DBB - Contract Awarded | CTA Construction Co. |
| Billerica PS | Parker ES | Construction | New Construction | Joslin, Lesser & Associates, Inc. | Symmes Maini & McKee Associates, Inc. | Sebesta Blomberg & Associates | DBB - Contract Awarded | CTA Construction Co |
| Billerica PS | Billerica Memorial HS | Approved Project Vote Pending | Repair | Municipal Building Consultants, Inc. | Knight, Bagge & Anderson, Inc. | VP Consultants, LLC | | |
| Blackstone Valley Reg PS | Blackstone Valley HS | Design Development | Repair | Strategic Building Solutions, LLC | Reinhardt Associates, Inc. | Cannon Design | | |
| Boston PS | Excel HS | Approved Project Vote Pending | Repair | Daedalus Projects Inc | Gale Associates, Inc. | Simpson Gumpertz & Heger | | |
| Boston PS | Joseph Lee ES* | Approved Project Vote Pending | Repair | Daedalus Projects Inc | BLW Engineers, Inc./Gale Associates, Inc. | Simpson Gumpertz & Heger | | |
| Boston PS | Thomas A Edison JHS | Approved Project Vote Pending | Repair | Daedalus Projects Inc | BLW Engineers, Inc. | Simpson Gumpertz & Heger | | |
| Boston PS | Washington Irving MS | Approved Project Vote Pending | Repair | Daedalus Projects Inc | Gale Associates, Inc. | Simpson Gumpertz & Heger | | |
| Boston PS | Clarence R Edwards MS | Approved Project Vote Pending | Repair | Daedalus Projects Inc | BLW Engineers, Inc. | RFS Engineering | | |
| Boston PS | Quincy Upper School | Designer Selection | | City of Boston | | | | |
| Boston PS | Dearborn MS | Local Clearance - 09/10 | | | | | | |
| Boxford PS | Harry Lee Cole Primary | Closeout/Audit | Repair | | Russo Barr Associates, Inc. | | Undetermined | MDM Engineering, Inc |
| Braintree PS | South MS | Closeout/Audit | Repair | Town Employee | Habeeb & Associates Architects, Inc. | | DBB - Contract Awarded | Construction Dynamics |
| Braintree PS | Hollis ES | Construction | Repair | RF Walsh Collaborative Partners | Habeeb & Associates Architects, Inc. | Cannon Design | | |
| Braintree PS | Highlands | Construction | Repair | RF Walsh Collaborative Partners | Habeeb & Associates Architects, Inc. | Cannon Design | | |
| Braintree PS | East MS | Construction | Repair | RF Walsh Collaborative Partners | Habeeb & Associates Architects, Inc. | Cannon Design | | |
| Braintree PS | Archie T Morrison ES | Construction | Repair | RF Walsh Collaborative Partners | Habeeb & Associates Architects, Inc. | Cannon Design | | |
| Braintree PS | Braintree HS | Construction | Repair | RF Walsh Collaborative Partners | Habeeb & Associates Architects, Inc. | Cannon Design | | |
| Brockton PS | North Junior HS | Design Development | Repair | Skanska USA Building Inc. | CSS Architects Incorporated | RFS Engineering | | |
| Brockton PS | Brockton HS | Design Development | Repair | Skanska USA Building Inc. | CSS Architects Incorporated | Simpson Gumpertz & Heger | | |
| Brockton PS | Downey ES | Design Development | Repair | Skanska USA Building Inc. | CSS Architects Incorporated | Simpson Gumpertz & Heger | | |
| Brockton PS | East Junior HS | Design Development | Repair | Skanska USA Building Inc. | CSS Architects Incorporated | RFS Engineering | | |
| Brockton PS | Edgar B Davis ES | Design Development | Repair | Skanska USA Building Inc. | CSS Architects Incorporated | Simpson Gumpertz & Heger | | |
| Brockton PS | Hancock ES | Design Development | Repair | Skanska USA Building Inc. | CSS Architects Incorporated | Simpson Gumpertz & Heger | | |

Yellow = Wait List Project

Geen = Green Repair

Red = Changes in last 60 days

# Master District Status List

| District Name | School Name | Status | Preferred Schematic | OPM | Designer | Cx Authority | Procurement Status | CM/GC |
|---|---|---|---|---|---|---|---|---|
| Brockton PS | Oscar F Raymond ES | Design Development | Repair | Skanska USA Building Inc. | CSS Architects Incorporated | Simpson Gumpertz & Heger | | |
| Brockton PS | West Junior HS | Design Development | Repair | Skanska USA Building Inc. | CSS Architects Incorporated | Simpson Gumpertz & Heger | | |
| Brookfield PS | Brookfield ES | Design Development | Repair | Diversified Project Management | Habeeb & Associates Architects, Inc. | | | |
| Brookline PS | Heath K-8 | Design Development | Addition/Renovation | Town of Brookline Building Department | Miller Dyer Spears Inc. | Consulting Engineering Services, LLC | | |
| Brookline PS | John D Runkle K-8 | Construction | Addition/Renovation | Town of Brookline Building Department | Design Partnership of Cambridge, Inc. | Consulting Engineering Services, LLC | DBB - In Design | |
| Burlington PS | Memorial ES | Construction | New Construction | Construction Monitoring Services, Inc. | Knight, Bagge & Anderson, Inc. | Consulting Engineering Services, LLC | DBB - Contract Awarded | CTA Construction Co. |
| Burlington PS | Marshall Simonds MS | Construction | Addition/Renovation | Construction Monitoring Services, Inc. | Knight, Bagge & Anderson, Inc. | RDK Engineering | CMR - CM Selected | CTA Construction Co. |
| Cambridge PS | Cambridge Rindge and Latin HS | Closeout/Audit | | | HMFH Architects, Inc. | | DBB - Contract Awarded | W.T. Rich, Inc. |
| Canton PS | Rodman Pre-K Center | Construction | Repair | Maguire Group | Russo Barr Associates, Inc. | Cannon Design | | |
| Canton PS | Canton HS | Construction | Repair | Maguire Group | Russo Barr Associates, Inc. | Cannon Design | | |
| Cape Cod Region Voc Tech PS | Cape Cod Regional Voc / Tech HS | Feasibility Study | Repair | URS Corporation | | | | |
| Carlisle PS | Carlisle K-8 | Construction | Addition/Renovation | Daedalus Projects, Inc. | HMFH Architects, Inc. | Horizon Engineering Associates, LLP | DBB - Contract Awarded | H.V. Collins Company |
| Central Berkshire PS | Craneville ES | Approved Project Vote Pending | Repair | Daedalus Projects Inc | Bradley Architects, Inc. | Strategic Building Solutions | | |
| Central Berkshire PS | Kittredge ES | Approved Project Vote Pending | Repair | Daedalus Projects Inc | Bradley Architects, Inc. | Strategic Building Solutions | | |
| Chatham PS | Chatham HS | Local Clearance - 09/10 | | | | | | |
| Chelmsford PS | Chelmsford HS | Design Development | Repair | Vertex Construction Services, Inc. | Russo Barr Associates, Inc. | Simpson Gumpertz & Heger | | |
| Chelmsford PS | Byam ES | Design Development | Repair | Vertex Construction Services, Inc. | Russo Barr Associates, Inc. | Simpson Gumpertz & Heger | | |
| Chelsea PS | Clark Avenue MS | Local Clearance - 07/08 | | | Jacobs | | | |
| Chicopee PS | Chicopee Academy | Designer Selection | | | | | | |
| Concord-Carlisle PS | Concord Carlisle HS | Feasibility Study | | KV Associates, Inc. | OMR Architects, Inc. | | | |
| Conway PS | Conway Grammar ES | Closeout/Audit | Repair | | Richardson Gorman Architects | | Undetermined | RAC Builders, Inc. |
| Danvers PS | Danvers HS | Construction | Addition/Renovation | Construction Monitoring Services, Inc. | DiNisco Design Partnership, Limited | Turner Facilities Management Solutions | DBB - In Design | Bacon Construction Co., Inc. |
| Dartmouth PS | James M. Quinn ES | Construction | Repair | Vertex Construction Services, Inc. | Russo Barr Associates, Inc. | Gale Associates, Inc. | | |
| Dartmouth PS | James M. Quinn ES | Closeout/Audit | Repair | | | | | |
| Dedham PS | Avery ES | Construction | New Construction | Construction Monitoring Services, Inc. | Dore & Whittier Architects, Inc. | WSP Flack + Kurtz | CMR - CM Selected | Consigli Construction Co |
| Dennis-Yarmouth PS | Ezra H Baker ES | Design Development | Repair | STV Construction, Inc. | Knight, Bagge & Anderson, Inc. | CBI Consulting Inc. | | |

| Yellow = Wait List Project | |
|---|---|
| Geen = Green Repair | Red = Changes in last 60 days |

# Master District Status List

| District Name | School Name | Status | Preferred Schematic | OPM | Designer | Cx Authority | Procurement Status | CM/GC |
|---|---|---|---|---|---|---|---|---|
| Douglas PS | Douglas IS | Design Development | | Heery International, Inc | DiNisco Design Partnership, Limited | Consulting Engineering Services, LLC | | |
| Dracut PS | Dracut SHS | Design Development | Addition/Renovation | RF Walsh Collaborative Partners | Mount Vernon Group Architects, Inc. | RDK Engineering | Undetermined | |
| Dudley-Charlton Reg PS | Shepherd Hill Reg HS | Design Development | Repair | Pinck & Co., Inc. | ICON architecture, inc. | Cannon Design | | |
| Duxbury PS | Duxbury HS | Preferred Schematic | | KV Associates, Inc. | | | | |
| East Bridgewater PS | East Bridgewater HS | Design Development | Model School | RF Walsh Collaborative Partners | Ai3 Architects LLC | Foreman Building Commissioning, LP | | |
| Easthampton PS | Easthampton HS | Construction | New Construction | Strategic Building Solutions, LLC | Caolo & Bieniek Associates, Inc. | Consulting Engineering Services, LLC | Undetermined | |
| Essex North Shore Agr and Tech PS | Essex North Shore Agr and Tech School | Design Development | New Construction | PMA Consultants | Design Partnership of Cambridge, Inc. | Turner Facilities Management Solutions | CMR - Procurement Pending | |
| Fairhaven PS | Rogers ES | Feasibility Study | | Daedalus Projects Inc | HMFH Architects, Inc. | | | |
| Fairhaven PS | Hastings MS | Design Development | Repair | Daedalus Projects Inc | Durland Van Voorhis Architects, Inc. | Gale Associates, Inc. | | |
| Fall River PS | Morton MS | Design Development | | Maguire Group Inc. | Mount Vernon Group Architects, Inc. | Sebesta Blomberg & Associates | | |
| Falmouth PS | North Falmouth ES | Construction | Repair | | Keenan + Kenny Architects, LTD | Gale Associates, Inc. | | |
| Falmouth PS | Falmouth High School | Building Completion 2011 | Addition/Renovation | Gilbane Building Company | DiNisco Design Partnership, Limited | | DBB - Contract Awarded | TLT Construction |
| Falmouth PS | East Falmouth ES | Construction | Repair | | Keenan + Kenny Architects, LTD | Gale Associates, Inc. | | |
| Fitchburg PS | South Street ES | Construction | Repair | Compass Project Management, Inc. | BLW Engineers, Inc. | RDK Engineering | | |
| Fitchburg PS | Reingold ES | Construction | Repair | Compass Project Management, Inc. | Knight, Bagge & Anderson, Inc. | RDK Engineering | | |
| Fitchburg PS | Memorial IS | Construction | Repair | Compass Project Management, Inc. | BLW Engineers, Inc. | RDK Engineering | | |
| Fitchburg PS | Goodrich K Center | Construction | Repair | Compass Project Management, Inc. | BLW Engineers, Inc. | RDK Engineering | | |
| Fitchburg PS | Crocker ES | Local Clearance - 07/08 | | | | | | |
| Fitchburg PS | Fitchburg HS | Construction | Repair | Compass Project Management, Inc. | BLW Engineers, Inc. | RDK Engineering | | |
| Fitchburg PS | Reingold ES | Construction | Repair | Compass Project Management, Inc. | BLW Engineers, Inc. | Simpson Gumpertz & Heger | | |
| Fitchburg PS | South Street ES | Construction | | Compass Project Management, Inc. | Knight, Bagge & Anderson, Inc. | Simpson Gumpertz & Heger | | |
| Fitchburg PS | Memorial IS | Construction | Repair | Compass Project Management, Inc. | Knight, Bagge & Anderson, Inc. | Simpson Gumpertz & Heger | | |
| Florida PS | Abbott Memorial K-8 | Building Completion 2011 | Repair | | Dietz and Company | | DBB - Contract Awarded | Waterman Excavating, Inc |
| Foxborough PS | Foxborough HS | Construction | Repair | Construction Monitoring Services, Inc. | Kaestle Boos Associates, Inc. | Consulting Engineering Services, LLC | DBB - Contract Awarded | CTA Construction Co. |
| Framingham PS | Mary E Stapleton ES | Construction | Repair | Bargmann, Hendrie + Archetype, Inc. | Russo Barr Associates, Inc. | CBI Consulting Inc. | | |
| Franklin PS | Franklin HS | Feasibility Study | Renovation | Daedalus Projects Inc. | Kaestle Boos Associates, Inc. | | | |

| Yellow = Wait List Project | |
|---|---|
| Geen = Green Repair | Red = Changes in last 60 days |

# Master District Status List

| District Name | School Name | Status | Preferred Schematic | OPM | Designer | Cx Authority | Procurement Status | CM/GC |
|---|---|---|---|---|---|---|---|---|
| Gardner PS | Waterford Street Primary | Construction | Repair | P3 Project Planning Professionals | Knight, Bagge & Anderson, Inc. | VP Consultants, LLC | | |
| Gardner PS | Elm Street IS | Construction | Repair | P3 Project Planning Professionals | Knight, Bagge & Anderson, Inc. | VP Consultants, LLC | | |
| Gardner PS | Gardner HS | Construction | Repair | P3 Project Planning Professionals | Knight, Bagge & Anderson, Inc. | VP Consultants, LLC | | |
| Georgetown PS | Penn Brook IS | Feasibility Study | | Municpal Building Consultants, Inc. | Drummey Rosane Anderson, Inc. | | | |
| Gloucester PS | West Parish ES | Local Clearance - 09/10 | | | | | | |
| Gloucester PS | Veterans Memorial ES | Design Development | Repair | Knight, Bagge, & Anderson, Inc. | CGKV Architects, Inc. | Russo Barr Associates, Inc. | | |
| Gloucester PS | Beeman Memorial IS | Design Development | Repair | Knight, Bagge, & Anderson, Inc. | CGKV Architects, Inc. | Russo Barr Associates, Inc. | | |
| Gloucester PS | East Gloucester ES | Design Development | Repair | Knight, Bagge, & Anderson, Inc. | CGKV Architects, Inc. | Russo Barr Associates, Inc. | | |
| Gloucester PS | Plum Cove School | Design Development | Repair | Knight, Bagge, & Anderson, Inc. | CGKV Architects, Inc. | Russo Barr Associates, Inc. | | |
| Gloucester PS | Ralph B O'Maley MS | Design Development | Repair | Knight, Bagge, & Anderson, Inc. | CGKV Architects, Inc. | Russo Barr Associates, Inc. | | |
| Grafton PS | Grafton Memorial SHS | Construction | New Construction | Joslin, Lesser & Associates, Inc. | Symmes Maini & McKee Associates, Inc. | Horizon Engineering Associates, LLP | CMR - CM Selected | Dimeo Construction |
| Grafton PS | South Grafton ES | Design Development | Repair | URS Corporation | CGKV Architects, Inc. | Horizon Engineering Associates, LLP | | |
| Grafton PS | Grafton Memorial SHS | Project Scope & Budget | Repair | URS Corporation | CGKV Architects, Inc. | | | |
| Greater Lowell Voc Tec PS | Gr Lowell Regional Voc / Tech HS | OPM Selection | Repair | | | | | |
| Greater New Bedford PS | Gr New Bedford Voc / Tech HS | Designer Selection | | | | | | |
| Greenfield PS | Greenfield HS | Feasibility Study | | Construction Monitoring Services, Inc. | Dore & Whittier Architects, Inc. | | | |
| Greenfield PS | Four Corners ES | Design Development | Repair | P3 Project Planning Professionals | Tighe & Bond, Inc. | Strategic Building Solutions | | |
| Hadley PS | Hopkins Academy | Feasibility Study | Repair | Strategic Building Solutions, LLC | | | | |
| Hamilton-Wenham PS | Cutler ES | Closeout/Audit | Repair | Municipal Building Consultants, Inc. | Richard D. Kimball Company, Inc. | Sebesta Blomberg & Associates | DBB - Contract Awarded | Thomas E. Snowden Inc. |
| Hampden-Wilbraham PS | Minnechaug Reg HS | Construction | Model School | ARCADIS U.S., Inc. | Mount Vernon Group Architects, Inc. | Horizon Engineering Associates, LLP | DBB - Contract Awarded | Fontaine Bros. |
| Hancock PS | Hancock ES | Construction | Repair | N/A | Westall Architects | | | |
| Hanover PS | Hanover HS | Construction | New Construction | PMA Consultants | HMFH Architects, Inc. | Horizon Engineering Associates, LLP | DBB - Contract Awarded | Callahan, Inc |
| Haverhill PS | John G Whittier MS | Feasibility Study | Repair | | | | | |
| Haverhill PS | Tilton Primary | Feasibility Study | Repair | | | | | |
| Haverhill PS | Haverhill HS | Construction | | | | | DBB - Contract Awarded | |
| Haverhill PS | Greenleaf Primary | Feasibility Study | Repair | | | | | |

| Yellow = Wait List Project | |
|---|---|
| Geen = Green Repair | Red = Changes in last 60 days |

# Master District Status List

| District Name | School Name | Status | Preferred Schematic | OPM | Designer | Cx Authority | Procurement Status | CM/GC |
|---|---|---|---|---|---|---|---|---|
| Haverhill PS | Consentino MS | Feasibility Study | Repair | | | | | |
| Haverhill PS | Caleb Dustin Hunking MS | Feasibility Study | Repair | | | | | |
| Haverhill PS | Walnut Square Primary | Feasibility Study | Repair | | | | | |
| Hingham PS | Hingham MS | Feasibility Study | Model School | Knight, Bagge & Anderson, Inc. | Ai3 Architects LLC | | | |
| Holbrook PS | Holbrook JHS / SHS | OPM Selection | | | | | | |
| Holyoke PS | Holyoke HS | Construction | | | Design Partnership of Cambridge, Inc. | | DBB - Contract Awarded | |
| Hopkinton PS | Center ES | Approved Project Vote Pending | New Construction | Town of Hopkinton | Design Partnership of Cambridge, Inc. | | Undetermined | |
| Hudson PS | John F Kennedy MS | Design Development | New Construction | PMA Consultants | OMR Architects, Inc. | WSP Flack + Kurtz | | |
| Leicester PS | Leicester Memorial ES | Design Development | Repair | Maguire Group | Bradley Architects, Inc. | | | |
| Leicester PS | Leicester MS | Design Development | Repair | Maguire Group | Bradley Architects, Inc. | Cannon Design | | |
| Leominster PS | Leominster SHS | Design Development | Addition/Renovation | Daedalus Projects, Inc. | Lamoureux Pagano & Associates, Inc. | Horizon Engineering Associates, LLP | DBB - In Design | |
| Leverett PS | Leverett ES | Design Development | Repair | Potomac Capital Advisors | DiMarinisi & Wolfe Architects Urban | Russo Barr Associates, Inc. | | |
| Lexington PS | Lexington HS | Construction | Repair | Skanska USA Building Inc. | Russo Barr Associates, Inc. | Simpson Gumpertz & Heger | | |
| Lexington PS | Joseph Estabrook ES | OPM Selection | | | | | | |
| Lincoln PS | Lincoln K-8 | Feasibility Study | | Skanska USA Building, Inc. | OMR Architects, Inc. | | | |
| Littleton PS | Russell St ES | Closeout/Audit | Repair | Daedalus Projects, Inc. | Drummey Rosane Anderson, Inc. | WSP Flack + Kurtz | DBB - Contract Awarded | Colantonio, Inc. |
| Longmeadow PS | Longmeadow HS | Construction | New Construction | Joslin, Lesser & Associates, Inc. | OMR Architects, Inc. | Foreman Building Commissioning, LP | CMR - CM Selected | Gilbane Building Company |
| Lowell PS | Lowell HS | Feasibility Study | Repair | Knight, Bagge, & Anderson, Inc. | ICON architecture, inc. | | | |
| Lowell PS | Washington ES | Feasibility Study | Repair | Knight, Bagge, & Anderson, Inc. | ICON architecture, inc. | | | |
| Lowell PS | Charles W Morey ES | Closeout/Audit | | Watermark | | | DBB - Contract Awarded | CTA Construction Co. |
| Lowell PS | Peter W Reilly ES | Feasibility Study | Repair | Knight, Bagge, & Anderson, Inc. | ICON architecture, inc. | | | |
| Lowell PS | Moody ES | Feasibility Study | Repair | Knight, Bagge, & Anderson, Inc. | ICON architecture, inc. | | | |
| Lunenburg PS | Lunenburg HS | Local Clearance - 09/10 | | | | | | |
| Lynn PS | Thurgood Marshall MS | Local Clearance - 09/10 | | | | | | |
| Lynnfield PS | Lynnfield HS | Designer Selection | | | | | | |
| Malden PS | Malden HS | Construction | Renovation | URS Corporation | Flansburgh Associates, Inc. | | CMR - CM Selected | Gilbane Building Company |

| Yellow = Wait List Project | |
|---|---|
| Geen = Green Repair | Red = Changes in last 60 days |

# Master District Status List

| District Name | School Name | Status | Preferred Schematic | OPM | Designer | Cx Authority | Procurement Status | CM/GC |
|---|---|---|---|---|---|---|---|---|
| Manchester Essex Regional PS | Manchester JHS / SHS | Closeout/Audit | | Design Technique | Mount Vernon Group Architects, Inc. | | DBB - Contract Awarded | TLT Construction |
| Marblehead PS | Glover Primary | Design Development | New Construction | Municipal Building Consultants, Inc. | JCJ Architecture, PC | | Undetermined | |
| Marblehead PS | Village IS | Building Completion 2011 | Repair | Municipal Building Consultants, Inc. | Symmes Maini & McKee Associates, Inc. | RDK Engineering | DBB - Contract Awarded | Groom Construction |
| Marlborough PS | Francis J Kane Primary | Feasibility Study | Repair | RF Walsh Collaborative Partners | Baker/Wohl Architects, Inc. | | | |
| Marlborough PS | Marlborough HS | Feasibility Study | Repair | RF Walsh Collaborative Partners | Baker/Wohl Architects, Inc. | | | |
| Marshfield PS | Marshfield HS | Feasibility Study | | | | | | |
| Marshfield PS | Gov Edward Winslow ES | Construction | Repair | Vertex Construction Services, Inc. | Knight, Bagge & Anderson, Inc. | RDK Engineering | DBB - In Design | |
| Maynard PS | Maynard HS | Design Development | New Construction | Municipal Building Consultants, Inc. | Tappe Associates, Inc. | WSP Flack + Kurtz | Undetermined | |
| Medway PS | Medway MS | Design Development | | Compass Project Management, Inc. | Knight, Bagge & Anderson, Inc. | Sebesta Blomberg & Associates | CMR - IG Application Pending | |
| Melrose PS | Melrose HS | Design Development | Repair | Municipal Building Consultants, Inc. | Gale Associates, Inc. | Russo Barr Associates, Inc. | | |
| Mendon-Upton PS | Miscoe Hill IS | Design Development | Repair | Maguire Group | | | | |
| Methuen PS | Methuen HS | Design Development | Addition/Renovation | KBA/Trident | Finegold Alexander and Associates Inc. | Environmental Health and Engineering | CMR - CM Selected | Dimeo Construction |
| Middleborough PS | Mary K. Goode ES | Project Scope & Budget | Repair | Maguire Group | Habeeb & Associates Architects, Inc. | | | |
| Middleton PS | Howe-Manning IS | Construction | New Construction | RF Walsh Collaborative Partners | DiNisco Design Partnership, Limited | Foreman Building Commissioning, LP | DBB - Contract Awarded | CTA Construction Co. |
| Minuteman Voc Tech PS | Minuteman Reg HS | Local Clearance - 09/10 | | | | | | |
| Mohawk Trail PS | Mohawk Trail Reg HS | Project Scope & Budget | Repair | Potomac Capital Advisors | Bradley Architects, Inc. | | | |
| Mohawk Trail PS | Colrain Central ES | Project Scope & Budget | Repair | Potomac Capital Advisors | Bradley Architects, Inc. | | | |
| Mohawk Trail PS | Buckland-Shelburne Reg ES | Project Scope & Budget | Repair | Potomac Capital Advisors | Bradley Architects, Inc. | | | |
| Mount Greylock PS | Mt Greylock Reg HS | Closeout/Audit | Repair | N/A | Hesnor Engineering & Barry Architects | Horizon Engineering Associates, LLP | DBB - Contract Awarded | Adams Plumbing & Heating |
| Narragansett PS | Phillipston Memorial ES | Design Development | Repair | Potomac Capital Advisors | DiMarinisi & Wolfe Architects Urban | RFS Engineering | | |
| Narragansett PS | Templeton Center | Feasibility Study | | Strategic Building Solutions, LLC | Symmes Maini & McKee Associates, Inc. | | Undetermined | |
| Narragansett PS | Narragansett MS | Design Development | Repair | Potomac Capital Advisors | DiMarinisi & Wolfe Architects Urban | RFS Engineering | | |
| Nashoba PS | Pompositticut Primary | Construction | Addition/Renovation | Construction Monitoring Services, Inc. | Symmes Maini & McKee Associates, Inc. | Strategic Building Solutions | DBB - Contract Awarded | Stella P.J. Construction Corp. |
| Nashoba Valley Tech PS | Nashoba Valley Tech HS | Design Development | Repair | | | | | |
| Natick PS | Johnson ES | Feasibility Study | Repair | Municipal Building Consultants, Inc. | Knight, Bagge & Anderson, Inc. | | | |
| Natick PS | Natick HS | Construction | Model School | RF Walsh Collaborative Partners | Ai3 Architects LLC | RFS Engineering | DBB - Contract Awarded | Brait Builders Corporation |

| Yellow = Wait List Project | |
|---|---|
| Geen = Green Repair | Red = Changes in last 60 days |

# Master District Status List

| District Name | School Name | Status | Preferred Schematic | OPM | Designer | Cx Authority | Procurement Status | CM/GC |
|---|---|---|---|---|---|---|---|---|
| Nauset PS | Nauset Reg HS | Project Scope & Budget | Repair | NETCO Construction Project Managers, Inc. | Habeeb & Associates Architects, Inc. | | | |
| Needham PS | Newman ES | Construction | Repair | Town of Needham | Drummey Rosane Anderson, Inc. | RFS Engineering | CMR - CM Selected | Consigli Construction Co. |
| Needham PS | Pollard MS | Construction | Repair | STV Construction, Inc. | Gale Associates, Inc. Gale Associates, Inc. | CBI Consulting Inc. | | |
| New Bedford PS | John Hannigan ES | OPM Selection | | | | | | |
| New Bedford PS | Abraham Lincoln | Building Completion 2011 | New Construction | Daedalus Projects Inc | Mount Vernon Group Architects, Inc. | Sebesta Blomberg & Associates | DBB - Contract Awarded | CTA Construction Co. |
| New Bedford PS | New Bedford HS | OPM Selection | | | | | | |
| New Salem-Wendell PS | Swift River ES | Design Development | Repair | Maguire Group | Bradley Architects, Inc. | | | |
| Newburyport PS | Francis T Bresnahan ES | Local Clearance - 09/10 | | | | | | |
| Newburyport PS | Rupert A Nock MS | Local Clearance - 09/10 | | | | | | |
| Newton PS | Bowen ES | Design Development | Repair | STV Construction, Inc. | Habeeb & Associates Architects, Inc. | | | |
| Newton PS | Williams ES | Design Development | Repair | STV Construction, Inc. | Habeeb & Associates Architects, Inc. | | | |
| Newton PS | Newton North HS | Building Completion 2011 | New Construction | Turner Construction Company | Dore & Whittier Architects, Inc. | | CMR - CM Selected | Dimeo Construction |
| Norfolk County Agr PS | Norfolk County Agr HS | Design Development | Addition/Renovation | Compass Project Management, Inc | Turowski2 Architecture, Inc. | RFS Engineering | | |
| Norfolk PS | Freeman-Centennial IS | Construction | New Construction | Joslin, Lesser & Associates, Inc. | Flansburgh Associates, Inc. | WSP Flack + Kurtz | DBB - In Design | Fontaine Bros., Inc. |
| North Adams PS | Silvio O Conte MS | Feasibility Study | | Strategic Building Solutions, LLC | Margo Jones Architects, Inc. | | | |
| North Andover PS | North Andover MS | Feasibility Study | Repair | Municipal Building Consultants, Inc. | ICON architecture, inc. | | | |
| North Andover PS | Annie L Sargent ES | Feasibility Study | Repair | Municipal Building Consultants, Inc. | ICON architecture, inc. | | | |
| North Andover PS | Atkinson ES | Feasibility Study | Repair | Municipal Building Consultants, Inc. | ICON architecture, inc. | | | |
| North Attleborough PS | Falls ES | Approved Project Vote Pending | Repair | Atlantic Construction & Management, Inc. | CSS Architects Incorporated | Gale Associates, Inc. | | |
| North Attleborough PS | Joseph W Martin Jr ES | Closeout/Audit | Repair | | CBI Consulting Inc. | Gale Associates, Inc. | DBB - Contract Awarded | Eagle Rivet Roof Services Corporation |
| North Brookfield PS | North Brookfield ES | Design Development | Repair | Vertex Construction Services, Inc. | LPBA/ Architects, Inc. | Simpson Gumpertz & Heger | | |
| North Middlesex PS | Ashby ES | Feasibility Study | Repair | Vertex Construction Services, Inc. | | | | |
| North Middlesex PS | Spaulding Memorial Primary | Feasibility Study | Repair | Vertex Construction Services, Inc. | | | | |
| North Reading PS | North Reading HS | Feasibility Study | | PMA Consultants | Dore & Whittier Architects, Inc. | | | |
| Northampton-Smith PS | Smith Vocational and Agricultural HS | Local Clearance - 09/10 | | | | | | |
| Northborough PS | Robert E. Melican MS | Project Scope & Budget | Repair | Pinck & Co., Inc. | ICON architecture, inc. | | | |

| Yellow = Wait List Project | |
|---|---|
| Geen = Green Repair | Red = Changes in last 60 days |

# Master District Status List

| District Name | School Name | Status | Preferred Schematic | OPM | Designer | Cx Authority | Procurement Status | CM/GC |
|---|---|---|---|---|---|---|---|---|
| Northeast Metro Voc PS | Northeast Metro Reg Voc HS | Local Clearance - 09/10 | | | | | | |
| Norton PS | Norton HS | Design Development | | Pinck & Co., Inc. | JCJ Architecture, PC | RFS Engineering | CMR - IG Application Pending | |
| Norwood PS | Norwood HS | Construction | Model School | Compass Project Management, Inc. | Ai3 Architects LLC | | DBB - Contract Awarded | Agostini Construction Company, Inc. |
| Old Colony Reg Voc Tech PS | Old Colony Regional Voc / Tech HS | OPM Selection | | | | | | |
| Orange PS | Butterfield MS | Closeout/Audit | Repair | | Tighe & Bond, Inc. | | Undetermined | SOM Construction, Inc. |
| Orange PS | Dexter Park IS | Local Clearance - 09/10 | | | | | | |
| Oxford PS | Oxford MS | Green Repair Program | Repair | | | | | |
| Palmer PS | Converse MS | Design Development | Repair | Diversified Project Management | Tighe & Bond, Inc. | Strategic Building Solutions | | |
| Palmer PS | Old Mill Pond ES | Design Development | Repair | Diversified Project Management | Tighe & Bond, Inc. | Strategic Building Solutions | | |
| Palmer PS | Palmer HS | Design Development | Repair | Diversified Project Management | Tighe & Bond, Inc. | Strategic Building Solutions | | |
| Peabody PS | John E Burke ES | Project Scope & Budget | Repair | Daedalus Projects Inc | LPBA/ Architects, Inc. | | | |
| Peabody PS | William A Welch Sr ES | Project Scope & Budget | Repair | Daedalus Projects Inc | LPBA/ Architects, Inc. | | | |
| Peabody PS | J Henry Higgins MS | Feasibility Study | Repair | Daedalus Projects Inc | DiNisco Design Partnership, Limited | | | |
| Pentucket PS | Dr John C Page ES | Design Development | Repair | PMA Consultants | Knight, Bagge & Anderson, Inc. | RDK Engineering | | |
| Pentucket PS | Elmer S Bagnall ES | Design Development | Repair | PMA Consultants | Knight, Bagge & Anderson, Inc. | CBI Consulting Inc. | | |
| Pentucket PS | Helen R Donaghue IS | Design Development | Repair | PMA Consultants | Knight, Bagge & Anderson, Inc. | CBI Consulting Inc. | | |
| Pentucket PS | Dr Frederick N Sweetsir Primary | Design Development | Repair | PMA Consultants | Knight, Bagge & Anderson, Inc. | CBI Consulting Inc. | | |
| Pioneer Valley PS | Bernardston ES | Feasibility Study | Repair | Diversified Project Management | CGKV Architects, Inc. | | | |
| Pioneer Valley PS | Northfield ES | Feasibility Study | Repair | Diversified Project Management | CGKV Architects, Inc. | | | |
| Pioneer Valley PS | Pioneer Valley Reg MS / HS | Feasibility Study | Repair | Diversified Project Management | CGKV Architects, Inc. | | | |
| Pittsfield PS | Taconic HS | Feasibility Study | | Skanska USA Building, Inc. | | | | |
| Plymouth PS | West ES | Closeout/Audit | Repair | | | | | |
| Plymouth PS | Plymouth North HS | Construction | Model School | Ted Gentry Associates | Ai3 Architects LLC | Sebesta Blomberg & Associates | DBB - Contract Awarded | J&J Contractors Inc. |
| Plymouth PS | Plymouth Community IS | Design Development | Repair | | Knight, Bagge & Anderson, Inc. | VP Consultants, LLC | | |
| Quabbin PS | Oakham Center ES | Closeout/Audit | Repair | | Russo Barr Associates, Inc. | VP Consultants, LLC | DBB - Contract Awarded | Cape Way Roofing |
| Quabbin PS | Quabbin Reg HS | Construction | Repair | Vertex Construction Services, Inc. | LPBA/ Architects, Inc. | VP Consultants, LLC | | |

| Yellow = Wait List Project | |
|---|---|
| Geen = Green Repair | Red = Changes in last 60 days |

# Master District Status List

| District Name | School Name | Status | Preferred Schematic | OPM | Designer | Cx Authority | Procurement Status | CM/GC |
|---|---|---|---|---|---|---|---|---|
| Quincy PS | Central MS | Design Development | New Construction | Tishman Construction Corporation of MA | Ai3 Architects LLC | Sebesta Blomberg & Associates | DBB - In Design | |
| Reading PS | J Warren Killam ES | Construction | Repair | Knight, Bagge, & Anderson, Inc. | LPBA/ Architects, Inc. | Russo Barr Associates, Inc. | | |
| Reading PS | Birch Meadow ES | Construction | Repair | Knight, Bagge, & Anderson, Inc. | LPBA/ Architects, Inc. | Russo Barr Associates, Inc. | | |
| Revere PS | Paul Revere ES | Building Completion 2011 | New Construction | RF Walsh Collaborative Partners | Drummey Rosane Anderson, Inc. | | DBB - Contract Awarded | Delulis Brothers Construction Company |
| Revere PS | William McKinley ES | Local Clearance - 09/10 | | | | | | |
| Rochester PS | Rochester Memorial ES | Construction | Addition/Renovation | PMA Consultants | Flansburgh Associates, Inc. | Horizon Engineering Associates, LLP | CMR - CM Selected | Gilbane Building Company |
| Rockland PS | John W Rogers MS | Construction | Addition/Renovation | Daedalus Projects Inc | Dore & Whittier Architects, Inc. | Consulting Engineering Services, LLC | CMR - CM Selected | Agostini Construction Company, Inc. |
| Rockland PS | R Stewart Esten ES | Approved Project Vote Pending | Repair | Daedalus Projects Inc | Habeeb & Associates Architects, Inc. | Russo Barr Associates, Inc. | | |
| Rockport PS | Rockport ES | Closeout/Audit | Repair | N/A | Russo Barr Associates, Inc. | | | |
| Rockport PS | Rockport HS | Closeout/Audit | Repair | | Russo Barr Associates, Inc. | VP Consultants, LLC | DBB - Contract Awarded | Feeley, McAnespie, Inc. |
| Salem PS | Saltonstall ES | Feasibility Study | Repair | KV Associates, Inc. | Reinhardt Associates, Inc. | | | |
| Salem PS | Collins MS | Feasibility Study | Repair | KV Associates, Inc. | Reinhardt Associates, Inc. | | | |
| Sandwich PS | Forestdale K-8 | Design Development | Repair | NETCO Construction Project Managers, Inc. | Habeeb & Associates Architects, Inc. | Gale Associates, Inc. | | |
| Sandwich PS | Oak Ridge K-8 | Design Development | Repair | NETCO Construction Project Managers, Inc. | Habeeb & Associates Architects, Inc. | Gale Associates, Inc. | | |
| Saugus PS | Belmonte Saugus MS | Preferred Schematic | Repair | Skanska USA Building, Inc. | Fletcher Thompson Architecture Engineering, | | | |
| Scituate PS | Wampatuck ES | Construction | Repair | Bargmann, Hendrie + Archetype, Inc. | Knight, Bagge & Anderson, Inc. | RFS Engineering | | |
| Sharon PS | Sharon HS | Construction | Repair | Daedalus Projects Inc | Baker/Wohl Architects, Inc. | Cannon Design | Undetermined | Titan Roofing, Inc. |
| Sharon PS | Sharon MS | Construction | Addition/Renovation | Daedalus Projects, Inc. | Kaestle Boos Associates, Inc. | Horizon Engineering Associates, LLP | CMR - CM Selected | Consigli Construction Co. |
| Shawsheen Valley Voc PS | Shawsheen Valley Voc / Tech HS | Construction | | Construction Monitoring Services Inc. | Knight, Bagge & Anderson, Inc. | | | |
| Shrewsbury PS | Sherwood MS | Construction | New Construction | PMA Consultants | Lamoureux Pagano & Associates, Inc. | RDK Engineering | CMR - CM Selected | Gilbane Building Company |
| Shrewsbury PS | Spring Street ES | Construction | Repair | PMA Consultants | Habeeb & Associates Architects, Inc. | Cannon Design | | |
| Somerset PS | Somerset HS | Designer Selection | | Skanska USA Building, Inc. | | | | |
| Somerville PS | E Somerville Community K-8 | Design Development | Renovation | City of Somerville | Maguire Group Inc. | Foreman Building Commissioning, LP | | |
| South Hadley PS | Plains ES | OPM Selection | | | | | | |
| South Shore Reg Voc PS | South Shore Voc / Tech HS | Construction | Repair | Vertex Construction Services, Inc. | Gale Associates, Inc. | VP Consultants, LLC | | |
| Southbridge PS | Southbridge HS | Construction | New Construction | Joslin, Lesser & Associates, Inc. | Tappe Associates, Inc. | Environmental Health and Engineering | CMR - CM Selected | Consigli Construction Co. |

| Yellow = Wait List Project | |
|---|---|
| Geen = Green Repair | Red = Changes in last 60 days |

# Master District Status List

| District Name | School Name | Status | Preferred Schematic | OPM | Designer | Cx Authority | Procurement Status | CM/GC |
|---|---|---|---|---|---|---|---|---|
| Southeastern Reg Voc Tech PS | Southeastern Regional Voc / Tech HS | Design Development | Addition/Renovation | RF Walsh Collaborative Partners | Drummey Rosane Anderson, Inc. | RDK Engineering | | |
| Southern Worcester Cty VT PS | Bay Path Regional Voc / Tech HS | Feasibility Study | | Heery International, Inc | Kaestle Boos Associates, Inc. | | | |
| Southwick-Tolland | Woodland ES | Feasibility Study | | Strategic Building Solutions, LLC | JCJ Architecture, PC | | | |
| Spencer-E Brookfield PS | David Prouty HS | OPM Selection | | | | | | |
| Springfield PS | Forest Park Middle School | Design Development | Addition/Renovation | ARCADIS-U.S., Inc. | Perkins Eastman | Foreman Building Commissioning, LP | | |
| Springfield PS | SCIPP Years 2 & 3 | Feasibility Study | Repair | | CGKV Architects, Inc./Gale Associates, Inc. | VP Consultants, LLC | | |
| Springfield PS | Putnam Voc / Tech HS | Construction | New Construction | ARCADIS | Drummey Rosane Anderson, Inc. | Strategic Building Solutions | CMR - CM Selected | Consigli Construction Co. |
| Stoneham PS | Stoneham MS | Feasibility Study | | Joslin, Lesser & Associates | Tappe Associates, Inc. | | | |
| Sturbridge PS | Burgess ES | Construction | Addition/Renovation | Lamoureux Pagano & Associates, Inc. | Drummey Rosane Anderson, Inc. | Horizon Engineering Associates, LLP | DBB - Contract Awarded | Fontaine Bros. |
| Sudbury PS | Peter Noyes ES | Construction | Repair | Compass Project Management, Inc. | Russo Barr Associates, Inc./BLW Engineers, Inc. | RDK Engineering | | |
| Sutton PS | Sutton MS | Construction | Addition/Renovation | Strategic Building Solutions | Flansburgh Associates, Inc. | RDK Engineering | | |
| Tantasqua PS | Tantasqua Reg JHS | Design Development | Repair | Diversified Project Management | Habeeb & Associates Architects, Inc. | Cannon Design | | |
| Taunton PS | Taunton HS | Construction | Addition/Renovation | Gilbane | Design Partnership of Cambridge, Inc. | | DBB - Contract Awarded | Bacon-Agostini Construction Joint Venture |
| Tewksbury PS | Tewksbury Memorial HS | Construction | Model School | Heery International, Inc | Symmes Maini & McKee Associates, Inc. | Sebesta Blomberg & Associates | DBB - Contract Awarded | CTA Ventures/ Methuen |
| Tri County PS | Tri County Regional Voc / Tech HS | Construction | Repair | Knight, Bagge, & Anderson, Inc. | Richard D. Kimball Company, Inc. | WSP Flack + Kurtz | | |
| Upper Cape Cod Voc Tech PS | Upper Cape Cod Voc / Tech HS | Approved Project Vote Pending | Repair | NETCO Construction Project Managers, Inc. | Knight, Bagge & Anderson, Inc. | Gale Associates, Inc. | | |
| Uxbridge PS | Uxbridge HS | Construction | New Construction | Joslin, Lesser & Associates, Inc. | Raymond Design Associates, Inc. | Turner Facilities Management Solutions | CMR - CM Selected | Shawmut Design and Construction |
| Wachusett PS | Mountview MS | OPM Selection | | Town Employee | | | | |
| Wachusett PS | Naquag ES | Design Development | Repair | Strategic Building Solutions, LLC | LPBA/ Architects, Inc. | RFS Engineering | | |
| Wachusett PS | Paxton K-8 Center | Design Development | Repair | Strategic Building Solutions, LLC | LPBA/ Architects, Inc. | RFS Engineering | | |
| Wachusett PS | Thomas Prince K-8 | Design Development | Repair | Strategic Building Solutions, LLC | LPBA/ Architects, Inc. | RFS Engineering | | |
| Wakefield PS | Galvin MS | Feasibility Study | | | Tappe Associates | | | |
| Wakefield PS | Wakefield Memorial HS | Closeout/Audit | Addition/Renovation | | | | | |
| Walpole PS | Bird MS | Closeout/Audit | Repair | | UDA Architects | | Undetermined | Wayne Roofing |
| Wayland PS | Wayland HS | Construction | New Construction | KV Associates | HMFH Architects, Inc. | WSP Flack + Kurtz | CMR - CM Selected | Shawmut Construction |
| Webster PS | Park Avenue ES | Designer Selection | | RF Walsh Collaborative Partners | | | | |

| Yellow = Wait List Project | |
|---|---|
| Geen = Green Repair | Red = Changes in last 60 days |

# Master District Status List

| District Name | School Name | Status | Preferred Schematic | OPM | Designer | Cx Authority | Procurement Status | CM/GC |
|---|---|---|---|---|---|---|---|---|
| Wellesley PS | Wellesley SHS | Construction | New Construction | Ryegate Inc | Symmes Maini & McKee Associates, Inc. | RFS Engineering | CMR - CM Selected | Turner Construction |
| West Boylston PS | Major Edwards ES | Project Scope & Budget | Repair | URS Corporation | Reinhardt Associates, Inc. | | | |
| West Boylston PS | West Boylston JHS / SHS | Feasibility Study | Repair | URS Corporation | Reinhardt Associates, Inc. | | | |
| West Bridgewater PS | West Bridgewater JHS / SHS | Designer Selection | | Strategic Building Solutions, LLC | | | | |
| West Springfield PS | West Springfield HS | Design Development | Model School | Strategic Building Solutions, LLC | Symmes Maini & McKee Associates, Inc. | Turner Facilities Management Solutions | | |
| Westborough PS | Sarah W Gibbons MS | Local Clearance - 09/10 | | | | | | |
| Westfield PS | Highland School | Design Development | Repair | P3 Project Planning Professionals | Tighe & Bond, Inc. | Strategic Building Solutions | | |
| Westfield PS | Southampton Road ES | Construction | Repair | P3 Project Planning Professionals | Tighe & Bond, Inc. | Strategic Building Solutions | Undetermined | R&H Roofing |
| Westfield PS | Westfield Voc / Tech HS | Design Development | Repair | P3 Project Planning Professionals | Tighe & Bond, Inc. | Strategic Building Solutions | | |
| Westfield PS | Westfield HS | Design Development | Repair | P3 Project Planning Professionals | Tighe & Bond, Inc. | Strategic Building Solutions | | |
| Westfield PS | Paper Mill ES | Design Development | Repair | P3 Project Planning Professionals | Tighe & Bond, Inc. | Strategic Building Solutions | | |
| Westfield PS | Abner Gibbs ES | Preferred Schematic | Model School | Skanska USA Building Inc. | Margo Jones Architects, Inc. | | | |
| Westfield PS | Highland School | Construction | Repair | P3 Project Planning Professionals | Tighe & Bond, Inc. | Strategic Building Solutions | Undetermined | Allied Restoration |
| Westfield PS | Southampton Road ES | Design Development | Repair | P3 Project Planning Professionals | Tighe & Bond, Inc. | Strategic Building Solutions | | |
| Weston PS | Field ES School | Feasibility Study | | Compass Project Management, Inc | Jonathan Levi Architects LLC | | | |
| Weston PS | Weston HS | Design Development | Repair | Compass Project Management, Inc. | Garcia Galuska DeSousa | RDK Engineering | | |
| Weston PS | Weston MS | Design Development | Repair | Compass Project Management, Inc. | Russo Barr Associates, Inc. | RDK Engineering | | |
| Westport PS | Alice A Macomber ECC | Project Scope & Budget | Repair | Pinck & Co., Inc. | CGKV Architects, Inc. | | | |
| Westport PS | Westport HS | Project Scope & Budget | Repair | Pinck & Co., Inc. | CGKV Architects, Inc. | | | |
| Westport PS | Westport MS | Feasibility Study | Repair | Pinck & Co., Inc. | CGKV Architects, Inc. | | | |
| Weymouth PS | Abigail Adams MS | Design Development | Repair | Knight, Bagge, & Anderson, Inc. | Gale Associates, Inc. | Cannon Design | | |
| Whitman-Hanson PS | John H Duval ES | Closeout/Audit | Repair | | BETA Group, Inc. | | Undetermined | S.I. Services, Inc. |
| Whitman-Hanson PS | Maquan ES | OPM Selection | | | | | | |
| Williamsburg PS | Anne T Dunphy IS | Feasibility Study | | Arcadis | Drummey Rosane Anderson, Inc. | | | |
| Wilmington PS | Wilmington HS | Feasibility Study | | Joslin, Lesser & Associates | Dore & Whittier Architects, Inc. | | | |
| Wilmington PS | Shawsheen ES | Design Development | Repair | P3 Project Planning Professionals | Russo Barr Associates, Inc. | CBI Consulting Inc. | | |

| Yellow = Wait List Project | |
|---|---|
| Geen = Green Repair | Red = Changes in last 60 days |

# Master District Status List

| District Name | School Name | Status | Preferred Schematic | OPM | Designer | Cx Authority | Procurement Status | CM/GC |
|---|---|---|---|---|---|---|---|---|
| Winchendon PS | Toy Town ES | Construction | Repair | NETCO Construction Project Managers, Inc. | Hesnor Engineering Company | RFS Engineering | | |
| Winchester PS | Winchester HS | Feasibility Study | | | | | | |
| Winchester PS | Vinson-Owen ES | Design Development | New Construction | Town of Winchester | Tappe Associates, Inc. | Turner Facilities Management Solutions | Undetermined | |
| Winchester PS | Lynch ES | Construction | Repair | Knight, Bagge, & Anderson, Inc. | Gale Associates, Inc. | Simpson Gumpertz & Heger | | |
| Winthrop PS | Winthrop Senior High | Designer Selection | | Skanska USA Building, Inc. | | | | |
| Woburn PS | John F Kennedy MS | Construction | Repair | Municipal Building Consultants, Inc. | Gale Associates, Inc. | Simpson Gumpertz & Heger | | |
| Woburn PS | Goodyear ES | Construction | New Construction | Municipal Building Consultants, Inc. | Tappe Associates, Inc. | Strategic Building Solutions | CMR - CM Selected | Gilbane Building Company |
| Woburn PS | Daniel L Joyce MS | Construction | Repair | Municipal Building Consultants, Inc. | Gale Associates, Inc. | Simpson Gumpertz & Heger | | |
| Worcester PS | North HS | Construction | | Maguire Group Inc | City of Worcester | | CMR - CM Selected | Gilbane Building Company |

**No. of Projects: 318**

## Project Status | July 13, 2011

New Program: 122
Waitlist: 9
Green Repair: 161
Closeout / Audit Complete: 24
Final Closout / Removal: 13
Total Projects: 329

45
40
35
30
25
20
15
10
5

2007 / 2008
2009/2010

**Final Closeout / Removal**

Ashland (R)
David Mindess ES
Avon (R)
Ralph D Butler ES
Bedford
High School
Chelmsford
McCarthy/Parker Schools
Duxbury (R)
Chandler ES
Hadley (R)
Hopkins Academy HS
Hingham
Hingham ES
Hopedale (R)
Memorial ES
North Attleboro
Joseph Martin ES
Quincy (WL)
Quincy High School
Springfield (R)
SCIPP Year 1
Whittier Reg
Voc Tech HS
Walpole
Bird MS

| Total Projects | Local Clearance Vote | OPM Selection | Designer Selection | Feasibility Study | Preferred Schematic | Project Scope & Budget | Approved Project Vote Pending | Design Development | Building Completion 2013 | Building Completion 2012 | Building Completion 2011 | Closeout |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| 329 | 18 | 14 | 9 | 31 | 10 | 24 | 8 | 83 | 10 | 26 | 59 | 37 |

Abington
Frolio Jr Hs
Chelsea (R)
Clark Ave School MS
Fitchburg (R)
Crocker ES
Oxford (R)
Middle School
Athol-Royalston ( R )
Riverbend ES
Ayer Shirley
High School
Boston
Dearborn MS
Gloucester
West Parish ES
Harwich - Chatham (MS)
Harwich - Chatham HS
Lunenburg
High School
Lynn
Thurgood Marshall MS
Minuteman Regional
Minutemen RVT
Northampton
Smith Voc & Agr.
Northeast Metropolitan
NE Metropolitan RVT
Orange
Dexter Park Intermediate
Revere
McKinley ES
Westborough (R)
Sarah W Gibbons MS
Winchester
High School

Auburn
Middle School
Berkshire Hills
Monument Mountain
Regional HS
Greater Lowell
Greater Lowell RVT (R)
Holbrook
Jr/Sr High School
Lexington
Estabrook ES
New Bedford
Hannigan / Taylor ES
New Bedford
High School
Newburyport
Bresnahan ES (MS)
Newburyport
Rupert A Nock MS
Old Colony Regional
Old Colony RVT
South Hadley
Plains ES
Spencer-East Brookfield
David Prouty HS
Wachusett
Mountview MS
Whitman-Hanson
Maquan ES

Boston
Upper Quincy HS
Chicopee
Chicopee MS
Greater New Bedford
Vocational Technical HS
Lynnfield
High School
Marshfield
Marshfield HS (MS)
Somerset-Berkley (MS)
Regional HS
Webster
Park Avenue ES
West Bridgewater
High School
Winthrop
Sr High School

Agawam
Agawam MS
Hadley
Hopkins Academy
Lowell
Lowell HS
Lowell
Moody ES
Lowell
Peter W Reilly School
Lowell
Washington School
Marlborough
Francis J. Kane ES
Marlborough
Marlborough HS
Natick
Johnson School
North Andover
Annie L Sargent School
North Andover
Atkinson School
North Andover
North Andover MS
Pioneer Valley
Bernardston ES
Pioneer Valley
Northfield ES
Pioneer Valley
Pioneer Valley Reg. MS / HS
Springfield
SCIPP Years 2 & 3
West Boylston
West Boylston Jr-Sr HS
Westport
Westport MS

Georgetown
Penn Brook ES
Greenfield
High School
Hingham (MS)
Hingham MS
Lincoln
K-8
Narragansett
Templeton Center ES
North Adams
Silvio O Conte MS
North Reading
High School
Peabody
J Henry Higgins MS
Pittsfield
Taconic HS
Southwick-Tolland
Woodland ES
Stoneham (R)
Middle School
Wakefield
Galvin MS
Williamsburg
Dunphy ES

Assabet Valley
Assabet Valley RVT
Concord-Carlisle
High School
Duxbury (MS)
High School
Fairhaven
Rogers ES
Franklin
High School
Saugus (R)
Belmonte Saugus MS
Southern Worcester
Baypath RVT HS
Westfield (MS)
Abner Gibbs ES
Weston
Field ES
Wilmington
High School

Cape Cod Regional
Cape Cod Voc Tech
Grafton
Grafton Memorial Sr. HS
Haverhill
Caleb Dustin Hunking MS
Haverhill
Consentino MS
Haverhill
John G. Whittier MS
Haverhill
Walnut Square ES
Haverhill
Greenleaf ES
Haverhill
Tilton ES
Middleborough
Mary K. Goode ES
Mohawk Trail Buckland-
Shelburne ES
Mohawk Trail
Colrain Central School
Mohawk Trail
Mohawk Trail Regional HS
Nauset
Nauset Regional HS
North Middlesex
Ashby ES
North Middlesex
Spaulding Memorial ES
Northborough
Robert E. Melican MS
Peabody
John E. Burke School
Peabody
William A Welch Sr. ES
Salem
Collins MS
Salem
Saltonstall ES
West Boylston
Major Edwards ES
Westport
Alice A Macomber Primary
Westport
Westport HS
Arlington
Thompson ES

Boston
Clarence R. Edwards MS
Boston
Joseph Lee ES
Boston
Washington Irving MS
Boston
Excel HS
Boston
Thomas A. Edison MS
Central Berkshire
Craneville ES
Central Berkshire
Kittredge ES
Hopkinton
Center ES

Abington
Woodsdale ES
Amherst-Pelham
Amherst Regional MS
Andover
Andover West MS
Avon
Ralph D. Butler ES
Billerica
Billerica Memorial HS
Blackstone Valley RVTHS
Brockton
Hancock ES
Brockton
West Junior HS
Brockton
Downey ES
Brockton
East MS
Brockton
Edgar B. Davis K-8
Brockton
High School
Brockton
North Junior HS
Brockton
Oscar F. Raymond K-8
Chelmsford
Byam ES
Chelmsford
Chelmsford HS
Dartmouth
James M. Quinn ES
Dennis-Yarmouth
Ezra H Baker ES
Dudley-Charlton
Sheperd Hill Regional HS
Fairhaven
Hastings MS
Gloucester
Beeman Memorial School
Gloucester
East Gloucester ES
Gloucester
Plum Cove ES
Gloucester
Ralph B O'Maley MS
Gloucester
Veterans Memorial School
Grafton
South Grafton ES
Greenfield
Four Corners ES
Leicester
Leicester Memorial ES
Leicester
Leicester MS
Leverett
Leverett ES
Melrose
Melrose HS

Mendon-Upton
Miscoe Hill School
Narragansett
Narragansett MS
Narragansett
Phillipston Memorial School
Nashoba
Nashoba Reg. Valley Tech
HS
New Salem-Wendell Swift
River ES
Newton
Bowen ES
Newton
Williams ES
North Attleborough
Falls ES
North Brookfield
North Brookfield ES
Pentucket
Dr. Frederick N. Sweetsir
School
Pentucket
Dr. John C. Page School
Pentucket
Elmer S. Bagnall
Pentucket
Helen R. Donaghue School
Plymouth
Community Intermediate
Rockland
R. Stewart Esten ES
Sandwich
Oak Ridge ES
Sandwich
Forestdale School
Tantasqua
Tantasqua MS
Upper Cape Cod RVTHS
Wachusett
Naquag ES
Wachusett
Paxton Center School
Wachusett
Thomas Prince School
Westfield
Paper Mill ES
Westfield
Westfield HS
Westfield
Westfield Voc Tech HS
Westfield
Highland ES
Westfield
Southhampton Road ES
Weston
Weston HS
Weston
Weston MS
Weymouth
Abigail Adams MS
Wilmington
Shawsheen ES

Andover
Bancroft ES
Ashburnham- Westminster
Briggs ES
Brookline
Heath ES
Douglas (MS)
Intermediate School
Dracut
Sr High School
East Bridgewater (MS)
High School
Essex /N. Shore
Agr/Voc Tech HS
Fall River
Morton MS
Hudson
John F Kennedy MS
Marblehead
Glover ES
Maynard
High School
Medway (R)
Middle School
Methuen
High School
Norfolk County
Norfolk County Agr
Norton
High School
Quincy (MS)
Central MS
Somerville
E Community School
Southeastern Regional
Southeastern RVT
Springfield (WL)
Forest Park MS
West Springfield (MS)
High School
Winchester
Vinson-Owen ES

Adams-Cheshire
Adams MS
Berlin-Boylston
Tahanto Reg HS
Burlington
Marshall Simonds MS
Danvers
High School
Easthampton
High School
Leominster
Sr High School
Longmeadow
High School
Natick (MS)
High School
Shrewsbury
Sherwood MS
Sutton
Middle School

Brookfield
Brookfield ES
Fitchburg
Memorial Intermediate
Fitchburg
Reingold ES
Fitchburg
South Street ES
Palmer
Old Mill Pond ES
Palmer
Palmer HS
Palmer
Converse MS
Shrewsbury
Spring Street ES
Billerica
Parker ES
Brookline
John D Runkle K-8
Carlisle
K-8
Dedham
Avery ES
Grafton
Memorial Sr HS
Hampden-Wilbraham (MS)
Minnechaug HS
Nashoba
Pompositticut ES
Needham (R)
Newman ES
Norfolk
Freeman-Centenntial ES
Plymouth (MS)
North HS
Rockland
John W Rogers MS
Sharon
Middle School
Southbridge
High School
Springfield (WL)
Putnam Voc Tec HS
Sturbridge
Burgess ES
Tewksbury (MS)
Memorial HS
Uxbridge
High School
Wellesley
Sr High School

Arlington
M. Norcross Stratton ES
Attleboro
A. Irvin Studley ES
Attleboro
Attleboro High School
Attleboro
Hill-Roberts ES
Attleboro
Hyman Fine ES
Barnstable
West Barnstable ES
Bellingham
Bellingham Memorial MS
Braintree
Archie T Morrison ES
Braintree
Braintree High School
Braintree
East MS
Braintree
Highlands ES
Braintree
Hollis ES
Canton
Canton HS
Canton
Rodman ECC
Falmouth
North Falmouth ES
Falmouth
East Falmouth ES
Fitchburg
Fitchburg HS
Fitchburg
Reingold ES
Fitchburg
Goodrich School
Fitchburg
Memorial Intermediate
Fitchburg
South Street ES
Framingham
Mary E Stapleton ES
Gardner
Elm Street School
Gardner
Gardner HS
Gardner
Waterford Primary
Hancock
Hancock ES
Lexington
Lexington HS
Needham
Pollard MS
Quabbin
Quabbin Regional High
School
Reading
Birch Meadow ES
Reading
J. Warren Killam ES
Scituate
Wampatuck ES
Sharon
Sharon HS
South Shore Reg
Voc Tech HS
Sudbury
Peter Noyes ES
Tri County Regional
Tri County Voc Tech
Westfield
Southampton Road ES
Westfield
Highland ES
Winchendon
Toy Town ES
Winchester
Lynch ES
Woburn
Daniel L. Joyce MS
Woburn
John F. Kennedy MS

Belmont
Roger E Wellington ES
Beverly
High School
Burlington
Memorial ES
Foxborough (R)
High School
Hanover
High School
Haverhill (WL)
Havehill High School
Holyoke (WL)
Holyoke High School
Malden (WL)
Malden HS
Marshfield (R)
Gov Edward Winslow ES
Middleton
Howe-Manning
Norwood (MS)
High School
Rochester
Memorial ES
Shawsheen Valley
Shawsheen Valley VTHS
Taunton (WL)
Parker Middle/High School
Wayland
High School
Woburn
Goodyear ES
Worcester (WL)
North High School

Acton
Douglas ES
Boxford
Harry Lee Cole ES
Conway
Conway Grammar ES
Dartmouth
James Quinn ES
Florida
Abbott Memorial K-8
Orange
Butterfield ES
Plymouth
West ES
Quabbin
Oakham Center ES
Rockport
High School
Rockport
Rockport ES
Whitman-Hanson
John H Duval Jr. ES
Braintree (R)
South MS
Cambridge (WL)
Rindge and Latin HS
Falmouth (WL)
Falmouth HS
Hamilton-Wenham (R)
Cutler School
Littleton (R)
Russell St ES
Lowell (WL)
Morey PK-4
Manchester Essex
Reg Jr/Sr High School
Marblehead (R)
Village ES
Mount Greylock (R)
Regional HS
New Bedford (WL)
Abraham Lincoln ES
Newton (WL)
Newton North HS
Revere (WL)
Paul Revere ES
Wakefield
High School

# PROJECT STATUS

Waitlist Projects
Green Repair Projects
Project Complete

New Program Projects
Capital Pipeline Status Presented at June 8, 2011 Board of Directors Meeting

# 2011 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

- Denotes bid phase in progress or complete

- Denotes estimated bid dates

| DISTRICT<br>*Projects Considering the CM @ Risk Method | DESIGN BASIS FOR ENROLLMENT | PROJECT BUDGET<br>Shown in Millions | CONSTRUCTION BUDGET<br>Shown in Millions | JAN | FEB | MAR | APR | MAY | JUN | JUL | AUG | SEP | OCT | NOV | DEC |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| ***SOUTHBRIDGE** | 1050 | $76.5 | 60.1 | Southbridge HS New Construction: Filed-Sub Bids rcv'd 1/7. GMP Issued 2/7. | | | | | | | | | | | |
| ***SHREWSBURY** | 900 | $47.3 | $37.0 | Sherwood MS New Construction: Filed-Sub Bids rcv'd 2/7. GMP Issued 5/10. | | | | | | | | | | | |
| **SO. SHORE RVT** | 595 | $3.2 | $2.6 | Regional VTHS Repair: Filed-Sub Bids rcv'd 1/7. G.C. Bids rcv'd 1/18. NTP issued 5/9. | | | | | | | | | | | |
| **CARLISLE** | 700 | $20.0 | $15.6 | Carlisle ES Addition/Renovation: Filed-Sub Bids rcv'd 1/26. G.C. Bids rcv'd 2/4. NTP Issued 2/9. | | | | | | | | | | | |
| **MARSHFIELD** | 485 | $2.4 | $2.0 | Marshfield Edward Winslow ES Repair: Filed-Sub Bids rcv'd 1/14. G.C. Bids rcv'd 1/21. NTP Issued 2/12. | | | | | | | | | | | |
| ***UXBRIDGE** | 600 | $43.0 | $34.4 | Uxbridge HS New Construction: Early Site & Steel Package rcv'd 1/13. Filed-Sub Bids rcv'd 3/17. GMP Issued 3/31. | | | | | | | | | | | |
| ***BURLINGTON** | 880 | $32.9 | $24.7 | Marshall Simonds MS Addition/Renovation: Filed-Sub Bids rcv'd 3/22. GMP Issued 4/12. | | | | | | | | | | | |
| **BERLIN / BOYLSTON** | 560 | $44.0 | $34.2 | Tahanto MS/HS New Construction: Filed-Sub Bids rcv'd 4/7. G.C. Bids rcv'd 4/20. NTP issued 5/10. | | | | | | | | | | | |
| **EASTHAMPTON** | 510 | $43.7 | $33.5 | Easthampton HS New Construction: Filed-Sub Bids rcv'd 4/20. G.C. Bids rcv'd 5/6. NTP issued 5/16. | | | | | | | | | | | |
| ***LONGMEADOW** | 1000 | $78.5 | $63.8 | Longmeadow HS New Construction: Filed-Sub Bids rcv'd 4/28. GMP issued 5/12. | | | | | | | | | | | |
| **SUTTON** | 840 | $59.9 | $46.4 | Sutton MS New Construction: Filed-Sub Bids Due 5/4. G.C.Bids Due 5/18. NTP issued 5/26. | | | | | | | | | | | |
| ***LEOMINSTER** | 1805 | $45.9 | $32.7 | Leominster HS Addition/Renovation: Filed-Sub Bids Due 6/2. GMP issued 6/23. | | | | | | | | | | | |
| ***SOMERVILLE** | 500 | $33.2 | $15.2 | East Somerville Community School Addition/Renovation: Filed-Sub Bids Due 6/14. GMP Targeted July. | | | | | | | | | | | |
| ***ADAMS/CHESHIRE** | 805 | $40.6 | $30.0 | Hoosac Valley MHS Addition/Renovation: Filed-Sub Bids Due 7/26. GMP Targeted July | | | | | | | | | | | |
| **MAYNARD** | 410 | $45.8 | $35.6 | Maynard HS New Construction: Filed-Sub Bids Due 7/13. G.C. Bids Due 7/27. NTP Targeted August. | | | | | | | | | | | |
| **HUDSON** | 715 | $44.1 | $34.8 | JFK MS New Construction: Filed-Sub Bids Due 8/29. G.C. Bids Due 9/12. NTP Targeted September. | | | | | | | | | | | |
| ***METHUEN** | 2075 | $99.1 | $74.9 | Methuen HS Addition/Renovation: Filed-Sub Bids Due8/23. GMP Targeted Sept-Oct. | | | | | | | | | | | |
| **Subtotal** | **14,430** | **$760.1** | **$577.5** | | | | | | | | | | | | |

# 2011 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

- Denotes bid phase in progress or complete

- Denotes estimated bid dates

| DISTRICT<br>*Projects Considering the CM @ Risk Method | DESIGN BASIS FOR ENROLLMENT | PROJECT BUDGET<br>Shown in Millions | CONSTRUCTION BUDGET<br>Shown in Millions | JAN | FEB | MAR | APR | MAY | JUN | JUL | AUG | SEP | OCT | NOV | DEC |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| ***MEDWAY** | 853 | $22.1 | $18.2 | | | | | | | | | | | | |
| **EAST BRIDGEWATER** | 950 | $77.1 | $60.3 | | | | | | | | | | | | |
| ***ANDOVER** | 680 | $44.7 | $34.5 | | | | | | | | | | | | |
| **BROOKLINE** | 560 | $8.8 | $7.0 | | | | | | | | | | | | |
| **WEST SPRINGFIELD** | 1270 | $107.6 | $73.3 | | | | | | | | | | | | |
| **FALL RIVER** | 625 | $53.2 | $42.4 | | | | | | | | | | | | |
| **QUINCY** | 620 | $50.0 | $32.6 | | | | | | | | | | | | |
| **WINCHESTER** | 420 | $28.7 | $21.7 | | | | | | | | | | | | |
| **DOUGLAS** | 552 | $32.2 | $24.8 | | | | | | | | | | | | |
| ***ASHBURNHAM-WESTMINSTER** | 520 | $30.0 | $24.8 | | | | | | | | | | | | |
| ***SRINGFIELD -FOREST PARK** | 660 | $43.4 | $34.0 | | | | | | | | | | | | |
| **NORFOLK COUNTY AGRICULUTURAL** | 550 | $28.6 | $22.3 | | | | | | | | | | | | |
| **Subtotal** | **8,260** | **$526.4** | **$395.9** | | | | | | | | | | | | |
| **GRAND TOTAL** | **22,690** | **$1.286B** | **$973.4** | | | | | | | | | | | | |
| **Number of Construction-Related Employment** | | | **4,867** | | | | | | | | | | | | |

Medway MS Repair: Filed-Sub Bids Due 9/27. GMP Targeted October.

East Bridgewater HS New Construction: Filed-Sub Bids Due 8/10. G.C. Bids Due 8/24. NTP TargetedAugust.

Bancroft ES New Construction: Early Site Packages Due 7/15. Early Foundation and Steel Packages Due 9/7.

Filed-Sub Bids Due 10/30. GMP Targeted December.

Brookline Heath ES Addition/Renovation: Filed-Sub Bids Due 8/26. G.C. Bids Due 9/7. NTP Targeted September

West Springfield HS New Construction: Filed-Sub Bids Due 9/9. G.C. Bids Due 10/3. NTP Targeted October

Fall River Morton MS New Construction: Filed-Sub Bids Due August. G.C. Bids Due September. NTP Targeted September.

Central MS HS New Construction: Filed-Sub Bids Due 10/25. G.C. Bids Due 11/15. NTP Targeted December.

Vinson-Owen ES New Construction: Filed-Sub Bids Due 11/24. G.C. Bids Due 12/15. NTP Targeted January 2012.

Douglas IS New Construction: Filed Sub Bids Due 12/2. G.C. Bids Due 12/16. NTP Targeted December.

JR Briggs ES New Construction: Filed-Sub and G.C. Bids Targeted November to February. NTP Targeted March

Springfield Forest Park MS : Filed Sub Bids Due 12/27. GMP Targeted February 2012.

Norfolk County Aggi Renovation: Filed Sub Bids Due 12/5. G.C. Bids Due 12/19. NTP Targeted December.

# 2012 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.


Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

- Denotes bid phase in progress or complete

- Denotes estimated bid dates

| DISTRICT<br>*Projects Considering the CM @ Risk Method | DESIGN BASIS FOR ENROLLMENT | PROJECT BUDGET<br>Shown in Millions | CONSTRUCTION BUDGET<br>Shown in Millions | JAN | FEB | MAR | APR | MAY | JUN | JUL | AUG | SEP | OCT | NOV | DEC |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| ***ESSEX-NS** | 1440 | $125.0 | $96.50 | | | | Essex Northshore HS New Construction: Early Site Packages 11/21/11 - 1/19/12. Filed-Sub Bids Due 3/1/12. GMP Targeted April. | | | | | | | | |
| **DRACUT** | 1160 | $60.4 | $47.30 | | | | Dracut Senior HS Addition/Renovation: Filed-Sub Bids Due 2/1. G.C. Bids Due 2/15. NTP Targeted March | | | | | | | | |
| ***NORTON** | 700 | $34.6 | $27.0 | | | | Norton HS Addition/RenovationFiled-Sub Bids Due 2/9. GMP Targeted March. | | | | | | | | |
| **MARBLEHEAD** | 425 | $25.9 | $20.2 | | | | | Marblehead Glover ES New Construction: Filed-Sub Bids Due 2/29. GMP Targeted March. | | | | | | | |
| **Subtotal** | **3,725** | **$245.9** | **$191.0** | | | | | | | | | | | | |
| **GRAND TOTAL** | **3,725** | **$246** | **$191** | | | | | | | | | | | | |
| **Number of Construction-Related Employment** | | | **955** | | | | | | | | | | | | |

| District-MSBA | Project Name | Due Date |
|---|---|---|
| **Roof Projects** | | |
| Hancock. | Hancock Elementary | 2/15/11 A |
| Attleboro | A Irvin Studley Elementary School | 2/23/11 A |
| Attleboro | Hill Roberts Elementary School | 2/23/11 A |
| Attleboro | Hyman Fine Elementary School | 2/23/11 A |
| Falmouth | East Falmouth Elem | 2/24/11 A |
| Falmouth | North Falmouth Elem | 2/24/11 A |
| Braintree | Braintree High School | 3/10/11 A |
| Quabbin | Quabbin Regional High School | 3/22/11 A |
| Andover | Andover West Middle | 3/28/11 A |
| Sharon | Sharon High School | 4/11/11 A |
| Sudbury | Peter Noyes | 4/14/11 A |
| Melrose | Melrose High | 4/20/11 A |
| Chelmsford | Byam School | 4/28/11 A |
| Winchester | Lynch Elementary | 4/28/11 A |
| Needham | Pollard Middle | 5/3/11 A |
| Lexington | Lexington High | 5/4/11 A |
| Springfield PS | Frank H Freedman ES | 5/4/11 A |
| Springfield PS | John F Kennedy MS | 5/4/11 A |
| Springfield PS | Gerena ES | 5/5/11 A |
| Canton | Canton High | 5/6/11 A |
| Canton | Rodman Early Childhood Center | 5/6/11 A |
| Springfield PS | Warner ES | 5/13/11 A |
| Palmer | Palmer High | 5/13/11 A |
| Tantasqua | Tantasqua Reg Jr High | 5/17/11 A |
| Palmer | Old Mill Pond | 5/25/11 A |
| Fitchburg | Reingold Elementary (Phase 2) | 5/26/11 A |
| Westfield | Southampton Road ES | 5/26/11 A |
| Fitchburg | Memorial Intermediate (Phase 2) | 5/26/11 A |
| Westfield | Highland ES | 5/26/11 A |
| Orange. | Butterfield | 5/31/11 |
| Reading | J Warren Killam | 6/1/11 |
| Gardner | Elm Street School | 6/2/11 |
| Gardner | Gardner High | 6/2/11 |
| Gardner | Waterford Primary School | 6/2/11 |
| Dennis Yarmouth | Ezra H Baker Elementary School | 6/4/11 |
| Weston | Weston Middle | 6/4/11 |
| Leverett | Leverett Elementary | 6/7/11 |
| Narrangsett | Narragansett Middle | 6/8/11 |
| Central Berkshire | Craneville | 6/11/11 |
| Pentucket | Dr John C Page School | 6/13/11 |
| Pentucket | Elmer S Bagnall | 6/13/11 |
| Pentucket | Helen R Donaghue School | 6/13/11 |
| Boston | Washington Irving Middle | 6/14/11 |
| Leicester | Leicester Middle | 6/15/11 |
| Woburn | John F Kennedy Middle School | 6/15/11 |
| Plymouth | Plymouth Commun Intermed | 6/16/11 |
| Sandwich | Forestdale | 6/16/11 |
| Sandwich | Oak Ridge K-8 | 6/16/11 |
| Weymouth | Abigali Adams Middle School | 6/17/11 |
| Avon | Ralph D Butler | 6/22/11 |
| Woburn | Daniel L Joyce Middle School | 6/22/11 |
| Central Berkshire | Kittredge | 6/23/11 |

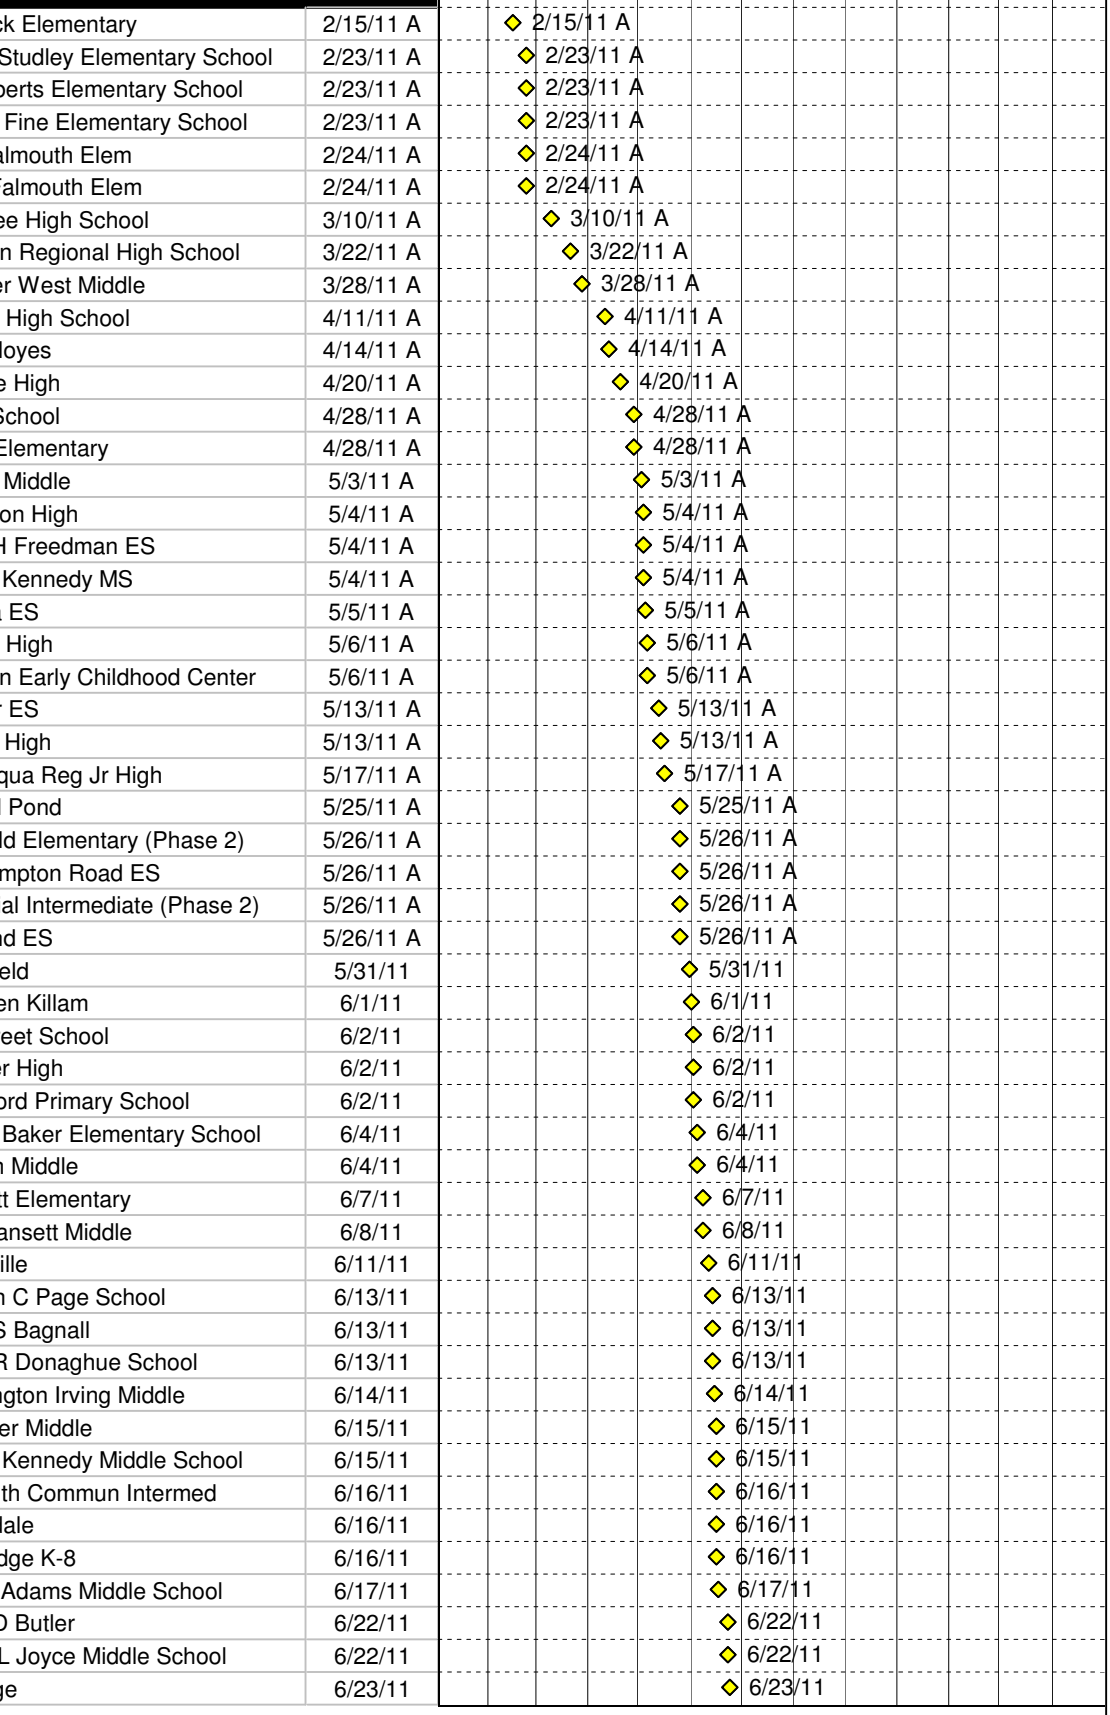



Massachusetts School Building Authority

MSBA-Green Repair Program
Projects with Bids Due Dates

Dates are based on the last update of June 23, 2011.

| District-MSBA | Project Name | Due Date | 2011 | | | | | | | | | | | | 2012 |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | | | Jan | Feb | Mar | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan |
| Boston | Joseph Lee | 6/24/11 | | | | | | 6/24/11 | | | | | | | |
| Boston | Thomas A Edison Jr High | 6/24/11 | | | | | | 6/24/11 | | | | | | | |
| Shrewsbury | Spring Street School | 7/1/11 | | | | | | | 7/1/11 | | | | | | |
| Dartmouth | James M Quinn School | 7/6/11 | | | | | | | 7/6/11 | | | | | | |
| Gloucester | Beeman Memorial School | 7/6/11 | | | | | | | 7/6/11 | | | | | | |
| Gloucester | East Gloucester Elementary School | 7/6/11 | | | | | | | 7/6/11 | | | | | | |
| Gloucester | Plum Cove ES | 7/6/11 | | | | | | | 7/6/11 | | | | | | |
| Gloucester | Veterans Memorial School | 7/6/11 | | | | | | | 7/6/11 | | | | | | |
| New Salem Wendell | Swift River | 7/7/11 | | | | | | | 7/7/11 | | | | | | |
| Gloucester | Ralph B O'Maley Middle School | 7/7/11 | | | | | | | 7/7/11 | | | | | | |
| Blackstone Valley RT | Blackstone Valley | 7/8/11 | | | | | | | 7/8/11 | | | | | | |
| Wachusett | Naquag Elementary | 7/12/11 | | | | | | | 7/12/11 | | | | | | |
| Wachusett | Paxton Center | 7/12/11 | | | | | | | 7/12/11 | | | | | | |
| Wachusett | Thomas Prince | 7/12/11 | | | | | | | 7/12/11 | | | | | | |
| Newton | Bowen | 7/15/11 | | | | | | | 7/15/11 | | | | | | |
| Walpole | Bird | 7/21/11 | | | | | | | 7/21/11 | | | | | | |
| Greenfield | Four Corners | 7/27/11 | | | | | | | | 7/27/11 | | | | | |
| Brockton | Brockton High | 7/29/11 | | | | | | | | 7/29/11 | | | | | |
| Brockton | Downey | 7/29/11 | | | | | | | | 7/29/11 | | | | | |
| Brockton | East Junior High | 7/29/11 | | | | | | | | 7/29/11 | | | | | |
| Brockton | Edgar B Davis | 7/29/11 | | | | | | | | 7/29/11 | | | | | |
| Brockton | Hancock | 7/29/11 | | | | | | | | 7/29/11 | | | | | |
| Brockton | North Junior High | 7/29/11 | | | | | | | | 7/29/11 | | | | | |
| Brockton | Oscar F Raymond | 7/29/11 | | | | | | | | 7/29/11 | | | | | |
| Brockton | West Junior High | 7/29/11 | | | | | | | | 7/29/11 | | | | | |
| Springfield PS | Milton Bradley ES | 8/2/11 | | | | | | | | 8/2/11 | | | | | |
| Nauset | Nauset Regional High | 9/5/11 | | | | | | | | | 9/5/11 | | | | |
| North Middlesex | Ashby Elementary | 9/5/11 | | | | | | | | | 9/5/11 | | | | |
| Peabody | John E Burke School | 9/5/11 | | | | | | | | | 9/5/11 | | | | |
| Weston | Westport High | 9/5/11 | | | | | | | | | 9/5/11 | | | | |
| Weston | Alice A Macomber | 9/6/11 | | | | | | | | | 9/6/11 | | | | |
| Hadley | Hopkins Academy | 9/7/11 | | | | | | | | | 9/7/11 | | | | |
| Marlborough | Marlborough High | 9/7/11 | | | | | | | | | 9/7/11 | | | | |
| Mohawk Trail | Buckland-Shelburne Reg | 9/7/11 | | | | | | | | | 9/7/11 | | | | |
| Mohawk Trail | Colrain Central | 9/7/11 | | | | | | | | | 9/7/11 | | | | |
| Mohawk Trail | Mohawk Trail Reg High | 9/7/11 | | | | | | | | | 9/7/11 | | | | |
| Agawam | Agawam Junior High | 9/7/11 | | | | | | | | | 9/7/11 | | | | |
| North Andover | North Andover Middle School | 9/7/11 | | | | | | | | | 9/7/11 | | | | |
| North Andover | Annie L Sargent School | 9/7/11 | | | | | | | | | 9/7/11 | | | | |
| Pioneer Valley | Northfield ES | 9/8/11 | | | | | | | | | 9/8/11 | | | | |
| Pioneer Valley | Pearl E Rhodes ES | 9/8/11 | | | | | | | | | 9/8/11 | | | | |
| Grafton | Grafton Memorial Senior | 9/10/11 | | | | | | | | | 9/10/11 | | | | |
| Peabody | William A Welch ES | 9/10/11 | | | | | | | | | 9/10/11 | | | | |
| North Middlesex | Spaulding Memorial | 9/11/11 | | | | | | | | | 9/11/11 | | | | |
| Lowell | Lowell HS | 9/14/11 | | | | | | | | | 9/14/11 | | | | |
| Lowell | Moody ES | 9/14/11 | | | | | | | | | 9/14/11 | | | | |
| Lowell | Peter W Reilly School | 9/14/11 | | | | | | | | | 9/14/11 | | | | |
| Lowell | Washington School | 9/14/11 | | | | | | | | | 9/14/11 | | | | |
| Haverhill | Greenleaf | 9/17/11 | | | | | | | | | 9/17/11 | | | | |
| Haverhill | Tilton | 9/17/11 | | | | | | | | | 9/17/11 | | | | |
| Haverhill | Walnut Square | 9/17/11 | | | | | | | | | 9/17/11 | | | | |
| Westfield | Westfield Voc Tech HS | 11/15/11 | | | | | | | | | | | 11/15/11 | | |
| Salem | Saltonstall Elementary School | 11/20/11 | | | | | | | | | | | 11/20/11 | | |
| Salem | Collins MS | 11/20/11 | | | | | | | | | | | 11/20/11 | | |
| Springfield PS | John J Duggan MS | 12/10/11 | | | | | | | | | | | | 12/10/1 | |

| District-MSBA | Project Name | Due Date |
|---|---|---|
| **Window Projects** | | |
| Wilmington | Shawsheen Elementary School | 1/21/11 A |
| Attleboro | Attleboro High School | 2/23/11 A |
| Arlington | Arlington Norcross Stratton | 3/1/11 A |
| Braintree | Archie T Morrison Elementary | 3/10/11 A |
| Braintree | East Middle School | 3/10/11 A |
| Braintree | Highlands Elementary School | 3/10/11 A |
| Braintree | Hollis Elementary School | 3/10/11 A |
| Springfield PS | Washington ES | 4/13/11 A |
| Springfield PS | White Street ES | 4/13/11 A |
| Sudbury | Peter Noyes | 4/14/11 A |
| Fairhaven | Hastings Middle | 4/21/11 A |
| Dudley Charlton Reg | Shepherd Hill Reg High | 4/28/11 A |
| Chelmsford | Chelmsford High | 4/29/11 A |
| Framingham | Mary E Stapleton Elem | 5/4/11 A |
| Springfield PS | Frank H Freedman ES | 5/4/11 A |
| Springfield PS | Warner ES | 5/13/11 A |
| Barnstable | West Barnstable Elem | 5/20/11 A |
| Brookfield | Brookfield Elementary | 5/20/11 A |
| Fitchburg | Reingold Elementary (Phase 2) | 5/26/11 A |
| Fitchburg | South Street Elementary (Phase 2) | 5/26/11 A |
| Fitchburg | Memorial Intermediate (Phase 2) | 5/26/11 A |
| Reading | Birch Meadow | 6/1/11 |
| Dennis Yarmouth | Ezra H Baker Elementary School | 6/4/11 |
| Upper Capecod VT | Upper Cape Cod Voc Tech | 6/4/11 |
| Leverett | Leverett Elementary | 6/7/11 |
| Abington | Woodsdale Elementary School | 6/8/11 |
| Pentucket | Dr Frederick Sweetsir | 6/13/11 |
| Pentucket | Dr John C Page School | 6/13/11 |
| Pentucket | Elmer S Bagnall | 6/13/11 |
| Billerica | Billerica Memorial High School | 6/14/11 |
| Sandwich | Forestdale | 6/16/11 |
| Sandwich | Oak Ridge K-8 | 6/16/11 |
| Rockland | R Stewart Esten ES | 6/20/11 |
| Central Berkshire | Kittredge | 6/23/11 |
| North Brookfield | North Brookfield Elem | 6/29/11 |
| Wachusett | Naquag Elementary | 7/12/11 |
| Wachusett | Paxton Center | 7/12/11 |
| Wachusett | Thomas Prince | 7/12/11 |
| Amherst-Pelham | Amherst Regional MS | 7/14/11 |
| Greenfield | Four Corners | 7/27/11 |
| North Attleboro | Falls | 7/27/11 |
| Brockton | Brockton High | 7/29/11 |
| Brockton | Downey | 7/29/11 |
| Nauset | Nauset Regional High | 9/5/11 |
| North Middlesex | Ashby Elementary | 9/5/11 |
| Peabody | John E Burke School | 9/5/11 |
| Weston | Westport High | 9/5/11 |
| Weston | Westport Middle | 9/5/11 |
| Marlborough | Francis J Kane | 9/7/11 |
| Marlborough | Marlborough High | 9/7/11 |
| Mohawk Trail | Colrain Central | 9/7/11 |
| Mohawk Trail | Mohawk Trail Reg High | 9/7/11 |

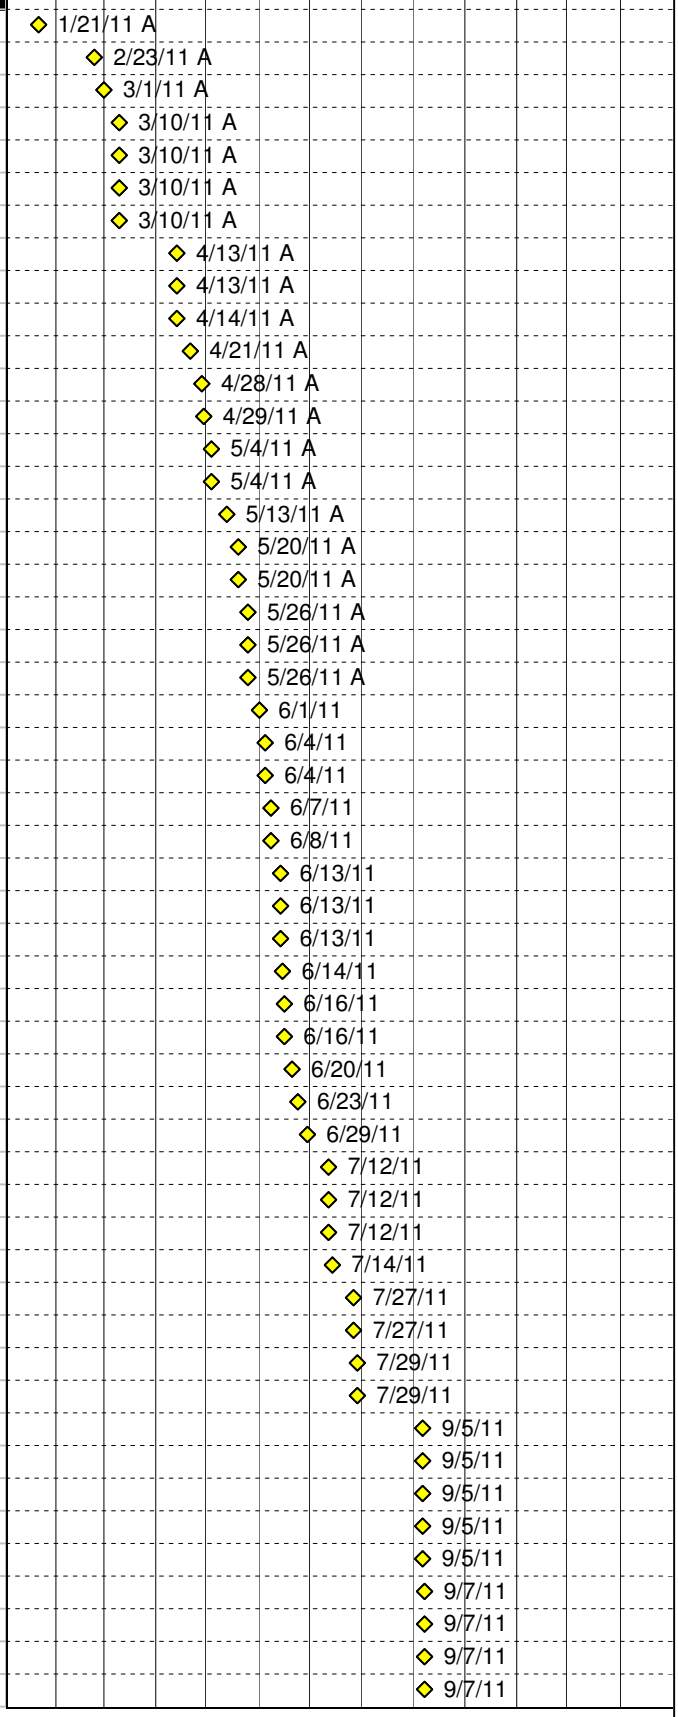



Massachusetts School Building Authority


MSBA-Green Repair Program
Projects with Bids Due Dates

Dates are based on the last update of June 23, 2011.

| District-MSBA | Project Name | Due Date |
|---|---|---|
| Agawam | Agawam Junior High | 9/7/11 |
| Middleborough | Mary K Goode ES | 9/7/11 |
| North Andover | Atkinson School | 9/7/11 |
| West Boylston | Major Edwards ES | 9/7/11 |
| West Boylston | West Boylston Jr-Sr HS | 9/7/11 |
| Pioneer Valley | Northfield ES | 9/8/11 |
| Pioneer Valley | Pearl E Rhodes ES | 9/8/11 |
| Lowell | Moody ES | 9/14/11 |
| Lowell | Peter W Reilly School | 9/14/11 |
| Lowell | Washington School | 9/14/11 |
| Natick | Johnson School | 9/14/11 |
| Haverhill | Caleb Dustin Hunking | 9/17/11 |
| Haverhill | Consentino | 9/17/11 |
| Haverhill | John G Whittier | 9/17/11 |
| Tantasqua | Brookfield Elementary | 10/1/11 |
| Westfield | Westfield Voc Tech HS | 11/15/11 |
| Salem | Collins MS | 11/20/11 |
| Salem | Saltonstall Elementary School | 11/20/11 |
| Springfield PS | John J Duggan MS | 12/10/11 |

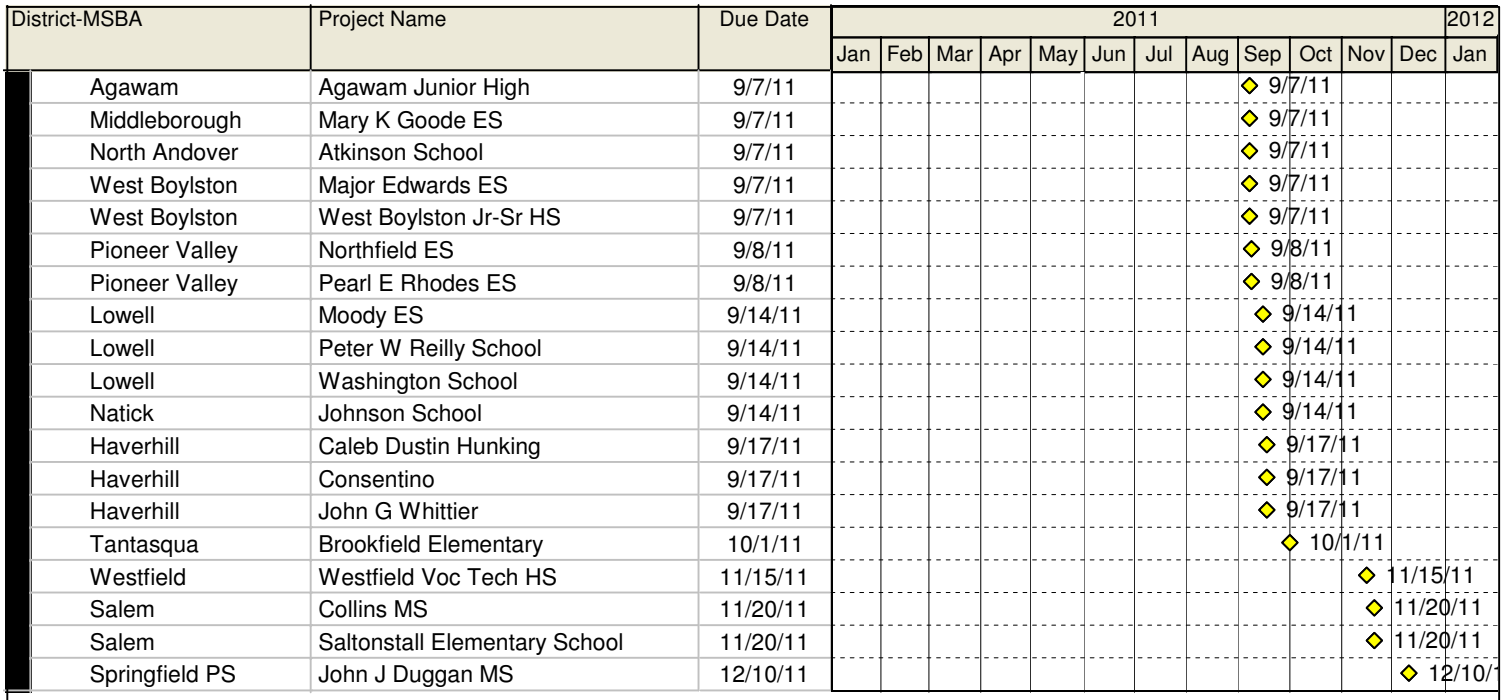

| District-MSBA | Project Name | Due Date |
|---|---|---|
| **Boiler Projects** | | |
| Fitchburg | Reingold Elementary School (Phase 1) | 1/26/11 A |
| Fitchburg | Memorial Middle School (Phase 1) | 1/26/11 A |
| Tri County Regional | Tri County Regional Voc Tech | 2/24/11 A |
| Arlington | Arlington Norcross Stratton | 3/1/11 A |
| Scituate PS | Wampatuck ES | 3/3/11 A |
| Sudbury | Peter Noyes | 4/14/11 A |
| Fitchburg | Fitchburg High (Phase 2) | 5/12/11 A |
| Leicester | Leicester Memorial Elem | 5/18/11 A |
| Newton | Williams | 5/20/11 A |
| Plymouth | West Elementary | 5/31/11 |
| Bellingham | Bellingham Memorial Middle | 6/3/11 |
| Boston | Clarence R Edwards Middle | 6/11/11 |
| Pentucket | Dr Frederick Sweetsir | 6/13/11 |
| Pentucket | Dr John C Page School | 6/13/11 |
| Pentucket | Elmer S Bagnall | 6/13/11 |
| Grafton | South Grafton Elementary | 6/22/11 |
| Boston | Thomas A Edison Jr High | 6/24/11 |
| New Salem Wendell | Swift River | 7/7/11 |
| Wachusett | Naquag Elementary | 7/12/11 |
| Wachusett | Thomas Prince | 7/12/11 |
| Narrangsett | Phillipston Memorial | 7/13/11 |
| Greenfield | Four Corners | 7/27/11 |
| Brockton | East Junior High | 7/29/11 |
| Brockton | North Junior High | 7/29/11 |
| Peabody | John E Burke School | 9/5/11 |
| Cape Cod Regional | Cape Cod Regional Voc Tech | 9/7/11 |
| Marlborough | Marlborough High | 9/7/11 |
| Middleborough | Mary K Goode ES | 9/7/11 |
| Pioneer Valley | Bernardston ES | 9/8/11 |
| Pioneer Valley | Pioneer Valley Regional School | 9/8/11 |
| Pioneer Valley | Pearl E Rhodes ES | 9/8/11 |
| Northborough | Robert E. Melican Middle School | 9/11/11 |
| Lowell | Moody ES | 9/14/11 |
| Lowell | Washington School | 9/14/11 |
| Natick | Johnson School | 9/14/11 |
| Haverhill | Consentino | 9/17/11 |
| Westfield | Highland Elementary School | 11/15/11 |
| Westfield | Paper Mill ES | 11/15/11 |
| Westfield | Westfield HS | 11/15/11 |
| Westfield | Westfield Voc Tech HS | 11/15/11 |
| Westfield | Southampton Road ES | 11/15/11 |
| Salem | Collins MS | 11/20/11 |
| Salem | Saltonstall Elementary School | 11/20/11 |

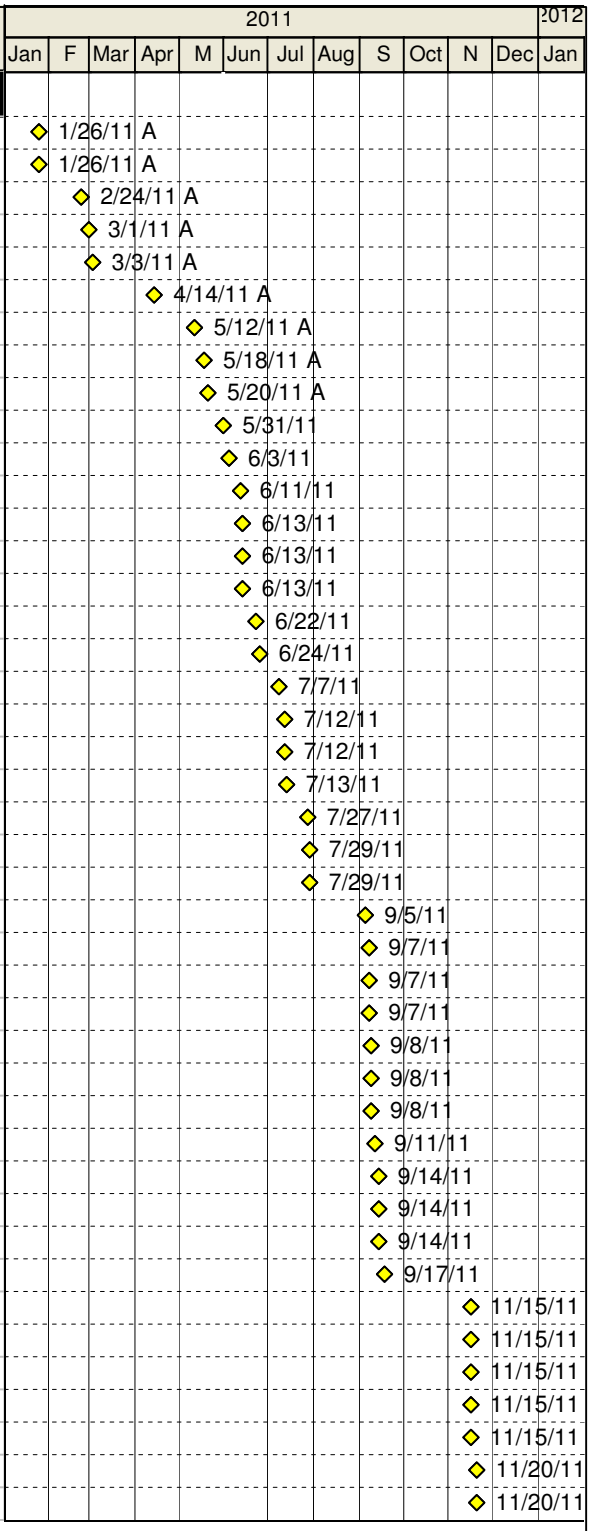


Massachusetts School Building Authority

MSBA-Green Repair Program
Projects with Bids Due Dates

Dates are based on the last update of June 23, 2011.

# Projects in Construction
## MSBA Grant Basis and Maximum Grant Amount

| New Program and Wait List Program Totals | | $1,770,303,461 | 43,687 | | 8,886,088 | | | | | | | | | | | $1,257,334,767 |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|

*Italicized amounts are estimates. Amounts based on bid results have yet to be determines.

| District & School | Grade | Contractor | Total Construction Cost | Projected Enroll | PFA or Bid Data | Proposed Square Footage | Construction Cost per Square Foot | Building Cost | Building Cost per Square Foot | Project Type | Construction Start | Estimated Substantial Completion Date | Physical Progress (%) | Change Orders (%) | Construction Status | Approximate Maximum Grant Amount * |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| **Capital Pipeline Projects in Construction** | | | | | | | | | | | | | | | | |
| **New Program Totals** | | | **$1,365,869,755** | **32,372** | | **6,036,252** | **$226** | | **$168** | | | | | | | **$879,762,538** |
| Berlin-Boylston<br>Tahanto Reg MS/HS | 6-12 | CTA | $31,287,000 | 560 | Bid | 126,100 | $248 | *24,629,999* | $195 | Design/Bid/ Build | 10-May-11 | 31-Dec-12 | 7% | 0.00% | Site preparation and clearing activities have been initiated including site survey, placement of hay bales and silt fencing. Demolition of an existing structure at the building footprint has also started. | *$19,311,013* |
| Beverly<br>Beverly HS | 9-12 | CTA | $67,563,917 | 1,200 | PFA | 247,275 | $273 | $51,251,689 | $207 | Design/Bid/ Build | 6-Jan-09 | 18-Nov-10 | 97% | 1.20% | The main building was completed November 2010. Phase 2, Existing Building Demolition is now completed. Site Work to be completed by December 2011. | $46,826,551 |
| Billerica<br>Parker ES | K-5 | CTA | $22,842,500 | 500 | Bid | 89,093 | $256 | $17,913,441 | $201 | Design/Bid/ Build | 15-Sep-10 | 25-May-12 | 30% | 0.00% | Construction of building envelope has commenced. Substantial Date shown is for Phase I building construction. Phase II is scheduled to be complete on November 26, 2012. | $15,851,020 |
| Brookline<br>Runkle ES | PK-8 | G&R Construction | $20,715,300 | 560 | Bid | 104,400 | $198 | $17,668,440 | $169 | Design/Bid/ Build | 10-Nov-10 | 10-Jul-12 | 17% | 0.20% | Foundations and footing are complete. Lead paint abatement and MEP rough-in have started. Steel erection is ongoing. | $11,135,430 |
| Burlington<br>Memorial ES | K-5 | CTA | $16,389,000 | 500 | Bid | 79,185 | $207 | $13,092,323 | $165 | Design/Bid/ Build | 4-Mar-10 | 15-Jul-11 | 78% | 3.00% | Ongoing work includes final cleaning, start-up and functional testing of several HVAC elements, electrical equipment and commissioning of operational elements within the building. Final inspections have been initiated with punch list work ongoing. | *$11,019,590* |
| Carlisle<br>Carlisle K-8 | K-8 | H.V. Collins Co. Inc | $15,277,344 | 700 | Bid | 140,312 | $109 | $11,342,751 | $81 | Design/Bid/ Build | 9-Feb-11 | 20-Apr-12 | 20% | 0.15% | 90% of the footing, walls, grade beams and piers have been placed. Site utilities are underway. Steel erection to commence shortly. | *$6,620,942* |
| Danvers<br>Danvers HS | 9-12 | Bacon Construction | $51,098,700 | 1,000 | Bid | 246,251 | $208 | $42,760,342 | $174 | Design/Bid/ Build | Oct-10 | 1-Jul-13 | 21% | 0.00% | Work is progressing in the academic areas, field house, auditorium and on site. Ongoing work includes steel erection, concrete placement, masonry work, installation of light gauge metal framing, door frame installations, roofing, MEP rough-ins and under-slab utility installations. | *$37,218,572* |
| Easthampton<br>Easthampton HS | 9-12 | Fontaine Brothers | $33,463,815 | 510 | PFA | 109,572 | $305 | $24,463,200 | $223 | Design/Bid/ Build | 16-May-11 | 25-Oct-13 | 3% | 0.00% | Installation of soil consolidation system, wick drain system, and grouted uplift columns continues. Preparations being made for placement of preload settlement fill and monitoring system. | *$25,543,860* |
| Foxborough<br>Foxborough HS | 9-12 | CTA | $11,469,333 | 885 | Bid | 218,500 | $52 | $8,845,000 | $40 | Design/Bid/ Build | 25-Jan-10 | 17-Aug-11 | 83% | 5.92% | HVAC systems and controls, fire alarm, sound and clock system work continues as well as door and hardware installation. Roofing and window installation continuing. Commissioning is ongoing. | $7,226,509 |
| Hampden-Wilbraham<br>Minnechaug HS | 9-12 | Fontaine Brothers | $48,597,500 | 1,225 | Bid | 231,467 | $210 | $37,499,962 | $162 | Design/Bid/ Build | 22-Jul-10 | 28-Jun-12 | 33% | 0.80% | Placement of concrete slabs are underway. Steel erection continues. Exterior masonry and roofing are now underway. Plumbing rough-ins have begun. Site work continues. | $34,863,838 |
| Hanover<br>Hanover HS | 9-12 | Callahan | $37,306,499 | 800 | Bid | 157,000 | $238 | $28,060,313 | $179 | Design/Bid/ Build | 28-Sep-09 | 1-Jun-11 | 95% | 3.80% | HVAC unit startup, testing, and commissioning continues. FF&E installation is well underway. Punchlist for Phase I underway. Project is 90% complete with the building 94% complete. | *$22,263,877* |
| Marshfield<br>Governor Winslow ES | K-5 | Enterprise Equipment Co. | $1,868,688 | 494 | Bid | 65,790 | $28 | $1,455,103 | $22 | Design/Bid/ Build | Apr-11 | 1-Dec-11 | 20% | 0.00% | Electrical and plumbing work continues in the new boiler room. Work above ceiling in cafeteria underway. | $1,112,880 |
| Middleton<br>Howe-Manning ES | 4-6 | CTA | $18,210,000 | 553 | Bid | 83,934 | $217 | $14,529,671 | $173 | Design/Bid/ Build | 06-Apr-10 | 30-Jul-11 | 94% | 4.33% | Finish paint work, ceramic tile, casework, and landscaping is ongoing. Mechanical balancing continues. Plumbing and roofing at punchlist stage. FF&E and Technology equipment scheduled for July 11, 2011 delivery. Abatement at old Howe-Manning ES started. | *$12,311,976* |
| Nashoba<br>Pompositticut ES | K-2 | P.J. Stella Construction | $23,640,900 | 600 | Bid | 98,030 | $241 | $18,431,325 | $188 | Design/Bid/ Build | 15-Jun-10 | 17-Apr-12 | 30% | 0.90% | Light gauge metal framing, drywall & MEP rough-in continue. The roofing and brick veneer also underway. Rooftop units are installed and windows have arrived on site. | *$15,042,648* |
| Natick<br>Natick HS | 9-12 | Brait Builders Corp. | $60,270,000 | 1,300 | Bid | 254,225 | $237 | $53,213,182 | $209 | Design/Bid/ Build | 13-Sep-10 | 15-Jun-13 | 27% | 2.20% | Exterior CMU is underway. Windows are on site. Rough plumbing and electrical are underway. Site work continues. Over the summer school vacation period, a section of the existing building needs to be demolished to install a section of the new school. | *$38,209,033* |
| Norfolk<br>Freeman-Centennial ES | 3-6 | Fontaine Brothers | $25,341,543 | 585 | Bid | 96,410 | $263 | $20,023,000 | $208 | Design/Bid/ Build | 9-Nov-10 | 18-Jun-12 | 13% | 0.00% | Steel erection is 75% complete. Exterior CMU is underway. Site work continues. | *$15,861,760* |
| Norwood<br>Norwood HS | 9-12 | Agostini | $52,627,980 | 1,100 | Bid | 227,374 | $231 | $42,573,646 | $187 | Design/Bid/ Build | 19-May-09 | 13-May-11 | 92% | 1.10% | Substantial Completion was in May. Phase II occurs during the summer months to remove a portion of the existing building that is in the path of the new main entry drive and installs the new main entry drive. Phase III starts on September 1, 2011 and includes the completion of the demolition of the existing building and completes the front fields. | $38,154,487 |
| Plymouth<br>Plymouth HS | 9-12 | J&J Contractors | $64,407,000 | 1,350 | Bid | 267,357 | $241 | $51,579,703 | $193 | Design/Bid/ Build | 3-May-10 | 15-May-12 | 42% | 0.40% | Vapor Barrier installed on north and east elevations. Slab-on-grade prepped for gym. Mechanical boiler and electrical switch gear installations are underway. | *$41,810,972* |
| Shawsheen<br>Shawsheen Voc Tech HS | 9-12 | Colantonio | $3,329,510 | 1,300 | Bid | 15,115 | $220 | $2,670,380 | $177 | Design/Bid/ Build | 3-Jan-11 | 15-Aug-11 | 79% | 0.00% | Interior work progressing includes gypsum drywall installation, primer and first coat of paint, acoustical ceiling grid installations, ceramic tile installation, window storefront installation, as well as progression of all mechanical, electrical and plumbing trades. Underway site work operations include the installation of the storm water treatment structures and associated storm water piping. | $2,497,790 |
| Sturbridge<br>Burgess ES | K-6 | Fontaine Brothers | $22,931,000 | 860 | Bid | 131,630 | $174 | $17,591,000 | $134 | Design/Bid/ Build | 10-Aug-10 | 1-Oct-12 | 55% | 1.00% | The exterior of the new addition is nearly complete. Finishes are progressing. Stairs have been installed with railing work remaining. MEP rough-in is nearly complete. The new transformer has been installed and permanent power is expected soon. | $16,808,626 |
| Tewksbury<br>Tewksbury HS | 9-12 | CTA/Methuen Construction Co. | $50,800,000 | 1,100 | Bid | 218,781 | $232 | $40,159,651 | $184 | Design/Bid/ Build | 15-Oct-10 | 3-Aug-12 | 35% | 1.20% | Exterior framing, sheathing and AVB are underway. MEP's rough-ins are well underway. Site utilities are continuing. | *$36,622,570* |
| Adams-Cheshire<br>Hoosac Valley MSHS | 6-12 | Gilbane | $30,075,221 | 805 | PFA | 173,999 | $173 | *15,483,125* | $89 | CM-R | 17-May-11 | 31-Jul-12 | 1% | 0.00% | Site preparation and clearing has started including establishing egress for the construction site. | $28,243,131 |
| Belmont<br>Roger E Wellington ES | K-5 | Skanska | $27,912,000 | 575 | Bid | 88,203 | $316 | $19,931,588 | $226 | CM-R | 1-Mar-10 | 24-Aug-11 | 85% | 3.00% | All building façade brickwork and window installations are complete. MEP is complete in SW wing and is ongoing in the NE wing. Drywall and taping are complete in the SW and NW wings. Drywall is 80% complete in the core, gym, Cafetorium and Kitchen. | *$12,245,940* |
| Burlington<br>Marshall Simonds MS | 6-8 | CTA | $24,683,286 | 880 | Bid | 151,000 | $163 | $18,923,176 | $125 | CM-R | 15-Apr-11 | 17-May-13 | 27% | 0.00% | Extensive site work and foundation construction for the proposed addition, including spread footings, frost walls and elevator pit walls is ongoing. Work on the renovation includes relocation of furnishings and asbestos abatement and preparation for floor replacement. Structural steel has been delivered to the site. | *$17,143,488* |
| Dedham<br>Avery ES | K-5 | Consigli | $18,174,209 | 310 | Bid | 62,887 | $289 | $13,524,768 | $215 | CM-R | 15-Oct-10 | 1-Jan-12 | 41% | 2.20% | The building envelope is enclosed. MEP rough-in is progressing on all floors. Masonry work continues with added manpower on the brick veneer. Window installations have begun. Roofing is also progressing. | $11,086,460 |
| Grafton<br>Memorial Sr HS | 9-12 | Dimeo | $54,059,520 | 900 | Bid | 186,351 | $290 | $41,783,110 | $224 | CM-R | 18-Aug-10 | 17-Jul-12 | 24% | 0.00% | Exterior sheathing, CMU and AVB are underway. Site work continues | *$36,163,052* |
| Leominster<br>Leominster SHS | 9-12 | S.O.M. | $32,709,051 | 1,825 | PFA | 295,859 | $111 | $22,855,000 | $77 | CM-R | 1-Jul-11 | 30-Aug-13 | 3% | 0.00% | Site utilities with the exception of the primary electric service have been completed by the modular contractor. Modular units began arriving to site on June 22, 2011. 12 out of 28 units are in place with the balance expected to be on site by the week of 7/25. | *$31,038,794* |
| Longmeadow<br>Longmeadow HS | 9-12 | Gilbane | $63,773,971 | 1,000 | PFA | 184,365 | $346 | $38,354,307 | $208 | CM-R | Nov-10 | 23-Feb-13 | 5% | 0.00% | Installation of footings and foundation walls have begun. The installation of the remaining temporary sanitary piping has been completed. The backfill and compaction and build-up of Area C to 2' below finish floor was completed. | $34,004,658 |
| Needham<br>Newman ES | K-5 | Consigli | $18,451,284 | 680 | Bid | 119,264 | $155 | $12,806,351 | $107 | CM-R | 16-Jun-10 | 27-Aug-12 | 5% | 0.00% | Site mobilization underway. Installation of the modulars underway. | *$8,598,929* |
| Rochester<br>Memorial ES | K-6 | Gilbane | $20,568,696 | 635 | PFA | 107,183 | $192 | $14,165,117 | $132 | CM-R | 19-Apr-10 | 1-Sep-11 | 88% | 3.27% | Structural reinforcement of the 1950's wing is complete. Phase 6 the last phase of the project is well underway. | $14,438,137 |
| Rockland<br>John Rogers MS/ HS | 5-12 | Agostini | $64,461,963 | 1,525 | Bid | 268,106 | $240 | $45,821,680 | $171 | CM-R | 15-Jan-10 | 3-Aug-12 | 17% | 0.00% | Interior CMU underway. Electrical underground work completed in the MS. Primary and secondary service complete and National Grid inspected. Site utilities are installed and backfill completed. Steel detailing remains to be performed. | *$53,356,682* |
| Sharon<br>Sharon MS | 6-8 | Consigli | $34,676,018 | 845 | Bid | 171,806 | $202 | $24,732,123 | $144 | CM-R | 1-Apr-10 | 23-Jan-12 | 58% | 1.00% | Work in the new addition continues. Finishes on the second floor are almost complete. Window abatement and replacement resumed after the school year ended. Kitchen and café underground work was completed and new slabs were placed. | *$21,952,095* |
| Shrewsbury<br>Sherwood MS | 9-12 | Gilbane | $33,986,285 | 900 | Bid | 129,378 | $263 | $23,133,512 | $179 | CM-R | 7-Mar-11 | 1-Sep-13 | 7% | 0.00% | Foundation is 65% complete. Site drainage and utility installations are in process. Structural steel is engineered and 90% fabricated. Site construction to enable phasing including permanent access road and temporary parking lot is complete. | $24,362,063 |

## Projects in Construction
## MSBA Grant Basis and Maximum Grant Amount

| District & School | Grade | Contractor | Total Construction Cost | Projected Enroll | PFA or Bid Data | Proposed Square Footage | Construction Cost per Square Foot | Building Cost | Building Cost per Square Foot | Project Type | Construction Start | Estimated Substantial Completion Date | Physical Progress (%) | Change Orders (%) | Construction Status | Approximate Maximum Grant Amount * |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| Southbridge<br>Southbridge HS | 6-12 | Consigli | $57,397,363 | 1,050 | Bid | 199,740 | $287 | $41,487,200 | $208 | CM-R | 30-Nov-10 | 1-Jun-12 | 23% | 0.00% | Slab on deck was completed for areas A and B, 2nd floor. The metal roof and floor decking is 95% complete in Area A. The metal roof and floor decking is 90% complete in Area E. Site drainage utilities are in progress and are approximately 70% complete. | *$51,542,762* |
| Uxbridge<br>High School | 9-12 | Shawmut Design | $35,265,819 | 600 | Bid | 123,000 | $287 | $25,169,257 | $205 | CM-R | 28-Feb-11 | 20-Jun-12 | 16% | 0.00% | Waterproofing and damproofing of the foundation is complete and backfilling is progressing. Structural steel is 20% complete. Interior underground electrical and plumbing is 90% complete. Site utility installation is nearly complete. Roughing of masonry walls is 90% complete. | *$21,973,620* |
| Wayland<br>Wayland HS | 9-12 | Shawmut Design | $54,230,819 | 900 | Bid | 171,000 | $317 | $37,343,299 | $218 | CM-R | 28-Jun-10 | 1-Dec-11 | 63% | 0.50% | Bldg A- MEP work and drywall installation is nearly complete. Drywall taping is ongoing. Bldg B- Curtain wall installation complete. Drywall taping, painting and acoustical ceiling grid installations are nearly complete. Ceramic tile and acoustical ceiling tile installations ar ongoing. | $24,051,231 |
| Wellesley<br>Wellesley HS | 9-12 | Turner | $82,942,222 | 1,500 | Bid | 280,000 | $296 | $55,814,300 | $199 | CM-R | 24-Aug-09 | 5-Feb-12 | 60% | 1.00% | Work continues on exterior curtain walls and metal panels, interior masonry, roof top equipment and screens, interior M.E.P. rough-in, partitioning work and finishes. | $40,117,222 |
| Woburn<br>Goodyear ES | K-5 | Gilbane | $17,994,825 | 320 | Bid | 67,278 | $267 | $13,989,980 | $208 | CM-R | 9-Mar-10 | 29-Jul-11 | 94% | 1.10% | Site work continues with sidewalks, paving, landscaping, and turf fields. Completed work includes masonry site walls, curtain walls & storefront installations, roof edge fascia flashing, tile work, and HVAC finish work. Nearing completion are drywall, elevator installation, wall panel millwork, fire protection systems, and electrical wiring finish work. Boiler equipment has been started and HVAC testing is underway. | $12,441,343 |
| **Wait List Projects in Construction** | | | | | | | | | | | | | | | | |
| **Wait List Program Totals** | | | **$404,433,706** | **11,315** | | **2,849,836** | | | | | | | | | | **$377,572,229** |
| Cambridge<br>Rindge & Latin HS | 9-12 | W.T. Rich, Inc. | $89,957,728 | 1,529 | PFA | 470,700 | $191 | TBD | TBD | Design/Bid/ Build | May-07 | Aug-11 | 90% | 8% | Phase 2B is currently underway which includes installation of windows, MEP upgrades and the conclusion of exterior restoration. The project is scheduled to be completed in September 2011. | $28,026,977 |
| Haverhill<br>Haverhill HS | 9-12 | CTA | $21,878,214 | 1,864 | PFA | 677,333 | $32 | TBD | TBD | Design/Bid/ Build | Apr-04 | Aug-11 | 97% | 7% | Finishes package being installed. Project completion expected in September of 2011. | $23,436,595 |
| Holyoke<br>Holyoke HS | 9-12 | WJ Mountford | $16,943,500 | 1,252 | PFA | 242,738 | $71 | TBD | TBD | Design/Bid/ Build | Mar-10 | Aug-11 | 99% | 20% | Contractor and District finishing punchlist items. Delays were encountered due to late material delivery. | $14,368,320 |
| Taunton<br>Parker MS | 5-8 | Bacon-Agostini | $88,467,267 | 2,350 | PFA | 539,224 | $164 | TBD | TBD | Design/Bid/ Build | 01-Jul-08 | 29-Aug-11 | 96% | 5% | Substantial Completion scheduled for August 30, 2011 | $93,590,656 |
| Malden<br>Malden HS | 9-12 | Gilbane | $50,002,293 | 1,720 | PFA | 365,271 | $137 | TBD | TBD | CM-R | 20-Apr-09 | 06-Jan-12 | 85% | 10% | Substantial Completion is scheduled for October 27, 2011. | $69,364,963 |
| Springfield<br>Putnam Voc Tech HS | 9-12 | Consigli | $86,039,066 | 1,400 | Bid | 315,000 | $273 | $62,949,742 | $200 | CM-R | 18-May-10 | 20-Jul-12 | 55% | 0% | Curtain wall and interior masonry wall installations continue. Window and MEP installations are ongoing. | $102,872,837 |
| Worcester<br>North HS | 9-12 | Gilbane | $51,145,638 | 1,200 | PFA | 239,570 | $213 | $40,860,983 | $171 | CM-R | 24-Sep-08 | Jun-11 | 90% | 4% | The architect & OPM have issued the punchlist for the entire building. Design for Phase 3&4 of the project which include abatement & demo of the existing school, construction of athletic fields and parking lots are underway. | $45,911,881 |
