
Project Overview Report
July 30, 2014

A total of 321 projects that have received invitations from the Board of Directors ("Board") to collaborate with the MSBA are currently in the MSBA's Eligibility Period and Capital Pipeline. The following summary chart provides the number of projects in the Eligibility Period and each phase of the Capital Pipeline:

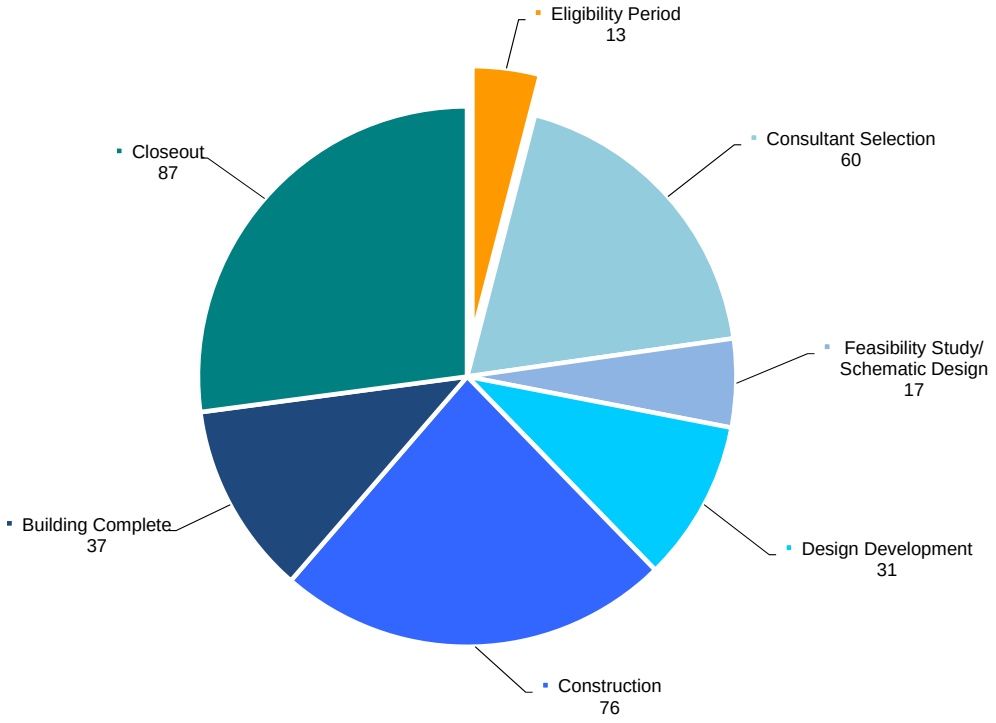

Statement of Interest ("SOI")

2014 SOI Process

The Fiscal Year 2014 SOI filing period opened on **January 10, 2014.** The deadline to file SOIs for consideration in the Accelerated Repair Program ("ARP") was Friday, February 14, 2014. The MSBA received 119 SOIs, submitted by 60 districts for consideration into the ARP. Invites into the ARP were concluded at the June 4, 2014 Board of Directors Meeting and 37 districts, representing 51 projects, were invited into the Program.

The SOI closing date for districts submitting for consideration in the Core Program, which is primarily for projects beyond the scope of Accelerated Repair, including extensive repairs, renovations, addition/renovations, and new school construction, was **April 11, 2014**. The MSBA received 108 Core Program SOIs. The review process for these SOIs will last throughout the summer. The MSBA anticipates invites into the Eligibility Period at the Fall 2014/Winter 2015 Board of Directors Meetings.

Eligibility Period

There are 13 districts in the Eligibility Period. Of the 13, six districts have already secured funding. The remaining seven districts have yet to confirm their date for action.

An agreed-upon enrollment is a key pre-requisite for the MSBA to commence a Feasibility Study with a district. To begin the enrollment projection process, a district must file enrollment information utilizing the MSBA's online enrollment projection tool. Since the last report, two districts have completed the enrollment process.

Based upon the schedules anticipated by the districts for completion of the Eligibility Period requirements, staff anticipates recommending the 13 districts in the Eligibility Period for an Invitation to Feasibility Study at upcoming Board meetings.

Capital Pipeline

Consultant Selection

After the district has completed all Eligibility Period requirements and has received a Board Invitation to Feasibility Study, the district procures an Owner's Project Manager ("OPM"). There are currently six districts in the Capital Pipeline that need to procure an OPM.

After a district has selected and executed a contract with an OPM, it selects a Designer utilizing either a local designer selection process for projects under $5 million or the MSBA's Designer Selection Panel ("DSP") for projects over $5 million. There are currently three districts in the Capital Pipeline that are in the process of procuring a Designer.

Feasibility Study

Once a district has procured an OPM and Designer and a Feasibility Study Agreement has been executed, the district and its consultants must complete two Feasibility Study submittals, the Preliminary Design Program and the Preferred Schematic Report, prior to Board consideration to proceed into Schematic Design. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that four districts will present their preferred schematic designs to the Board at the upcoming September and November Board meetings.

Prior to consideration by the Board for Project Scope and Budget authorization, a district must submit a Schematic Design to the MSBA for review. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that four districts will appear before the Board for Project Scope and Budget Agreement authorization at the upcoming September and November Board meetings.

Commissioning

Since the last report, the MSBA has assigned Commissioning Consultants to an additional five projects presented in the table below. To date, the MSBA has executed 279 Commissioning Consultant contracts, totaling $20.8 million. To date, 116 contracts have been completed.

District	School	Estimated Const. Cost (million)	Commissioning Consultant	Contract Amount
Northborough	Lincoln Street Elementary School	$25.40	Fitzemeyer & Tocci Associates	$66,152
Wareham	Wareham High School (2013 ARP: Roofs)	$2.26	Russo Barr Associates, Inc.	$31,965
Georgetown	Georgetown Middle/High School Renovation	$5.90	WSP Flack + Kurtz	$32,000
Haverhill	Caleb Dustin Hunking Middle School	$50.00	Strategic Building Solutions, LLC	$110,998
Westford	Norman Day Elementary School (2013 ARP: Windows)	$1.61	CBI Consulting Inc.	$27,000
	Total	**$85.17 M**	**Total**	**$268,115**

The table below represents the status of commissioning assignments sorted by the fiscal year in which the commissioning work orders were issued.

Fiscal Year	No. Work Orders Issued	Value of Work Orders Issued	Total Invoiced	Percent Complete
FY10	31	$4,231,376	$4,227,043.00	99.90%
FY11	95	$6,328,287	$5,480,185.75	86.60%
FY12	52	$4,459,061	$3,043,303.00	68.25%
FY13	55	$3,386,847	$1,488,218.61	43.94%
FY14	46	$2,608,272	$256,086.94	9.82%

Design Development

Once a district has secured local funding and has entered into a Project Funding Agreement with the MSBA, it enters into the Design Development phase. Currently, there are 31 projects in the Design Development phase with a total estimated construction cost of approximately $595.28 million: 19 Accelerated Repair projects and 12 Core Program projects. The 12 Core Program projects in Design Development have a total estimated construction cost of approximately $565.39 million and are listed below.

Elementary School Districts	Middle and Middle/High School Districts	High School Districts
Athol-Royalston Regional	Georgetown	Boston
Gloucester	Haverhill	Lunenburg
Milford		North Middlesex Regional
Newton		Winchester
Northborough		Winthrop

Construction

When a district issues a Notice to Proceed, the project is advanced to the Construction phase. Currently, there are 76 projects in the Construction phase with a total estimated construction cost of $1.707 billion: one Green Repair project, 33 Accelerated Repair projects, two Science Lab Initiative projects, and 40 Core Program projects. The 40 Core Program projects have a total estimated construction cost of $1.619 billion and are listed below. This does not include the 37 projects that have reached substantial completion and are currently in the Building Complete phase.

Elementary School Districts	Middle and Middle/High School Districts	High School Districts
Georgetown	Auburn	**Addition/Renovation**
Newburyport *(Bresnahan)*	Chicopee	Assabet Valley Regional Technical
Revere	Greenfield	Ayer Shirley Regional
Springfield *(Brookings)*	Lynn	Dracut
South Hadley	Newburyport *(Nock)*	Greater Lawrence Regional Voc/Tech
Southwick-Tolland-Granville Regional *(Woodland)*	North Adams	Greater Lowell Regional Voc/Tech
Webster	Oxford	Greater New Bedford Voc/Tech
Westfield	Peabody	Norfolk County Agricultural
Weston	Southwick-Tolland-Granville Regional *(Powder Mill)*	North Reading
Williamsburg	Stoneham	Southern Worcester Regional Voc/Tech
	Sutton	Southwick-Tolland-Granville Regional
	Wachusett Regional	**New**
	Wakefield	Concord-Carlisle Regional
		Essex/North Shore Regional Voc/Tech
		West Bridgewater
		Wilmington
		Model
		Franklin
		Marshfield
		Monomoy Regional

Summary of Bid Data

These numbers are based on preliminary information received from the district and are subject to further review and calculation.

Year	Number of Projects	Design Basis for Enrollment	Project Budget	Construction Budget
2014	17	14,345	$935.0 M	$731.9 M
2015	4	2,830	$203.0 M	$154.8 M
Grand Total	**21**	**17,175**	**$1.14 B**	**$886.7 M**

Core Program – Total Project Budget Update

Upon receiving the Board's approval of the Project Scope and Budget, the MSBA and participating districts enter into a Project Funding Agreement that establishes the Total Project Budget and the Estimated Maximum Total Facilities Grant for an approved project. Of the grants authorized by the Board, nine projects have increased their Total Project Budgets due to acceptance of construction bids higher than the project estimates, and one project has increased its Total Project Budget due to an increase in its site acquisition cost budget. In no event has the increase in budget resulted in an increase to the Estimated Maximum Total Facilities Grant as authorized by the Board. Please note that staff reported on these budget increases for the seven projects shaded below at previous Board meetings.

District	School Name	Scope	Project Funding Agreement		PFA Bid Amendment		Reason for Increase to Total Project Budget
			Total Project Budget	Total Maximum Facilities Grant	Total Project Budget	Total Maximum Facilities Grant	
Core Program							
Andover	Bancroft Elementary School	New	$44,659,837	$16,773,753	$50,374,837	TBD*	The District has appropriated additional funds to cover the costs associated with increased construction costs and additional contingencies for litigation/settlement costs and other ineligible costs.
Essex North Shore Agricultural & Technical High School	Essex North Shore Agricultural & Technical School District	New	$125,000,000	$77,500,000	$133,770,000	$77,500,000	The Board was informed at the March 30, 2011 meeting that the Total Project Budget had increased due to additional ineligible scope that would be funded by DCAM.
Essex North Shore Agricultural & Technical High School	Essex North Shore Agricultural & Technical School District	New	$125,000,000	$77,500,000	$134,501,368	$77,500,000	The District has appropriated additional funds to cover the costs associated with increased construction costs for horse tack barn renovations.
Lexington	Estabrook Elementary School	New	$40,792,248	$12,250,739	$43,392,248	$12,148,491	The District has executed a GMP that exceeds the Construction Budget of the PFA.The District has appropriated additional funds to cover the costs associated with increased construction costs and additional contingencies.
North Reading	North Reading Middle /High School	Add/ Reno	$107,727,074	$49,323,123	$123,227,074	$49,323,123	This is a CMR project. The estimated, reconciled construction costs tracked over budget at DD ($9,746,655 over), 60% ($4,655,965 over), and 90% ($15,136,846 over). A Town override vote in March 2013 obtained an additional $15,500,000 in local funding to proceed.
Revere	Staff Sergeant James J. Hill Elementary School *(currently the McKinley ES)*	New	$45,402,396	$29,551,048	TBD*	$29,551,048	At Project Scope and Budget, the Total Project Budget was approved at $44,382,396. The City of Revere has increased the land acquisition budget. Therefore, the projected total project budget at PFA has increased to $45,402,396. Note that the MSBA grant has not changed since the Project Scope and Budget Agreement.
Somerville	East Somerville Community School	Add/ Reno	$33,185,258	$15,237,996	$38,006,621	$15,237,996	At the March 28, 2012 Board Meeting, the Board approved an amendment to the PFA and a $6.25M District loan.
Uxbridge	Uxbridge High School	New	$43,000,000	$22,362,328	$44,986,479	$22,362,328	The District has appropriated additional funds to cover the costs associated with the construction of athletic fields originally included in the PFA but which were not included in the bid as the District's construction contract would have exceeded the budget.

*PFA Bid Amendment has not been developed to calculate a revised total facilities grant amount. The Total Maximum Facilities Grant will not exceed the Board authorized amount in the PFA but, upon review, may decrease.

Status of Accelerated Repair Program


Currently there are a total of 70 districts, representing 132 projects, either active or completed in the Accelerated Repair Program.

2014 Accelerated Repair Program

Following a review of 2014 Accelerated Repair Statements of Interest, 37 districts, representing 51 projects, were invited into the Program at the June 2014 Board Meeting. The districts are completing initial Program documents and securing schematic design funding in preparation for consultant assignments.


2013 Accelerated Repair Program

Currently 26 districts, representing 47 projects, have been approved for Project Funding Agreements. Two districts authorized Declarations of Removal of a Statement of Interest and removed their potential projects from the Program. The 2013 Accelerated Repair Program is proceeding with 25 districts, representing 45 projects authorized for $94,650,790 in Total Project Budgets, and a maximum of $54,662,550 in MSBA Total Facilities Grant Funding.

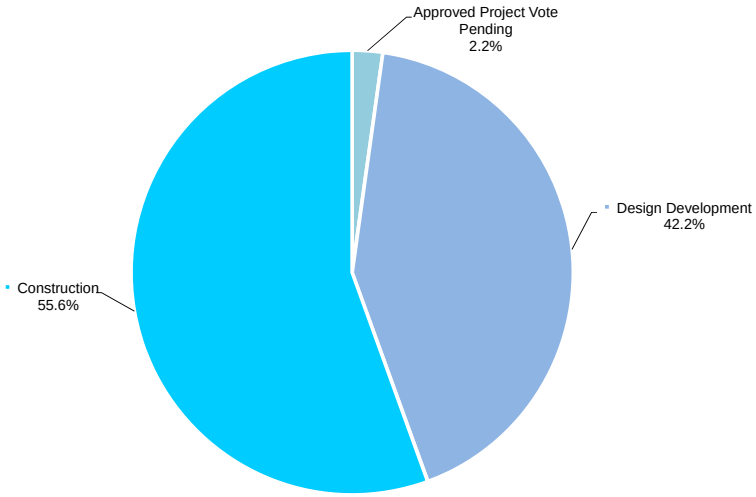

2012 Accelerated Repair Program

All 24 districts, representing 36 projects, approved in 2012 are under contract with consultants and have been authorized to enter into a Project Funding Agreement, totaling $63,009,653 in Total Project Costs and a maximum of $38,267,952 in MSBA Total Facilities Grant funding. Of the 36 projects, 27 completed construction in 2013, and nine are scheduled to complete construction in 2014. The chart below represents the progress of the 36 projects approved in 2012.

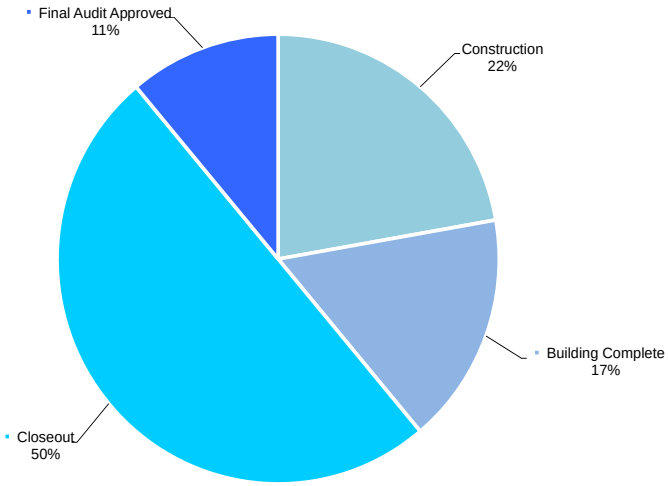

Status of Green Repair Program

The Green Repair Program has resulted in PFA authorizations totaling $366,647,226 in Total Project Costs and $222,885,258 in MSBA grants. One project, Douglas Intermediate School, remains in construction with substantial completion scheduled for July 2014.

2012 Accelerated Repair Projects – Construction Estimate vs. 2013 Bid Amount

- Out of 36 projects, 36 bids have been received.
- Of the 36 projects, 34 bids have been reported.
- Of the 34 projects, 29 bids came within the estimated budget.

				Total	$49,232,661	$37,117,085	$12,115,576	-	$7,745,967
District	School	Scope	Project Type	Bid Date	Construction Estimate **	Bid Amount **	Variance from Construction Estimate	Reimbursement Rate	Potential Grant Variance *
Weymouth	William Seach PS	Boiler	DBB	Dec-12	$425,213	$459,104	-$33,891	54.16%	$0
Groton-Dunstable RSD	Gronton-Dunstable MS	Roof	DBB	Feb-13	$1,316,890	$942,000	$374,890	45.74%	$171,475
Hamilton-Wenham	Cutler ES	Roof	DBB	Feb-13	$547,326	$444,150	$103,176	43.42%	$44,799
North Brookfield	North Brookfield ES	Windows	DBB	Feb-13	$274,254	$199,400	$74,854	62.67%	$46,911
Shawsheen Valley Voc/Tech.	Shawsheen Valley VTHS	Boiler	DBB	Mar-13	$805,423	$535,000	$270,423	52.06%	$140,782
Sudbury	Gen. John Nixon ES	Roof	DBB	Mar-13	$621,554	$542,775	$78,779	36.89%	$29,062
Easton	Easton Jr. HS	Roof	DBB	Mar-13	$1,850,830	$1,889,000	-$38,170	50.16%	$0
Norton	Solmonese ES	Roof	DBB	Mar-13	$1,166,044	$986,000	$180,044	55.63%	$100,158
Attleborough	Irvin Studley ES	Roof	DBB	Mar-13	$773,363	$489,000	$284,363	57.74%	$164,191
Lynn	Breed MS	Windows	DBB	Mar-13	$1,796,674	$2,167,300	-$370,626	80.00%	$0
Lynn	Lynn Voc. Tech	Roof	DBB	Mar-13	$4,173,000	$3,097,000	$1,076,000	80.00%	$860,800
Worcester	Chandler Magnet	Windows	DBB	Mar-13	$3,723,463	$3,142,320	$581,143	80.00%	$464,914
Worcester	Jacob Hiatt Magnet	Boiler	DBB	Mar-13	$298,877	$321,703	-$22,826	80.00%	$0
Worcester	James Caradonio Center	Windows / Boiler	DBB	Mar-13	$1,021,820	$1,007,132	$14,688	80.00%	$11,750
Worcester	Lake View School	Windows	DBB	Mar-13	$1,127,970	$789,398	$338,572	80.00%	$270,858
Worcester	May Street School	Windows	DBB	Mar-13	$1,655,289	$1,548,167	$107,122	80.00%	$85,698
Gardner	Gardner MS	Boiler	DBB	Apr-13	$438,439	$396,100	$42,339	78.95%	$33,427
North Attleborough	Roosevelt Ave. ES	Windows	DBB	Apr-13	$768,000	$656,483	$111,517	52.06%	$58,056
Quabaog RSD	Warren ES	Boiler	DBB	Apr-13	$207,000	$182,444	$24,556	68.34%	$16,782
Quabbin	Ruggles Lane ES	Roof / Windows	DBB	Apr-13	$2,588,409	$2,287,836	$300,573	57.74%	$173,551
Leominster	Fall Brook ES	Boiler	DBB	Apr-13	$949,550	$684,000	$265,550	73.38%	$194,861
Leominster	Southeast ES	Roof / Boiler	DBB	Apr-13	$3,146,097	$1,948,000	$1,198,097	73.38%	$879,164
Westfield	Munger Hill ES	Roof	DBB	Apr-13	$1,170,735	$593,499	$577,236	59.84%	$345,418
Westfield	Paper Mill ES	Roof	DBB	Apr-13	$1,170,735	$562,525	$608,210	59.84%	$363,953
Southampton	William Norris ES	Roof	DBB	May-13	$1,504,147	$922,000	$582,147	55.00%	$320,181
Taunton	Galligan School	Roof	DBB	May-13	$543,570	$486,600	$56,970	73.95%	$42,129
Wayland	Wayland MS	Roof	DBB	May-13	$2,445,767	$1,965,800	$479,967	36.89%	$177,060
Blackstone-Millville RSD	Maloney ES	Roof	DBB	Sep-13	$1,405,656	$702,000	$703,656	57.74%	$406,291
Blackstone-Millville RSD	J.F.Kennedy ES	Roof	DBB	Sep-13	$2,315,707	$1,093,000	$1,222,707	57.74%	$705,991
Wilmington	North IS	Windows	DBB	Nov-13	$1,206,312	$1,217,649	-$11,337	49.94%	$0
Canton	Peter Hanson School	Windows	DBB	Dec-13	$734,414	$660,200	$74,214	45.11%	$33,478
Canton	William Galvin MS	Windows	DBB	Dec-13	$1,014,385	$856,600	$157,785	45.11%	$71,177
Bridgewater-Raynham RSD	Bridgewater MS	Roof	DBB	Mar-14	$2,788,716	$1,482,000	$1,306,716	55.63%	$726,926
Blackstone-Millville RSD	Blackstone-Melville RHS	Roof	DBB	Apr-14	$3,257,032	$1,860,900	$1,396,132	57.74%	$806,127

*These numbers are based on preliminary information received from the district and are subject to further review and calculation.
**The construction estimate and bid amount do not include pre-construction services and alternatives.

2013 Accelerated Repair Projects – Construction Estimate vs. 2014 Bid Amount

- Out of 45 projects, 32 bids have been received.
- Of the 32 projects, 18 bids have been reported.
- Of the 18 projects, 18 bids came within the estimated budget.

				Total	$30,250,908	$17,914,090	$12,336,818	-	$7,919,188
District	School	Scope	Project Type	Bid Date	Construction Estimate **	Bid Amount **	Variance from Construction	Reimbursement Rate	Potential Grant Variance *
Springfield	High School / Science Tech	Roof	DBB	Mar-14	$2,856,796	$2,145,000	$711,796	80.00%	$569,437
Springfield	Margaret C. Ells	Roof	DBB	Mar-14	$1,333,530	$911,000	$422,530	80.00%	$338,024
Springfield	South End MS	Roof	DBB	Mar-14	$564,152	$292,000	$272,152	80.00%	$217,722
Springfield	Springfield Public Day HS	Roof	DBB	Mar-14	$676,093	$575,000	$101,093	80.00%	$80,874
Hopedale	Memorial ES	Roof	DBB	Apr-14	$406,219	$258,000	$148,219	52.89%	$78,393
Hamilton-Wenham RSD	Bessie Buker ES	Boiler	DBB	Apr-14	$610,530	$419,910	$190,620	44.05%	$83,968
South Middlesex RVTSD	Joseph P. Keefe RTHS	Roof	DBB	Apr-14	$5,130,738	$3,218,000	$1,912,738	69.89%	$1,336,813
Randolph	Randolph Community MS	Boiler	DBB	Apr-14	$384,601	$259,590	$125,011	74.74%	$93,433
Randolph	Randloph HS	Roof	DBB	Apr-14	$1,206,462	$739,000	$467,462	74.74%	$349,381
Westhampton	Westhampton ES	Roof / Windows	DBB	Apr-14	$817,213	$275,131	$542,082	50.58%	$274,185
Nashoba Valley RVTSD	Nashoba Valley THS	Roof	DBB	May-14	$2,421,424	$1,265,000	$1,156,424	52.26%	$604,347
Easton	Moreau Hall ES	Roof	DBB	May-14	$690,007	$658,000	$32,007	50.79%	$16,256
Ashland	Ashland MS	Roof	DBB	May-14	$2,900,968	$1,584,000	$1,316,968	50.16%	$660,591
Ashland	Henry E. Warren ES	Roof	DBB	May-14	$2,074,007	$977,000	$1,097,007	50.16%	$550,259
Medford	Medford HS	Boiler	DBB	May-14	$1,894,490	$1,481,000	$413,490	55.58%	$229,818
Walpole	Fisher	Roof	DBB	May-14	$1,554,441	$998,459	$555,982	48.68%	$270,652
Springfield	Chestnut Accel. MS	Roof	DBB	Jun-14	$3,720,576	$1,360,000	$2,360,576	80.00%	$1,888,461
Stoughton	West ES	Roof	DBB	Jun-14	$1,008,661	$498,000	$510,661	54.16%	$276,574

*These numbers are based on preliminary information received from the district and are subject to further review and calculation.
**The construction estimate and bid amount do not include pre-construction services and alternatives.

Accelerated Repair Projects – Schedule Extension Update

The MSBA has granted districts conditional extensions to their Project Funding Agreements pending compliance with the following stipulations:

- The district needed to submit a detailed, revised construction timeline showing how the work will be completed at each school; and
- Any costs that may result from the district's requested extension of the construction schedule will be the sole responsibility of the district and are categorically ineligible for reimbursement by the MSBA.

Schedule delays for these districts can be attributed to local funding issues, lead time for windows, and construction delays on site. In no event have the extended schedules resulted in an increase to the Estimated Maximum Total Facilities Grant as authorized by the Board.

Nine of the 36 2012 Accelerated Repair Projects have not met their anticipated construction completion dates. Each of these projects has a revised construction schedule and is scheduled to be completed by the beginning of the 2014-2015 school year.

District	School	Scope	Original Construction Completion Date	Updated Construction Completion Date	Reason for Schedule Extension
Blackstone-Millville RSD	Blackstone-Millville RHS	Roof	26-Dec-13	1-Sep-14	The District fell behind schedule due to local funding issues.
Bridgewater-Raynham RSD	Bridgewater MS	Roof	1-Sep-13	1-Sep-14	The District fell behind schedule as a result of local issues funding issues and incorporation of new OPM to project team.
Bridgewater-Raynham RSD	Laliberte ES	Roof	1-Sep-13	1-Sep-14	The District fell behind schedule as a result of local issues funding issues and incorporation of new OPM to project team.
Bridgewater-Raynham RSD	L.B. Merrill ES	Roof	1-Sep-13	1-Sep-14	The District fell behind schedule as a result of local issues funding issues and incorporation of new OPM to project team.
North Attleborough	Roosevelt Ave. ES	Windows	27-Sep-13	31-Mar-14	Construction fell behind schedule due to material delivery delays. Corrective work was completed to ensure windows pass commissioning tests.
Taunton	Galligan School	Roof	13-Nov-13	31-Dec-13	District issued a Change Order for installation of tapered insulation and membrane overlay to prevent ponding around the chimney area.
Worcester	Lake View School	Windows/Doors	13-Sep-13	14-Feb-14	Construction fell behind schedule due to material delivery delays.
Worcester	May Street School	Windows/Doors	14-Sep-13	15-Mar-14	Construction fell behind schedule due to material delivery delays.
Worcester	New Citizens Center School	Windows/Doors & Boilers	13-Sep-14	14-Feb-13	Construction fell behind schedule due to material delivery delays. Boiler scope completed per baseline schedule.

Four of the 45 2013 Accelerated Repair Projects will not meet their anticipated construction completion dates in 2014. The projects have revised construction schedules and are scheduled to be completed by the beginning of the 2015-2016 school year.

District	School	Scope	Original Construction Completion Date	Updated Construction Completion Date	Reason for Schedule Extension
Hamilton-Wenham RSD	Winthrop ES	Windows	15-Sep-14	13-Aug-15	The District and its consultants have determined that the estimated lead time for windows requires construction to be scheduled for 2015.
Quincy	Merrymount ES	Windows	22-Sep-14	28-Aug-15	The District and its consultants have elected to rebid the project and complete construction in 2015.
Quincy	North Quincy High	Windows	22-Sep-14	28-Aug-15	The District and its consultants have elected to rebid the project and complete construction in 2015.
Quincy	Wollaston ES	Windows	22-Sep-14	28-Aug-15	The District and its consultants have elected to rebid the project and complete construction in 2015.

2013-2014 Eligibility Period Status

July 9, 2014

13 Projects in Eligibility Period

Task Remaining | Partial Task Completed | Invite / Completion Date | Completed Task

Board Meeting 2 / 8 | 2 / 27 | 3 / 9 | 4 / 8 | 7 / 3 | 6 / 6 | 11 / 4


ICC | SBC | Maint Doc | Enroll Certification | Local Authorization / FAS

District	Oct 2013	Nov 2013	Dec 2013	Jan 2014	Feb 2014	Mar 2014	April 2014	May 2014	June 2014	July 2014	Aug 2014	Sept 2014	Oct 2014	Nov 2014	Dec 2014	Jan 2015	Feb 2015	Mar 2015
Mount Greylock RSD **Mount Greylock RHS**	10/02/13 10/16/13	11/15/13	12/16/13	01/14/14			04/14/14			07/14/14								
	ICC (30 days)	SBC (60 days)	Online Enrollment Projection Info	Maintenance Docs / Enroll Certification (180 days)						Local Authorization / FSA (270 days)								
Amherst **Wildwood Elementary School**	11/20/13 12/04/13	01/03/14	02/03/14	03/04/14					06/02/14						09/01/14			
	ICC (30 days)	SBC (60 days)	Online Enrollment Projection Info	Maintenance Docs					Enroll Certification (180 days)		Local Authorization		FSA (270 days)					
Needham **Hillside Elementary School**	ICC (30 days)	SBC (60 days)	Online Enrollment Projection Info	Maintenance Docs					Enroll Certification (180 days)		Local Authorization		FSA (270 days)					
Carver **Carver Elementary School**	01/29/14 02/12/14	03/04/14	04/03/14	05/05/14						08/01/14					10/30/14			
	ICC (30 days)	SBC (60 days)	Online Enrollment Projection Info / Ed Profile Questionaire (90 days)	Maintenance Docs / Enroll Certification (180 days)						Local Authorization			FSA (270 days)					
Hanover **Sylvester Elementary School**	ICC (30 days)	SBC (60 days)	Online Enrollment Projection Info / Ed Profile Questionaire (90 days)	Maintenance Docs					Enroll Certification (180 days)		Local Authorization / FSA (270 days)							
Provincetown **Provincetown Schools**	ICC (30 days)	SBC (60 days)	Online Enrollment Projection Info / Ed Profile Questionaire (90 days)	Maintenance Docs / Enroll Certification (180 days)						Local Authorization			FSA (270 days)					
Quincy **Reay E. Sterling Middle School**	ICC (30 days)	SBC (60 days)	Online Enrollment Projection Info / Ed Profile Questionaire (90 days)	Maintenance Docs					Enroll Certification (180 days)		Local Authorization / FSA (270 days)							
Somerville **Somerville High School**	ICC (30 days)	SBC (60 days)	Online Enrollment Projection Info / Ed Profile Questionaire (90 days)	Maintenance Docs					Enroll Certification (180 days)		Local Authorization / FSA (270 days)							
Stoughton **Stoughton High School**	ICC (30 days)	SBC (60 days)	Online Enrollment Projection Info / Ed Profile Questionaire (90 days)	Maintenance Docs					Enroll Certification (180 days)		Local Authorization		FSA (270 days)					
Orange **Dexter Park School**	03/26/14 04/09/14	05/09/14	06/09/14	07/08/14						10/06/14					01/05/15			
	ICC (30 days)	SBC (60 days)	Online Enrollment Projection Info / Ed Profile Questionaire (90 days)	Maintenance Docs / Enroll Certification (180 days)						Local Authorization / FSA (270 days)								
Bourne **James F. Peebles Elementary School**	06/04/14 06/18/14	07/18/14	08/18/14	09/16/14						12/15/14					03/16/15			
	ICC (30 days)	SBC (60 days)	Online Enrollment Projection Info / Ed Profile Questionaire (90 days)	Maintenance Docs / Enroll Certification (180 days)						Local Authorization / FSA (270 days)								
Ipswich **Winthrop Elementary School**	ICC (30 days)	SBC (60 days)	Online Enrollment Projection Info / Ed Profile Questionaire (90 days)	Maintenance Docs / Enroll Certification (180 days)						Local Authorization / FSA (270 days)								
Millis **Clyde F. Brown Elementary School**	ICC (30 days)	SBC (60 days)	Online Enrollment Projection Info / Ed Profile Questionaire (90 days)	Maintenance Docs / Enroll Certification (180 days)						Local Authorization / FSA (270 days)								
District	Oct 2013	Nov 2013	Dec 2013	Jan 2014	Feb 2014	Mar 2014	April 2014	May 2014	June 2014	July 2014	Aug 2014	Sept 2014	Oct 2014	Nov 2014	Dec 2014	Jan 2015	Feb 2015	Mar 2015

PROJECT STATUS

Total Number of Projects: 308

Wednesday, July 09, 2014

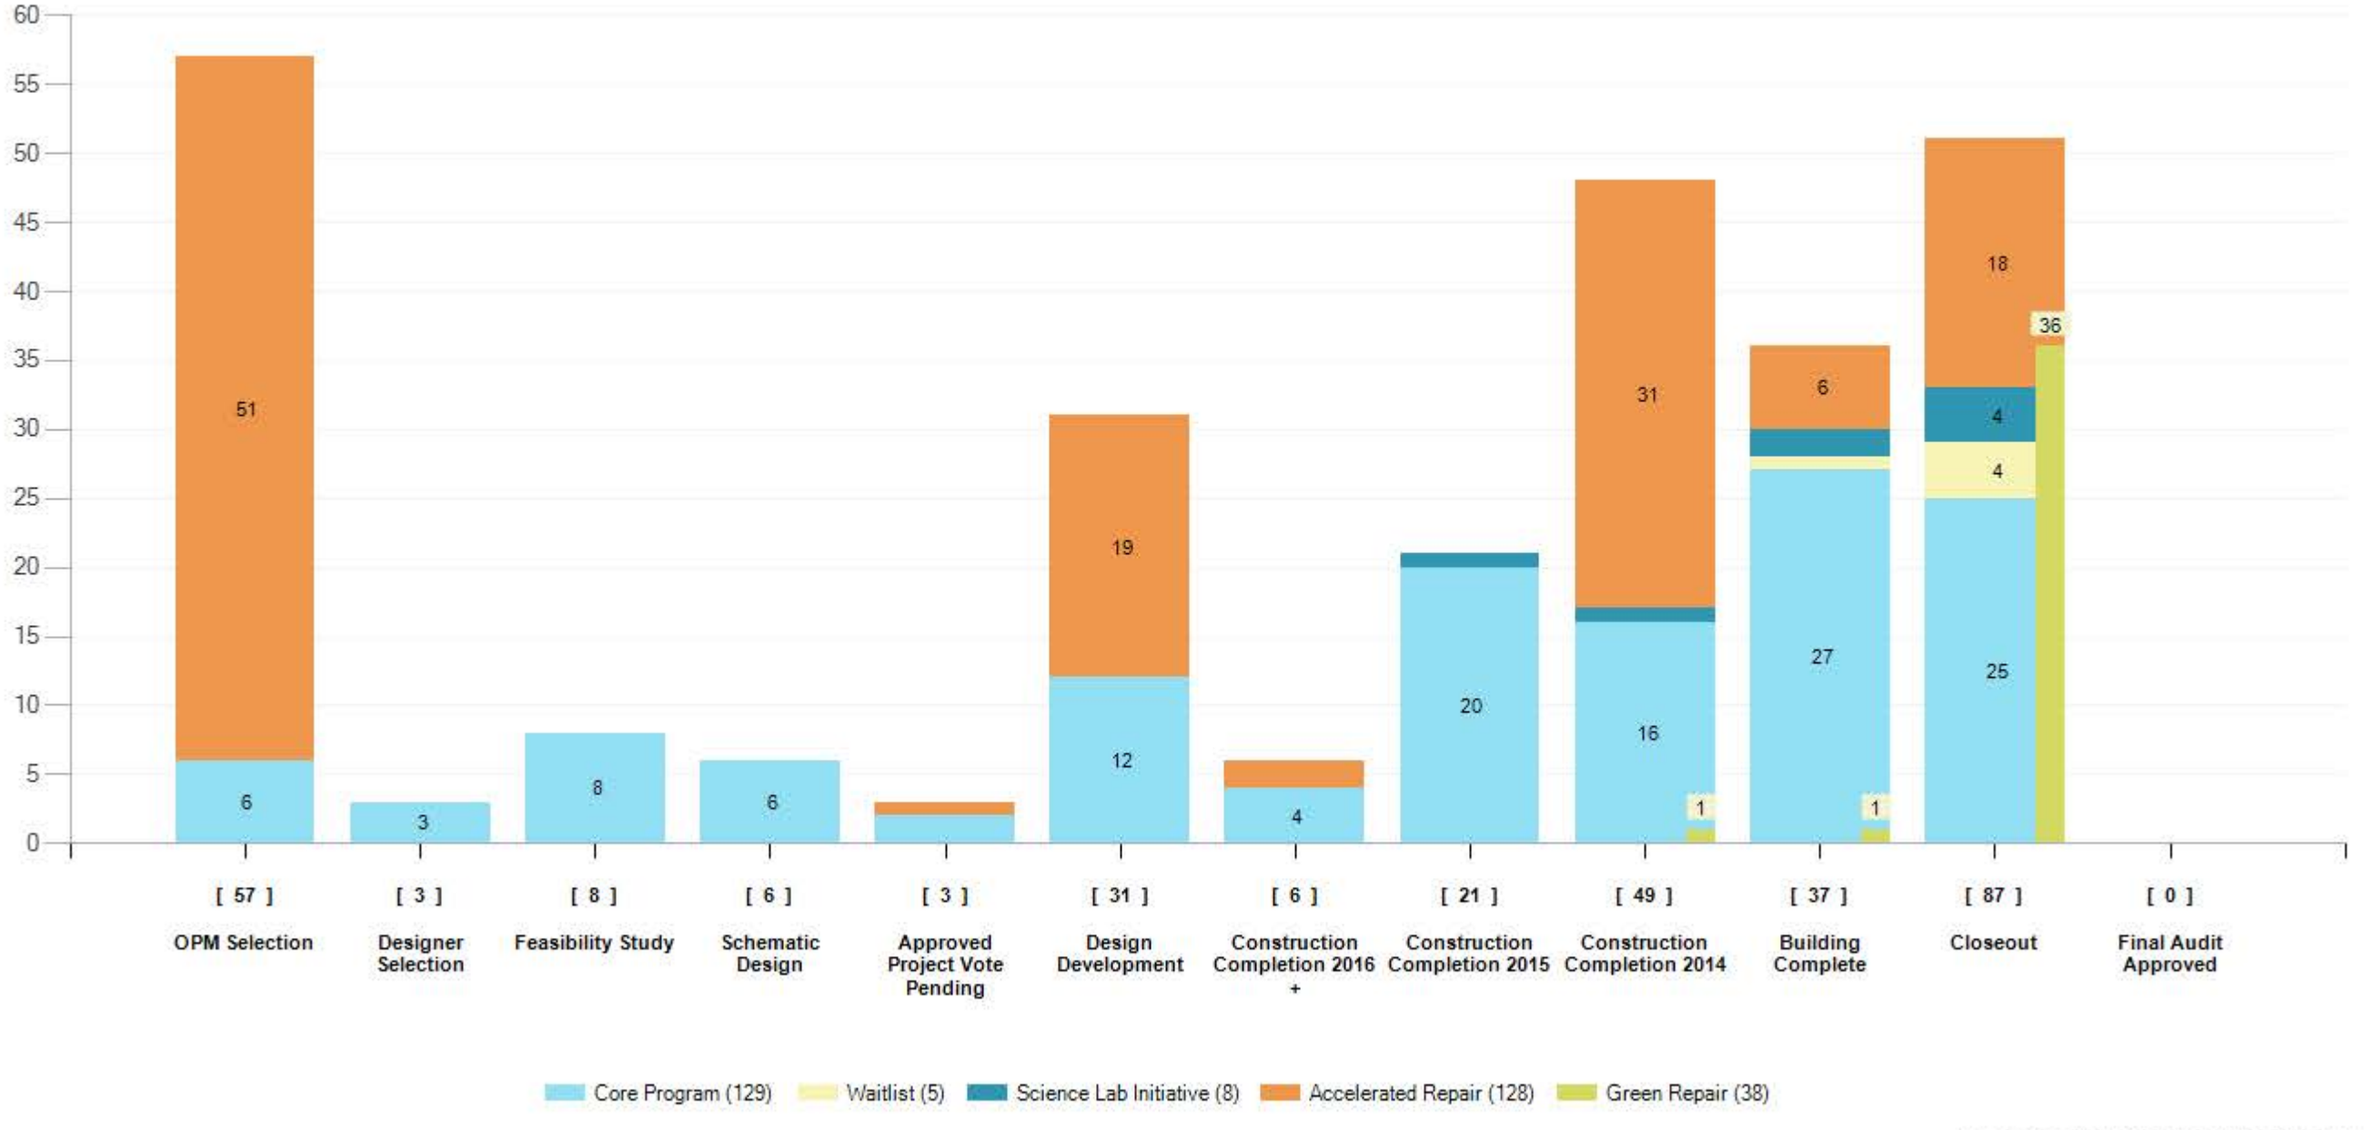

Number less than 3 is not shown in the chart

Date of Report: 7/9/2014

Total Projects: 321

MSBA ID	District	School	Project Phase	Project Type	Project Scope	Procurement Type	OPM	Designer	CM\GC	Commissioning Consultant
200800010405	Abington	Frolio Middle School	Schematic Design	Core Program	New Construction	DBB	Knight, Bagge & Anderson Inc.	Ai3 Architects LLC	-	-
200806030505	Adams-Cheshire	Hoosac Valley High School	Closeout	Core Program	Addition / Renovation	CM@R	URS Corporation	Tessier Associates, Inc.	Gilbane Building Company	Strategic Building Solutions, LLC
201300080050	Amherst	Wildwood Elementary	Eligibility Period	Core Program			-	-	-	-
200800090003	Andover	Bancroft Elementary School	Building Complete	Core Program	New Construction	CM@R	Dore & Whittier Management Partners, Inc.	Symmes Maini & McKee Associates, Inc.	Skanska USA Building, Inc.	Sebesta Blomberg & Associates, Inc.
200900100050	Arlington	Thompson Elementary School	Building Complete	Core Program	New Construction	DBB	PMA Construction Services	HMFH Architects, Inc.	G & R Construction, Inc.	Consulting Engineering Services, LLC
200806100025	Ashburnham-Westminster	John R. Briggs Elementary School	Building Complete	Core Program	New Construction	CM@R	STV Incorporated	Lamoureux Pagano & Associates, Inc.	Consigli Construction Company, Inc.	Foreman Building Commissioning, LP
201300140405	Ashland	Ashland Middle	Construction	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	Raymond Design Associates, Inc.	Gibson Roofs, Inc.	Gale Associates, Inc.
201300140010	Ashland	Henry E Warren Elem	Construction	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	Raymond Design Associates, Inc.	-	Gale Associates, Inc.
200908010605	Assabet Valley	Assabet Valley Regional Technical High School	Construction	Core Program	Repair	DBB	Strategic Building Solutions, LLC	Design Partnership of Cambridge, Inc.	CTA Construction Co., Inc.	Symmes, Maini & McKee Associates
200906150020	Athol-Royalston	Riverbend School	Design Development	Core Program	New Construction	DBB	Symmes Maini & McKee Associates	Mount Vernon Group Architects, Inc.	-	Strategic Building Solutions, LLC
200800170305	Auburn	Auburn Middle	Construction	Core Program	New Construction	CM@R	Skanska USA Building, Inc	Lamoureux Pagano & Associates, Inc.	Fontaine Brothers, Inc.	WSP Flack + Kurtz
201400170305	Auburn	Auburn Middle	OPM Selection	Accelerated Repair	Roof, Boiler		-	-	-	-
201400170010	Auburn	Bryn Mawr	OPM Selection	Accelerated Repair	Roof		-	-	-	-
200806160505	Ayer-Shirley	Ayer-Shirley Regional Middle/High School	Construction	Core Program	Addition / Renovation	CM@R	Dore and Whittier Architects, Inc.	Symmes Maini & McKee Associates, Inc.	Consigli Construction Company, Inc.	WSP Flack + Kurtz
201300200010	Barnstable	Barnstable United Elementary School	Construction	Accelerated Repair	Roof	DBB	exPERTcon, Inc.	Gale Associates, Inc.	-	Russo Barr Associates, Inc.
201100200005G	Barnstable	West Barnstable Elem	Closeout	Green Repair	Windows / Doors	DBB	PMA Construction Services	-	Paul J. Rogan Co., Inc.	CBI Consulting Inc.
201400250020	Bellingham	South Elem	OPM Selection	Accelerated Repair	Roof		-	-	-	-
200800260035	Belmont	Roger Wellington Elementary School	Closeout	Core Program	New Construction	CM@R	PMA Construction Services	Jonathan Levi Architects LLC	Skanska USA Building, Inc.	Strategic Building Solutions, LLC
201006180505	Berkshire Hills	Monument Mountain Regional High School	Approved Project Vote Pending	Core Program	Addition / Renovation	DBB	Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.	-	-
200806200505	Berlin-Boylston	Tahanto Regional High School	Building Complete	Core Program	New Construction	DBB	PMA Construction Services	HMFH Architects, Inc.	CTA Construction Co., Inc.	Strategic Building Solutions, LLC
200800300505	Beverly	Beverly High School	Closeout	Core Program	Addition / Renovation	DBB	HEERY	-	CTA Ventures	-
201300300305	Beverly	Briscoe Middle	Designer Selection	Core Program			HEERY	-	-	-
201300310505	Billerica	Billerica Memorial High School	OPM Selection	Core Program			-	-	-	-
200800310015	Billerica	Parker Elementary School	Closeout	Core Program	New Construction	DBB	Joslin, Lesser + Associates Inc.	Symmes Maini & McKee Associates, Inc.	CTA Construction Co., Inc.	Sebesta Blomberg & Associates, Inc.
201208050605	Blackstone Valley Reg	Blackstone Valley	Closeout	Science Lab Initiative	Addition / Renovation	DBB	Compass Project Management, Inc.	Flansburgh Associates, Inc.	Pergola Construction Co., Inc.	Horizon Engineering Associates, LLP
201206220015	Blackstone-Millville	A F Maloney	Closeout	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	DiMarinisi & Wolfe Architects Urban Designers	Greenwood Industries, Inc.	Gale Associates, Inc.
201206220505	Blackstone-Millville	Blackstone Millville RHS	Construction	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	DiMarinisi & Wolfe Architects Urban Designers	-	Gale Associates, Inc.
201206220008	Blackstone-Millville	John F Kennedy Elem	Closeout	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	DiMarinisi & Wolfe Architects Urban Designers	Greenwood Industries, Inc.	Gale Associates, Inc.
201306220010	Blackstone-Millville	Millville Elem	Design Development	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	CBI Consulting Inc.	-	Simpson Gumpertz & Heger Inc.

201000350074	Boston	Henry Dearborn Middle School	Design Development	Core Program	New Construction		Daedalus Projects Inc	Jonathan Levi Architects LLC	-	-
201000350565	Boston	Quincy Upper School	Schematic Design	Core Program	New Construction		Skanska USA Building, Inc	HMFH Architects, Inc.	-	-
201400360010	Bourne	James F Peebles Elem	Eligibility Period	Core Program			-	-	-	-
201300400305	Braintree	East Middle School	OPM Selection	Core Program			-	-	-	-
201206250320	Bridgewater-Raynham	Bridgewater Middle School	Construction	Accelerated Repair	Roof	DBB	Vertex Construction Services	-	-	CBI Consulting Inc.
201206250050	Bridgewater-Raynham	Laliberte Elementary School	Construction	Accelerated Repair	Roof	DBB	Vertex Construction Services	Raymond Design Associates, Inc.	-	CBI Consulting Inc.
201206250020	Bridgewater-Raynham	Merrill Elementary School	Construction	Accelerated Repair	Roof	DBB	Vertex Construction Services	Raymond Design Associates, Inc.	-	CBI Consulting Inc.
201400440421	Brockton	Ashfield Middle School	OPM Selection	Accelerated Repair	Roof, Boiler		-	-	-	-
201400440080	Brockton	Barrett Russell School	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201400440010	Brockton	Brookfield	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201400440035	Brockton	Gilmore	OPM Selection	Accelerated Repair	Roof, Boiler		-	-	-	-
201100460015	Brookline	Edward Devotion	Feasibility Study	Core Program			-	HMFH Architects, Inc.	-	-
201000480303	Burlington	Marshall Simonds Middle School	Closeout	Core Program	Addition / Renovation	CM@R	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	CTA Construction Co., Inc.	RDK Engineers
201200500012	Canton	Lt Peter M Hansen	Construction	Accelerated Repair	Windows / Doors	DBB	Vertex Construction Services	CSS Architects Incorporated	-	Simpson Gumpertz & Heger Inc.
201200500305	Canton	Wm H Galvin Middle	Construction	Accelerated Repair	Windows / Doors	DBB	Vertex Construction Services	CSS Architects Incorporated	-	Simpson Gumpertz & Heger Inc.
200800510025	Carlisle	Carlisle School	Closeout	Core Program	Addition / Renovation	DBB	Daedalus Projects Inc	HMFH Architects, Inc.	H.V. Collins Co., Inc.	Horizon Engineering Associates, LLP
201300520015	Carver	Carver Elementary School	Eligibility Period	Core Program			-	-	-	-
200800570050	Chelsea	Clark Avenue School	Schematic Design	Core Program	New Construction		Pinck & Co., Inc.	HMFH Architects, Inc.	-	-
200900610021	Chicopee	Chicopee Academy	Construction	Core Program	Addition / Renovation	DBB	Arcadis U.S., Inc.	Caolo & Bieniek Associates, Inc.	-	Symmes, Maini & McKee Associates
200906400505	Concord-Carlisle	Concord-Carlisle Regional High School	Construction	Core Program	New Construction	CM@R	KV Associates, Inc.	OMR Architects, Inc.	Turner Construction Company	Strategic Building Solutions, LLC
200800710505	Danvers	Danvers High School	Building Complete	Core Program	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	DiNisco Design Partnership, Limited	Bacon Construction Co, Inc.	Turner Facilities Management Solutions
201400720030	Dartmouth	George H Potter	OPM Selection	Accelerated Repair	Roof		-	-	-	-
200800730010	Dedham	Avery Elementary School	Closeout	Core Program	New Construction	CM@R	Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.	Consigli Construction Company, Inc.	WSP Flack + Kurtz
201200730005	Dedham	Early Childhood Center	Designer Selection	Core Program			Construction Monitoring Services, Inc.	-	-	-
201306500005	Dighton-Rehoboth	Dighton Elementary	Design Development	Accelerated Repair	Roof	DBB	-	-	-	Gale Associates, Inc.
201306500305	Dighton-Rehoboth	Dighton Middle School	Design Development	Accelerated Repair	Roof	DBB	-	-	-	Gale Associates, Inc.
201306500310	Dighton-Rehoboth	Dorothy L Beckwith	Design Development	Accelerated Repair	Roof	DBB	-	-	-	Gale Associates, Inc.
200800770010	Douglas	Douglas Elementary	Building Complete	Core Program	New Construction - Model School	DBB	HEERY	DiNisco Design Partnership, Limited	CTA Construction Co., Inc.	Consulting Engineering Services, LLC
200800770100G	Douglas	Douglas Intermediate Elementary School	Construction	Green Repair	Roof, Windows / Doors, Boiler	DBB	HEERY	DiNisco Design Partnership, Limited	CTA Construction Co., Inc.	Consulting Engineering Services, LLC
200800790505	Dracut	Dracut Senior High School	Construction	Core Program	Addition / Renovation	DBB	Hill International Company	Mount Vernon Group Architects, Inc.	CTA Construction Co., Inc.	RDK Engineers
201000820505	Duxbury	Duxbury High School	Building Complete	Core Program	New Construction - Model School	CM@R	KV Associates, Inc.	Mount Vernon Group Architects, Inc.	Dimeo Construction Company	WSP Flack + Kurtz
200900830505	East Bridgewater	East Bridgewater High School	Building Complete	Core Program	New Construction - Model School	DBB	Hill International Company	Ai3 Architects LLC	Fontaine Brothers, Inc.	Foreman Building Commissioning, LP
200800860505	Easthampton	Easthampton High School	Building Complete	Core Program	New Construction	DBB	Strategic Building Solutions, LLC	Caolo & Bieniek Associates, Inc.	Fontaine Brothers, Inc.	Consulting Engineering Services, LLC
201200880405	Easton	Easton Junior High	Closeout	Accelerated Repair	Roof	DBB	PMA Construction Services	Russo Barr Associates, Inc.	Gibson Roofs, Inc.	Gale Associates, Inc.

201300880020	Easton	Moreau Hall	Construction	Accelerated Repair	Roof	DBB	Skanska USA Building, Inc	Baker/Wohl Architects, Inc.	-	Gale Associates, Inc.
200809130705	Essex Agr Tech	Essex Agricultural and Technical High School	Construction	Core Program	New Construction	CM@R	PMA Construction Services	Design Partnership of Cambridge, Inc.	Gilbane Building Company	Turner Facilities Management Solutions
200800940020	Fairhaven	Rogers Elementary School	Building Complete	Core Program	New Construction - Model School	DBB	Daedalus Projects Inc	HMFH Architects, Inc.	CTA Construction Co., Inc.	Consulting Engineering Services, LLC
200900950315	Fall River	James Madison Morton Middle School	Closeout	Core Program	New Construction	DBB	Maguire Group Inc.	Mount Vernon Group Architects, Inc.	J & J Contractors, Inc.	Sebesta Blomberg & Associates, Inc.
201400960405	Falmouth	Lawrence	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
200901010505	Franklin	Franklin High School	Construction	Core Program	New Construction - Model School	DBB	Daedalus Projects Inc	Ai3 Architects LLC	Bacon-Agostini Construction Joint Venture	Consulting Engineering Services, LLC
201408180605	Franklin County	Franklin County Tech	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201401030001	Gardner	Elm Street School	OPM Selection	Accelerated Repair	Windows / Doors, Boiler		-	-	-	-
201201030505	Gardner	Gardner High	Building Complete	Science Lab Initiative	Addition / Renovation	DBB	Pinck & Co., Inc.	Lamoureux Pagano & Associates, Inc.	Five Star Building Corp.	Fitzemeyer & Tocci Associates, Inc.
201201030405	Gardner	Gardner Middle School	Closeout	Accelerated Repair	Boiler		Leftfield, LLC	Richard D. Kimball Company, Inc.	Royal Steam Heater Co.	Fitzemeyer & Tocci Associates, Inc.
200801050505	Georgetown	Georgetown Middle/High School	Design Development	Core Program	Addition / Renovation	DBB	Municipal Building Consultants, Inc.	Drummey Rosane Anderson, Inc.	-	WSP Flack + Kurtz
200901050010	Georgetown	Penn Brook Elementary School	Construction	Core Program	New Construction	DBB	Municipal Building Consultants, Inc.	Drummey Rosane Anderson, Inc.	Brait Builders Corp.	Rist-Frost-Shumway Engineering, P.C.
201406740050	Gill-Montague	Sheffield Elementary	OPM Selection	Accelerated Repair	Windows / Doors, Boiler		-	-	-	-
200901070050	Gloucester	West Parish Elementary School	Design Development	Core Program	New Construction		Knight, Bagge & Anderson Inc.	Dore & Whittier Architects, Inc.	-	Fitzemeyer & Tocci Associates, Inc.
200801100505	Grafton	Grafton Memorial Senior	Closeout	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Symmes Maini & McKee Associates, Inc.	Dimeo Construction Company	Horizon Engineering Associates, LLP
201201110010	Granby	West St	OPM Selection	Core Program			Strategic Building Solutions, LLC	-	-	-
201108230605	Greater Lawrence RVT	Gr Lawrence Reg Voc Tech	Construction	Core Program	Repair	DBB	Vertex Construction Services	Richard D. Kimball Company, Inc.	-	WSP Flack + Kurtz
200908280605	Greater Lowell Voc Tec	Greater Lowell Regional Technical High School	Construction	Core Program	Addition / Renovation	CM@R	Joslin, Lesser + Associates Inc.	Knight, Bagge & Anderson, Inc.	Consigli Construction Company, Inc.	Horizon Engineering Associates, LLP
201008250605	Greater New Bedford	Greater New Bedford Vocational Technical High School	Construction	Core Program	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Drummey Rosane Anderson, Inc.	Agostini Construction Co., Inc.	Symmes, Maini & McKee Associates
201401140030	Greenfield	Green River	OPM Selection	Accelerated Repair	Roof, Windows / Doors, Boiler		-	-	-	-
200901140505	Greenfield	Greenfield High School	Construction	Core Program	New Construction	CM@R	Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.	Shawmut Design and Construction	BVH Integrated Services, P.C.
201206730305	Groton-Dunstable	Groton/Dun Reg'l Middle	Closeout	Accelerated Repair	Roof	DBB	Hill International Company	ICON architecture, inc.	Greenwood Industries, Inc.	Russo Barr Associates, Inc.
201306750007	Hamilton-Wenham	Bessie Buker Elementary	Construction	Accelerated Repair	Boiler	DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	-	Strategic Building Solutions, LLC
201306750015	Hamilton-Wenham	Winthrop School	Construction	Accelerated Repair	Windows / Doors, Boiler	DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	-	CBI Consulting Inc. | Strategic Building Solutions, LLC
200806800505	Hampden-Wilbraham	Minnechaug Regional High School	Closeout	Core Program	New Construction - Model School	DBB	Pinnacle One, Inc.	Mount Vernon Group Architects, Inc.	Fontaine Brothers, Inc.	Horizon Engineering Associates, LLP
201406800030	Hampden-Wilbraham	Soule Road	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201406800305	Hampden-Wilbraham	Thornton Burgess	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201406800310	Hampden-Wilbraham	Wilbraham Middle	OPM Selection	Accelerated Repair	Roof		-	-	-	-
200801220505	Hanover	Hanover High School	Closeout	Core Program	New Construction	DBB	PMA Construction Services	HMFH Architects, Inc.	Callahan, Inc.	Horizon Engineering Associates, LLP
201301220015	Hanover	Sylvester	Eligibility Period	Core Program			-	-	-	-
201301270505	Hatfield	Smith Academy	Design Development	Accelerated Repair	Roof, Windows / Doors	DBB	Hill International Company	Civitects	Silktown Roofing	Building Enclosure Associates, LLC

201201280035	Haverhill	Caleb Dustin Hunking	Design Development	Core Program	New Construction		Joslin, Lesser + Associates Inc.	JCJ Architecture, PC	-	Strategic Building Solutions, LLC
201101280100G	Haverhill	Consentino	Closeout	Green Repair	Windows / Doors	DBB	Vertex Construction Services	CSS Architects Incorporated	New England Builders & Contractors, Inc.	RDK Engineers | Russo Barr Associates, Inc.
W20034393	Haverhill	Haverhill High School	Closeout	Waitlist	Repair		-	-	-	-
201101280085G	Haverhill	John G Whittier	Closeout	Green Repair	Windows / Doors	DBB	Vertex Construction Services	CSS Architects Incorporated	New England Builders & Contractors, Inc.	Russo Barr Associates, Inc.
201101280075G	Haverhill	Tilton	Closeout	Green Repair	Roof	DBB	Vertex Construction Services	CSS Architects Incorporated	Titan Roofing, Inc.	Russo Barr Associates, Inc.
201101280080G	Haverhill	Walnut Square	Closeout	Green Repair	Roof, Windows / Doors	DBB	Vertex Construction Services	CSS Architects Incorporated	Titan Roofing, Inc.	RDK Engineers | Russo Barr Associates, Inc.
201001310410	Hingham	Hingham Middle School	Building Complete	Core Program	New Construction - Model School	DBB	Knight, Bagge & Anderson Inc.	Ai3 Architects LLC	Brait Builders Corp.	Foreman Building Commissioning, LP
200801330505	Holbrook	Holbrook Junior-Senior High School	Schematic Design	Core Program	New Construction		Symmes Maini & McKee Associates, Inc.	Flansburgh Associates, Inc.	-	-
201401370045	Holyoke	E N White Elem	OPM Selection	Accelerated Repair	Boiler		-	-	-	-
201201370015	Holyoke	Lt Elmer J McMahon Elem	OPM Selection	Core Program			-	-	-	-
201401370025	Holyoke	Morgan Elem	OPM Selection	Accelerated Repair	Boiler		-	-	-	-
201201370605	Holyoke	Wm J Dean Voc Tech High	Building Complete	Science Lab Initiative	Addition / Renovation	DBB	Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	RAC Builders, Inc.	BVH Integrated Services, P.C.
201301380010	Hopedale	Memorial	Construction	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	Civitects	-	Simpson Gumpertz & Heger Inc.
201301390005	Hopkinton	Center	OPM Selection	Core Program			-	-	-	-
200801410410	Hudson	John F. Kennedy Middle School	Building Complete	Core Program	New Construction	DBB	PMA Construction Services	OMR Architects, Inc.	Bacon-Agostini Construction Joint Venture	WSP Flack + Kurtz
201401410007	Hudson	Mulready Elementary	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201401440015	Ipswich	Winthrop	Eligibility Period	Core Program			-	-	-	-
201201530007	Leominster	Fall Brook	Closeout	Accelerated Repair	Boiler	DBB	Compass Project Management, Inc.	Reinhardt Associates, Inc.	NB Kenney Company, Inc	Horizon Engineering Associates, LLP
200801530505	Leominster	Leominster High School	Building Complete	Core Program	Addition / Renovation	CM@R	Daedalus Projects Inc	Lamoureux Pagano & Associates, Inc.	S.O.M. Construction Ent,, Inc.	Horizon Engineering Associates, LLP
201401530030	Leominster	Northwest	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201201530010	Leominster	Southeast School	Closeout	Accelerated Repair	Roof, Boiler	DBB	Compass Project Management, Inc.	Reinhardt Associates, Inc.	NB Kenney Company, Inc	Horizon Engineering Associates, LLP | Russo Barr Associates, Inc.
201101540005G	Leverett	Leverett Elementary	Closeout	Green Repair	Roof, Windows / Doors	DBB	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban Designers	-	Russo Barr Associates, Inc.
201101550010E	Lexington	Joseph Estabrook	Building Complete	Core Program	New Construction	CM@R	Hill International Company	DiNisco Design Partnership, Limited	Shawmut Design and Construction	BVH Integrated Services, P.C.
200801590505	Longmeadow	Longmeadow High School	Building Complete	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	OMR Architects, Inc.	Gilbane Building Company	Foreman Building Commissioning, LP
201101600027G	Lowell	Moody Elem	Closeout	Green Repair	Roof, Windows / Doors	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Paul J. Rogan Co., Inc.	Building Enclosure Associates, LLC
201101600055G	Lowell	Washington	Closeout	Green Repair	Roof, Windows / Doors, Boiler	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Alpha Contracting Associates, Inc.	Building Enclosure Associates, LLC | RDK Engineers
201001620505	Lunenburg	Lunenburg High School	Design Development	Core Program	New Construction		Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	Shawmut Design and Construction	Cannon Design
201201630405	Lynn	Breed Middle School	Closeout	Accelerated Repair	Windows / Doors	DBB	Diversified Project Management	Kaestle Boos Associates, Inc.	GVW, Inc.	CBI Consulting Inc.
201401630045	Lynn	E J Harrington	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201201630605	Lynn	Lynn Voc Tech Institute	Closeout	Accelerated Repair	Roof	DBB	Diversified Project Management	Kaestle Boos Associates, Inc.	Gibson Roofs, Inc.	CBI Consulting Inc.
200901630305	Lynn	Thurgood Marshall Middle School	Construction	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Raymond Design Associates, Inc.	Walsh Brothers, Inc.	Rist-Frost-Shumway Engineering, P.C.
201401630040	Lynn	Wm P Connery	OPM Selection	Accelerated Repair	Roof		-	-	-	-

200901640505	Lynnfield	Lynnfield High School	Building Complete	Core Program	Addition / Renovation	DBB	HEERY	Edward Rowse Architects, Inc.	E.A. Colangeli Construction Co. Inc	Fitzemeyer & Tocci Associates, Inc.
200801680020	Marblehead	Glover School	Building Complete	Core Program	New Construction	DBB	Municipal Building Consultants, Inc.	JCJ Architecture, PC	G & R Construction, Inc.	RDK Engineers
201101700008G	Marlborough	Francis J Kane	Closeout	Green Repair	Windows / Doors	DBB	Hill International Company	Baker/Wohl Architects, Inc.	A&A Window Products, Inc.	Building Enclosure Associates, LLC
201101700505G	Marlborough	Marlborough High	Closeout	Green Repair	Roof, Windows / Doors, Boiler	DBB	Hill International Company	Baker/Wohl Architects, Inc.	A&A Window Products, Inc.| Feeley, McAnespie, Inc.| Veterans Development Corporation, Inc.	Building Enclosure Associates, LLC | RDK Engineers
201101710505	Marshfield	Marshfield High	Construction	Core Program	New Construction - Model School	DBB	Compass Project Management, Inc.	Ai3 Architects LLC	Brait Builders Ventures	Sebesta Blomberg & Associates, Inc.
200801740505	Maynard	Maynard High School	Building Complete	Core Program	New Construction	DBB	Municipal Building Consultants, Inc.	Tappe Associates, Inc.	CTA Construction Co., Inc.	WSP Flack + Kurtz
201401750007	Medfield	Ralph Wheelock School	OPM Selection	Accelerated Repair	Boiler		-	-	-	-
201201760505	Medford	Medford High	Construction	Science Lab Initiative	Addition / Renovation	DBB	Leftfield, LLC	DiNisco Design Partnership, Limited	G & R Construction, Inc.	Cannon Design
201301760505	Medford	Medford High	Construction	Accelerated Repair	Windows / Doors, Boiler	DBB	Architectural Consulting Group, LLC	Dietz & Company Architects, Inc.	-	Symmes, Maini & McKee Associates
201401770013	Medway	John D Mc Govern Elem	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201401780017	Melrose	Herbert Clark Hoover	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201201780505	Melrose	Melrose High	Closeout	Science Lab Initiative	Addition / Renovation	DBB	Hill International Company	Ai3 Architects LLC	G & R Construction, Inc.	WSP Flack + Kurtz
200801810505	Methuen	Methuen High School	Building Complete	Core Program	Addition / Renovation	CM@R	KBA/Trident	Finegold Alexander and Associates Inc.	Consigli Construction Company, Inc.	Environmental Health and Engineering
201401840003	Middleton	Fuller Meadow	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201101850090	Milford	Woodland	Design Development	Core Program	New Construction		Joslin, Lesser + Associates Inc.	HMFH Architects, Inc.	Shawmut Design and Construction	Consulting Engineering Services, LLC
201401870005	Millis	Clyde F Brown	Eligibility Period	Core Program			-	-	-	-
200908300605	Minuteman Voc Tech	Minuteman Regional High School	Feasibility Study	Core Program			Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	-	-
201107129999	Monomoy	Monomoy Regional High School	Construction	Core Program	New Construction - Model School	DBB	Skanska USA Building, Inc	Mount Vernon Group Architects, Inc.	Fontaine Brothers, Inc.	Sebesta Blomberg & Associates, Inc.
201307150505	Mount Greylock	Mt Greylock Reg High	Eligibility Period	Core Program			-	-	-	-
201107200003G	Narragansett	Phillipston Memorial	Closeout	Green Repair	Boiler	DBB	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban Designers	-	Rist-Frost-Shumway Engineering, P.C.
200807200020	Narragansett	Templeton Center School	Feasibility Study	Core Program			Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.	-	-
201407250025	Nashoba	Florence Sawyer Sch	OPM Selection	Accelerated Repair	Boiler		-	-	-	-
200807250015	Nashoba	Pompositticut Elementary School	Closeout	Core Program	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Symmes Maini & McKee Associates, Inc.	P.J. Stella Construction Corp.	Strategic Building Solutions, LLC
200908520605G	Nashoba Valley Tech	Nashoba Valley Tech H S	Closeout	Green Repair	Roof	DBB	-	-	-	-
201308520605	Nashoba Valley Tech	Nashoba Valley Tech H S	Design Development	Accelerated Repair	Roof	DBB	STV Incorporated	CGKV Architects, Inc.	-	CBI Consulting Inc.
200801980505	Natick	Natick High School	Closeout	Core Program	New Construction - Model School	DBB	Hill International Company	Ai3 Architects LLC	Brait Builders Corp.	Rist-Frost-Shumway Engineering, P.C.
201306600305	Nauset	Nauset Reg Middle	Design Development	Accelerated Repair	Roof	DBB	Strategic Building Solutions, LLC	ICON architecture, inc.	-	Russo Barr Associates, Inc.
201301990035	Needham	Hillside Elementary	Eligibility Period	Core Program			-	-	-	-
200901990050	Needham	Newman Elementary School	Closeout	Core Program	Repair	CM@R	-	Drummey Rosane Anderson, Inc.	Consigli Construction Company, Inc.	Rist-Frost-Shumway Engineering, P.C.
200902010070	New Bedford	John Hannigan	Designer Selection	Core Program			Daedalus Projects Inc	-	-	-
W201002010505P1	New Bedford	New Bedford High	Closeout	Waitlist	Repair	DBB	-	-	-	-
201102040005	Newburyport	Francis T Bresnahan Elem	Construction	Core Program	New Construction - Model School	DBB	HEERY	HMFH Architects, Inc.	CTA Construction Co., Inc.	Fitzemeyer & Tocci Associates, Inc.
201002040305	Newburyport	Rupert A. Nock Middle School	Construction	Core Program	Addition / Renovation	CM@R	HEERY	Miller Dyer Spears Inc.	Gilbane Building Company	Fitzemeyer & Tocci Associates, Inc.

201102070005	Newton	A E Angier	Design Development	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	DiNisco Design Partnership, Limited	-	Fitzemeyer & Tocci Associates, Inc.
201302070025	Newton	Cabot	OPM Selection	Core Program			Joslin, Lesser + Associates Inc.	-	-	-
200802080005	Norfolk	Freeman-Kennedy Elementary School	Closeout	Core Program	New Construction	DBB	Joslin, Lesser + Associates Inc.	Flansburgh Associates, Inc.	Fontaine Brothers, Inc.	WSP Flack + Kurtz
200909150705	Norfolk County Agriculture	Norfolk County Agr	Construction	Core Program	Addition / Renovation	DBB	Compass Project Management, Inc.	Turowski2 Architecture, Inc.	TLT Construction Corporation	Rist-Frost-Shumway Engineering, P.C.
200802090305	North Adams	Silvio O Conte Middle School	Construction	Core Program	Addition / Renovation	DBB	Strategic Building Solutions, LLC	Margo Jones Architects, Inc.	-	Rist-Frost-Shumway Engineering, P.C.
201202120505	North Attleborough	North Attleboro High	Closeout	Science Lab Initiative	Addition / Renovation	DBB	Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	M. O'Connor Contracting, Inc.	Consulting Engineering Services, LLC
201202120015	North Attleborough	Roosevelt Avenue	Closeout	Accelerated Repair	Windows / Doors	DBB	Skanska USA Building, Inc	Russo Barr Associates, Inc.	Evergreen Construction Corporataion	Gale Associates, Inc.
201402120015	North Attleborough	Roosevelt Avenue	OPM Selection	Accelerated Repair	Boiler		-	-	-	-
201202150015	North Brookfield	North Brookfield Elem	Closeout	Accelerated Repair	Windows / Doors	DBB	Strategic Building Solutions, LLC	CBI Consulting Inc.	Garland Construction Corp.	Simpson Gumpertz & Heger Inc.
201107350505	North Middlesex	North Middlesex Reg	Design Development	Core Program	New Construction	DBB	HEERY	Symmes Maini & McKee Associates, Inc.	-	Horizon Engineering Associates, LLP
201002170505	North Reading	North Reading High School	Construction	Core Program	Addition / Renovation	CM@R	PMA Construction Services	Dore & Whittier Architects, Inc.	Gilbane Building Company	Cannon Design
201402100025	Northampton	Leeds	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201402100029	Northampton	R. K. Finn Ryan Road	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201102130003	Northborough	Lincoln Street	Design Development	Core Program	Addition / Renovation	DBB	Strategic Building Solutions, LLC	Lamoureux Pagano & Associates, Inc.	-	Fitzemeyer & Tocci Associates, Inc.
201202180015	Norton	J C Solmonese	Closeout	Accelerated Repair	Roof	DBB	Joslin, Lesser + Associates Inc.	Habeeb & Associates Architects, Inc.	Silktown Roofing	Simpson Gumpertz & Heger Inc.
200902180505	Norton	Norton High School	Building Complete	Core Program	Addition / Renovation	CM@R	Pinck & Co., Inc.	JCJ Architecture, PC	W. T. Rich Company Inc.	Rist-Frost-Shumway Engineering, P.C.
201402200010	Norwood	Cornelius M Callahan	OPM Selection	Accelerated Repair	Boiler		-	-	-	-
200908550605	Old Colony Reg Voc Tech	Old Colony Regional Vocational Technical High School	Closeout	Core Program	Repair	DBB	Vertex Construction Services	Habeeb & Associates Architects, Inc.	J.D. Rivet & Co., Inc.	Consulting Engineering Services, LLC
201302230010	Orange	Dexter Park	Eligibility Period	Core Program			-	-	-	-
201402240005	Orleans	Orleans Elementary	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
200802260405	Oxford	Oxford Middle School	Construction	Core Program	Repair	DBB	Diversified Project Management	CGKV Architects, Inc.	J.J. Cardosi, Inc.	Cannon Design
201102270305G	Palmer	Converse Middle	Closeout	Green Repair	Roof, Boiler	DBB	Diversified Project Management	-	Royal Steam Heater Co.| Titan Roofing, Inc.	Strategic Building Solutions, LLC
201102270008G	Palmer	Old Mill Pond	Closeout	Green Repair	Roof, Boiler	DBB	Diversified Project Management	-	Royal Steam Heater Co.	Strategic Building Solutions, LLC
201102270505G	Palmer	Palmer High	Closeout	Green Repair	Roof, Boiler	DBB	Diversified Project Management	-	Royal Steam Heater Co.| Titan Roofing, Inc.	Strategic Building Solutions, LLC
201308600605	Pathfinder Voc Tech	Pathfinder Voc Tech	Approved Project Vote Pending	Accelerated Repair	Roof	DBB	exPERTcon, Inc.	Baker/Wohl Architects, Inc.	-	Building Enclosure Associates, LLC
200802290305	Peabody	Higgins Middle School	Construction	Core Program	New Construction	DBB	Daedalus Projects Inc	DiNisco Design Partnership, Limited	-	BVH Integrated Services, P.C.
201102290007G	Peabody	John E Burke	Closeout	Green Repair	Roof, Windows / Doors, Boiler	DBB	Daedalus Projects Inc	LPBA/ Architects, Inc.	-	Sebesta Blomberg & Associates, Inc.
201402290016	Peabody	John E. McCarthy	OPM Selection	Accelerated Repair	Roof, Windows / Doors		-	-	-	-
201102290027G	Peabody	William A Welch Sr	Closeout	Green Repair	Roof	DBB	Daedalus Projects Inc	LPBA/ Architects, Inc.	-	Sebesta Blomberg & Associates, Inc.
201302310010	Pembroke	Hobomock Elementary	Construction	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	The S/L/A/M Collaborative	-	CBI Consulting Inc.
201302310015	Pembroke	North Pembroke Elem	Construction	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	The S/L/A/M Collaborative	Paul J. Rogan Co., Inc.	CBI Consulting Inc.
201302310305	Pembroke	Pembroke Community Middle School	Construction	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	The S/L/A/M Collaborative	Paul J. Rogan Co., Inc.	CBI Consulting Inc.
201302310505	Pembroke	Pembroke High School	Construction	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	The S/L/A/M Collaborative	-	CBI Consulting Inc.

201107450020G	Pentucket	Dr Frederick N Sweetsir	Closeout	Green Repair	Roof, Windows / Doors, Boiler	DBB	PMA Construction Services	Knight, Bagge & Anderson, Inc.	E. Amanti & Sons, Inc.	CBI Consulting Inc. | RDK Engineers
201107450015G	Pentucket	Dr John C Page School	Closeout	Green Repair	Roof, Windows / Doors, Boiler	DBB	PMA Construction Services	Knight, Bagge & Anderson, Inc.	Capeway Roofing Systems, Inc.	CBI Consulting Inc. | RDK Engineers
201307450405	Pentucket	Pentucket Reg Middle	Construction	Accelerated Repair	Roof, Boiler	DBB	Arcadis U.S., Inc.	CGKV Architects, Inc.	-	CBI Consulting Inc. | Strategic Building Solutions, LLC
201002360510	Pittsfield	Taconic High School	Feasibility Study	Core Program			Skanska USA Building, Inc	Drummey Rosane Anderson, Inc.	-	-
200802390505	Plymouth	Plymouth North High School	Closeout	Core Program	New Construction - Model School	DBB	Ted Gentry Associates, Inc	Ai3 Architects LLC	-	Sebesta Blomberg & Associates, Inc.
201202390515	Plymouth	Plymouth South High	Schematic Design	Core Program	New Construction		Ted Gentry Associates, Inc	Ai3 Architects LLC	-	-
201302420505	Provincetown	Provincetown High	Eligibility Period	Core Program			-	-	-	-
201207530030	Quabbin	Ruggles Lane	Closeout	Accelerated Repair	Roof, Windows / Doors	DBB	Vertex Construction Services	Turowski2 Architecture, Inc.	PDS Engineering and Construction, Inc.	Simpson Gumpertz & Heger Inc.
201207780005	Quaboag Regional	Warren Elementary	Building Complete	Accelerated Repair	Boiler	DBB	Coast and Harbor Association, Inc.	Lindgren & Sharples, Inc.	AAlanco Service Corporation	Strategic Building Solutions, LLC
200802430315	Quincy	Central Middle School	Building Complete	Core Program	New Construction - Model School	DBB	Tishman Construction Corporation of MA	Ai3 Architects LLC	H.V. Collins Co., Inc.	Sebesta Blomberg & Associates, Inc.
201402430075	Quincy	Francis W Parker	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201402430035	Quincy	Lincoln-Hancock Comm Sch	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201302430060	Quincy	Merrymount	Design Development	Accelerated Repair	Windows / Doors	DBB	Skanska USA Building, Inc	Habeeb & Associates Architects, Inc.	-	Simpson Gumpertz & Heger Inc.
201302430510	Quincy	North Quincy High	Design Development	Accelerated Repair	Windows / Doors	DBB	Skanska USA Building, Inc	Habeeb & Associates Architects, Inc.	-	Simpson Gumpertz & Heger Inc.
201302430320	Quincy	Reay E Sterling Middle	Eligibility Period	Core Program			-	-	-	-
201302430110	Quincy	Wollaston School	Design Development	Accelerated Repair	Windows / Doors	DBB	Skanska USA Building, Inc	Habeeb & Associates Architects, Inc.	-	Simpson Gumpertz & Heger Inc.
201402440018	Randolph	J F Kennedy Elem	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201302440410	Randolph	Randolph Community Middle	Construction	Accelerated Repair	Windows / Doors	DBB	NETCO Construction Project Managers, Inc.	Taylor & Burns, Inc.	-	Consulting Engineering Services, LLC
201302440505	Randolph	Randolph High	Construction	Accelerated Repair	Roof	DBB	NETCO Construction Project Managers, Inc.	-	-	Gale Associates, Inc.
201402440505	Randolph	Randolph High	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201002480035	Revere	Staff Sergeant James J. Hill School	Construction	Core Program	New Construction	DBB	Hill International Company	-	CTA Construction Co., Inc.	Rist-Frost-Shumway Engineering, P.C.
200802510305	Rockland	John W. Rogers Middle School	Closeout	Core Program	New Construction	CM@R	Daedalus Projects Inc	Dore & Whittier Architects, Inc.	Agostini Construction Co., Inc.	Consulting Engineering Services, LLC
200902580305G	Salem	Collins Middle School	Building Complete	Green Repair	Roof, Windows / Doors, Boiler, Building Envelope	CM@R	KV Associates, Inc.	Reinhardt Associates, Inc.	Gilbane Building Company	Rist-Frost-Shumway Engineering, P.C.
201002580050G	Salem	Saltonstall School	Closeout	Green Repair	Roof, Windows / Doors, Boiler, Building Envelope	CM@R	KV Associates, Inc.	Reinhardt Associates, Inc.	Gilbane Building Company	Rist-Frost-Shumway Engineering, P.C.
201002620305	Saugus	Belmonte Middle School	Closeout	Core Program	Repair	CM@R	Skanska USA Building, Inc	Fletcher Thompson Architecture Engineering, LLC	Consigli Construction Company, Inc.	Consulting Engineering Services, LLC
201202640305	Scituate	Gates Intermediate School	Feasibility Study	Core Program			Daedalus Projects Inc	Dore & Whittier Architects, Inc.	-	-
201208710605	Shawsheen Valley Voc Tech	Shawsheen Valley Voc Tech High School	Closeout	Accelerated Repair	Boiler	DBB	Diversified Project Management	Shekar & Associates, Inc.	NB Kenney Company, Inc	Fitzemeyer & Tocci Associates, Inc.
200802710305	Shrewsbury	Sherwood Middle School	Building Complete	Core Program	New Construction	CM@R	PMA Construction Services	Lamoureux Pagano & Associates, Inc.	Gilbane Building Company	RDK Engineers
201308290605	So Middlesex Voc Tech Reg	Joseph P Keefe Tech HS	Construction	Accelerated Repair	Roof	DBB	PMA Construction Services	Raymond Design Associates, Inc.	Greenwood Industries, Inc.	Russo Barr Associates, Inc.
200811119999	Somerset-Berkley	Somerset-Berkley High	Building Complete	Core Program	New Construction - Model School	DBB	Skanska USA Building, Inc	Ai3 Architects LLC	Bacon-Agostini Construction Joint Venture	Horizon Engineering Associates, LLP

200902740111E	Somerville	East Somerville Community School at Cummings	Closeout	Core Program	Addition / Renovation	CM@R	PMA Construction Services	Maguire Group Inc.	Gilbane Building Company	Foreman Building Commissioning, LP
201302740505	Somerville	Somerville High	Eligibility Period	Core Program			-	-	-	-
200902780015	South Hadley	Plains School	Construction	Core Program	New Construction	DBB	Arcadis U.S., Inc.	Margo Jones Architects, Inc.	-	Strategic Building Solutions, LLC
201408730605	South Shore Reg Voc Tech	So Shore Voc Tech High	OPM Selection	Accelerated Repair	Boiler		-	-	-	-
201202750005	Southampton	William E Norris	Building Complete	Accelerated Repair	Roof	DBB	Tishman Construction Corporation of MA	Reinhardt Associates, Inc.	Greenwood Industries, Inc.	Building Enclosure Associates, LLC
200802770505	Southbridge	Southbridge High School	Closeout	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	Consigli Construction Company, Inc.	Environmental Health and Engineering
200908720605	Southeastern Reg Voc Tech	Southeastern Regional Vocational Technical School	Closeout	Core Program	Addition / Renovation	CM@R	Hill International Company	Drummey Rosane Anderson, Inc.	W. T. Rich Company Inc.	RDK Engineers
201407650505	Southern Berkshire	Mt Everett Regional	OPM Selection	Accelerated Repair	Roof, Boiler		-	-	-	-
200908760605	Southern Worcester Cty VT	Bay Path Regional Vocational Technical High School	Construction	Core Program	Addition / Renovation	CM@R	HEERY	Kaestle Boos Associates, Inc.	Consigli Construction Company, Inc.	RDK Engineers
201107660305	Southwick-Tolland	Powder Mill	Construction	Core Program	Repair	DBB	Strategic Building Solutions, LLC	JCJ Architecture, PC	PDS Engineering and Construction, Inc.	BVH Integrated Services, P.C.
201107660505	Southwick-Tolland	Southwick-Tolland Regional High	Construction	Core Program	Addition / Renovation	DBB	Strategic Building Solutions, LLC	JCJ Architecture, PC	Fontaine Brothers, Inc.	BVH Integrated Services, P.C.
200807660010	Southwick-Tolland	Woodland Elementary School	Construction	Core Program	Addition / Renovation	DBB	Strategic Building Solutions, LLC	JCJ Architecture, PC	PDS Engineering and Construction, Inc.	BVH Integrated Services, P.C.
200902810165G	Springfield	Arthur T Talmadge	Closeout	Green Repair	Windows / Doors	DBB	-	-	-	-
201302810310	Springfield	Chestnut Accelerated Middle School	Construction	Accelerated Repair	Roof	DBB	-	-	-	Building Enclosure Associates, LLC
201102810125E	Springfield	Dryden Memorial	Building Complete	Core Program	Addition / Renovation	CM@R	Arcadis U.S., Inc.	Drummey Rosane Anderson, Inc.	Morganti/Aquadro & Cerruti	BVH Integrated Services, P.C.
201102810030E	Springfield	Elias Brookings	Construction	Core Program	New Construction	CM@R	Arcadis U.S., Inc.	Drummey Rosane Anderson, Inc.	Morganti/Aquadro & Cerruti	BVH Integrated Services, P.C.
W20014137	Springfield	Forest Park Middle School	Building Complete	Waitlist	Addition / Renovation	CM@R	Arcadis U.S., Inc.	Perkins Eastman	Consigli Construction Company, Inc.	Foreman Building Commissioning, LP
200902810075G	Springfield	Frank H Freedman	Closeout	Green Repair	Roof, Windows / Doors	DBB	-	-	-	Building Enclosure Associates, LLC
200902810068G	Springfield	Glickman Elementary	Closeout	Green Repair	Windows / Doors	DBB	-	-	-	Building Enclosure Associates, LLC
201302810530	Springfield	High School/Science-Tech	Construction	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	CBI Consulting Inc.	Kronenberger & Sons Restoration, INc.	Building Enclosure Associates, LLC
201402810328	Springfield	John F Kennedy Middle	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
200902810320G	Springfield	John J Duggan Middle	Closeout	Green Repair	Roof, Windows / Doors	DBB	-	-	-	Building Enclosure Associates, LLC
201402810110	Springfield	Kensington Avenue	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
200902810330G	Springfield	M Marcus Kiley Middle	Closeout	Green Repair	Roof	DBB	-	-	-	Building Enclosure Associates, LLC
200802810060G	Springfield	Margaret C Ells	Closeout	Green Repair	Windows / Doors	DBB	-	-	-	Building Enclosure Associates, LLC
201302810060	Springfield	Margaret C Ells	Construction	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	CBI Consulting Inc.	Allied Restoration Corporation	Building Enclosure Associates, LLC
200902810140G	Springfield	Mary M Lynch	Closeout	Green Repair	Windows / Doors	DBB	-	-	-	Building Enclosure Associates, LLC
200902810155G	Springfield	Mary M Walsh	Closeout	Green Repair	Roof	DBB	-	-	-	Building Enclosure Associates, LLC
200902810023G	Springfield	Milton Bradley School	Closeout	Green Repair	Roof	DBB	-	-	-	Building Enclosure Associates, LLC
W20054428	Springfield	Roger L. Putnam Vocational Technical High School	Closeout	Waitlist	New Construction	CM@R	Pinnacle One, Inc.	Drummey Rosane Anderson, Inc.	Consigli/Morganti	Strategic Building Solutions, LLC
201302810355	Springfield	South End Middle School	Construction	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	CBI Consulting Inc.	-	Building Enclosure Associates, LLC
201202810500	Springfield	Springfield Central High	Construction	Science Lab Initiative	Addition / Renovation	CM@R	Leftfield, LLC	DiNisco Design Partnership, Limited	Morganti/Aquadro & Cerruti	Horizon Engineering Associates, LLP

201302810550	Springfield	Springfield Public Day High School	Construction	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	CBI Consulting Inc.	-	Building Enclosure Associates, LLC
200902810180G	Springfield	Warner	Closeout	Green Repair	Roof, Windows / Doors, Boiler	DBB	-	-	-	Building Enclosure Associates, LLC
200902810185G	Springfield	Washington	Closeout	Green Repair	Windows / Doors	DBB	-	-	-	Building Enclosure Associates, LLC
200902810190G	Springfield	White Street	Closeout	Green Repair	Windows / Doors	DBB	-	-	-	Building Enclosure Associates, LLC
200902840405	Stoneham	Stoneham Middle School	Construction	Core Program	Addition / Renovation	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	Shawmut Design and Construction	RDK Engineers
201302850010	Stoughton	Helen Hansen Elementary	Design Development	Accelerated Repair	Windows / Doors	DBB	Hill International Company	Russo Barr Associates, Inc.	-	-
201402850025	Stoughton	Joseph H Gibbons	OPM Selection	Accelerated Repair	Roof, Windows / Doors		-	-	-	-
201302850014	Stoughton	Joseph R Dawe Jr Elem	Design Development	Accelerated Repair	Windows / Doors	DBB	Hill International Company	Russo Barr Associates, Inc.	-	-
201302850505	Stoughton	Stoughton High	Eligibility Period	Core Program			-	-	-	-
201302850020	Stoughton	West Elementary	Design Development	Accelerated Repair	Roof	DBB	Hill International Company	Russo Barr Associates, Inc.	-	-
200802870005	Sturbridge	Burgess Elementary School	Building Complete	Core Program	Addition / Renovation	DBB	Lamoureux Pagano & Associates, Inc.	Drummey Rosane Anderson, Inc.	Fontaine Brothers, Inc.	Horizon Engineering Associates, LLP
201402880025	Sudbury	General John Nixon Elem	OPM Selection	Accelerated Repair	Roof, Windows / Doors		-	-	-	-
200802900305	Sutton	Sutton Middle School	Construction	Core Program	Addition / Renovation	DBB	Strategic Building Solutions, LLC	Flansburgh Associates, Inc.	Brait Builders Corp.	RDK Engineers
201102910010	Swampscott	Hadley	Schematic Design	Core Program	New Construction	DBB	Hill International Company	Mount Vernon Group Architects, Inc.	-	-
200802950505	Tewksbury	Tewksbury Memorial High School	Closeout	Core Program	New Construction - Model School	DBB	HEERY	Symmes Maini & McKee Associates, Inc.	CTA Ventures	Sebesta Blomberg & Associates, Inc.
201208780605	Tri County	Tri County Reg Voc Tech	Closeout	Science Lab Initiative	Addition / Renovation	DBB	Hill International Company	Ai3 Architects LLC	Federal Construction Corp.	-
201408780605	Tri County	Tri County Reg Voc Tech	OPM Selection	Accelerated Repair	Boiler		-	-	-	-
201403010505	Tyngsborough	Tyngsborough High School	OPM Selection	Accelerated Repair	Roof, Boiler		-	-	-	-
200803040505	Uxbridge	Uxbridge High	Closeout	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Raymond Design Associates, Inc.	Shawmut Design and Construction	Turner Facilities Management Solutions
200907750305	Wachusett	Mountview Middle School	Construction	Core Program	New Construction	DBB	-	Lamoureux Pagano & Associates, Inc.	-	Fitzemeyer & Tocci Associates, Inc.
201107750035G	Wachusett	Naquag Elementary	Closeout	Green Repair	Roof, Windows / Doors, Boiler	DBB	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	MDM Engineering	Rist-Frost-Shumway Engineering, P.C.
201107750040G	Wachusett	Paxton Center	Closeout	Green Repair	Roof, Windows / Doors	DBB	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	MDM Engineering	Rist-Frost-Shumway Engineering, P.C.
201107750045G	Wachusett	Thomas Prince	Closeout	Green Repair	Roof, Windows / Doors, Boiler	DBB	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	MDM Engineering	Rist-Frost-Shumway Engineering, P.C.
201003050310	Wakefield	Galvin Middle School	Construction	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	Bond Brothers, Inc.	B2Q Associates, Inc.
201303070015	Walpole	Fisher	Construction	Accelerated Repair	Roof	DBB	-	-	-	Gale Associates, Inc.
201303100505	Wareham	Wareham Senior High	Design Development	Accelerated Repair	Roof	DBB	Hill International Company	Tighe & Bond, Inc.	-	Russo Barr Associates, Inc.
201403150005	Wayland	Claypit Hill School	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201203150305	Wayland	Wayland Middle School	Closeout	Accelerated Repair	Roof	DBB	Joslin, Lesser + Associates Inc.	DiMarinisi & Wolfe Architects Urban Designers	Capeway Roofing Systems, Inc.	CBI Consulting Inc.
200903160015	Webster	Park Avenue Elementary School	Construction	Core Program	New Construction	DBB	Hill International Company	Dore & Whittier Architects, Inc.	CTA Construction Co., Inc.	Cannon Design
201403170305	Wellesley	Wellesley Middle	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
200803170505	Wellesley	Wellesley Senior School	Closeout	Core Program	New Construction	CM@R	-	Symmes Maini & McKee Associates, Inc.	-	Rist-Frost-Shumway Engineering, P.C.
201303180005	Wellfleet	Wellfleet Elementary	Design Development	Accelerated Repair	Roof	DBB	Architectural Consulting Group, LLC	CSS Architects Incorporated	DDC Construction Inc.	Russo Barr Associates, Inc.
201103220005G	West Boylston	Major Edwards Elementary	Closeout	Green Repair	Windows / Doors	DBB	URS Corporation	Reinhardt Associates, Inc.	-	Cannon Design

201003230505	West Bridgewater	West Bridgewater Middle-Senior High School	Construction	Core Program	New Construction	DBB	Strategic Building Solutions, LLC	Flansburgh Associates, Inc.	CTA Construction Co., Inc.	Cannon Design
200903320505	West Springfield	West Springfield High School	Building Complete	Core Program	New Construction - Model School	DBB	Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.	Fontaine Brothers, Inc.	Turner Facilities Management Solutions
200903210305	Westborough	Gibbons Middle School	Feasibility Study	Core Program			HEERY	Habeeb & Associates Architects, Inc.	-	-
200903250020	Westfield	Abner Gibbs Elementary School	Construction	Core Program	New Construction - Model School	DBB	Skanska USA Building, Inc	Margo Jones Architects, Inc.	Fontaine Brothers, Inc.	Horizon Engineering Associates, LLP
201103250033E	Westfield	Munger Hill	Closeout	Accelerated Repair	Roof	DBB	Vertex Construction Services	Knight, Bagge & Anderson, Inc.	Allied Restoration Corporation	Building Enclosure Associates, LLC
201203250036	Westfield	Paper Mill	Closeout	Accelerated Repair	Roof	DBB	Vertex Construction Services	Knight, Bagge & Anderson, Inc.	R & H Roofing, LLP	Building Enclosure Associates, LLC
201303260025	Westford	Col John Robinson	Design Development	Accelerated Repair	Windows / Doors	DBB	Strategic Building Solutions, LLC	Gale Associates, Inc.	-	CBI Consulting Inc.
201303260007	Westford	Day Elementary	Design Development	Accelerated Repair	Windows / Doors	DBB	Strategic Building Solutions, LLC	Gale Associates, Inc.	-	CBI Consulting Inc.
201303270005	Westhampton	Westhampton Elem School	Construction	Accelerated Repair	Roof, Windows / Doors, Boiler	DBB	Atlantic Construction and Management, Inc.	CSS Architects Incorporated	-	Building Enclosure Associates, LLC
200903300012	Weston	Field Elementary School	Construction	Core Program	New Construction	DBB	Compass Project Management, Inc.	Jonathan Levi Architects LLC	Colantonio, Inc.	Foreman Building Commissioning, LP
201203360080	Weymouth	William Seach	Closeout	Accelerated Repair	Boiler	DBB	PMA Construction Services	BLW Engineers, Inc.	Multitemp Mechanical Corporation	B2Q Associates, Inc.
200907800025	Whitman-Hanson	Maquan Elementary School	Approved Project Vote Pending	Core Program	New Construction	DBB	Knight, Bagge & Anderson Inc.	Turowski2 Architecture, Inc.	-	-
200803400005	Williamsburg	Anne T. Dunphy School	Construction	Core Program	Addition / Renovation	DBB	Arcadis U.S., Inc.	Drummey Rosane Anderson, Inc.	Enfield Builders, Inc.	B2Q Associates, Inc.
201203420060	Wilmington	North Intermediate	Construction	Accelerated Repair	Windows / Doors	DBB	Diversified Project Management	-	-	CBI Consulting Inc.
200903420505	Wilmington	Wilmington High School	Construction	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Dore & Whittier Architects, Inc.	Gilbane Building Company	Symmes, Maini & McKee Associates
200803440025	Winchester	Vinson-Owen Elementary School	Building Complete	Core Program	New Construction	DBB	Skanska USA Building, Inc	Tappe Associates, Inc.	CTA Construction Co., Inc.	Turner Facilities Management Solutions
201003440505	Winchester	Winchester High School	Design Development	Core Program	Addition / Renovation	DBB	Skanska USA Building, Inc	Symmes Maini & McKee Associates, Inc.	-	RDK Engineers
200803460505	Winthrop	Winthrop High School	Design Development	Core Program	New Construction	CM@R	Skanska USA Building, Inc	HMFH Architects, Inc.	Gilbane Building Company	WSP Flack + Kurtz
201203470060	Woburn	Wyman	Feasibility Study	Core Program			Municipal Building Consultants, Inc.	DiNisco Design Partnership, Limited	-	-
201203480052	Worcester	Chandler Magnet	Construction	Accelerated Repair	Windows / Doors	DBB	Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201403480055	Worcester	Clark St Community	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201303480060	Worcester	Columbus Park	Design Development	Accelerated Repair	Windows / Doors, Boiler	DBB	Architectural Consulting Group, LLC	The S/L/A/M Collaborative	-	RDK Engineers | Russo Barr Associates, Inc.
201203488099	Worcester	Dr. James Caradonio Center	Building Complete	Accelerated Repair	Boiler	DBB	Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	CAM HVAC & Construction, Inc.	RDK Engineers | Russo Barr Associates, Inc.
201403480100	Worcester	Goddard Sch/Science Tech	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201203480140	Worcester	Jacob Hiatt Magnet	Building Complete	Accelerated Repair	Boiler	DBB	Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	CAM HVAC & Construction, Inc.	RDK Engineers
201203480145	Worcester	Lake View	Building Complete	Accelerated Repair	Windows / Doors	DBB	Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201203480175	Worcester	May Street	Building Complete	Accelerated Repair	Windows / Doors	DBB	Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201203480200	Worcester	Nelson Place	Feasibility Study	Core Program			Tishman Construction Corporation of MA	Lamoureux Pagano & Associates, Inc.	-	-
W20004048	Worcester	North High School	Closeout	Waitlist	New Construction	CM@R	-	-	-	-
201303480230	Worcester	Tatnuck	Construction	Accelerated Repair	Windows / Doors	DBB	Architectural Consulting Group, LLC	The S/L/A/M Collaborative	-	Russo Barr Associates, Inc.
201403480240	Worcester	Union Hill School	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201403480260	Worcester	West Tatnuck	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-


201303480225	Worcester	Worcester Arts Magnet Sch	Construction	Accelerated Repair	Windows / Doors	DBB	Architectural Consulting Group, LLC	The S/L/A/M Collaborative	-	Russo Barr Associates, Inc.
201303480420	Worcester	Worcester East Middle	Design Development	Accelerated Repair	Boiler	DBB	Architectural Consulting Group, LLC	The S/L/A/M Collaborative	-	RDK Engineers

2014 ESTIMATED BID DATES


Note bid dates are Estimates ONLY. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

District	Enrollment	Project Budget	Start	Finish	Construction Budget	Notes
Ayer Shirley RSD	495	$ 56.5	9/18/13	3/31/14	$ 44.4	GMP issued: March
Revere	690	$ 44.4	1/1/14	1/23/14	$ 33.9	NTP issued: March
North Adams	310	$ 29.7	1/15/14	3/17/14	$ 21.9	NTP issued: April
Greater Lowell RVTSD	1990	$ 65.3	1/22/14	3/31/14	$ 53.2	GMP issued: March
Auburn	560	$ 44.5	2/1/14	6/6/14	$ 35.5	GMP issued: June
Wachusett RSD	800	$ 54.3	2/21/14	5/15/14	$ 43.1	NTP issued: May
South Hadley	270	$ 28.2	3/15/14	4/22/14	$ 21.6	NTP issued: May
Chicopee	850	$ 38.0	4/1/14	5/14/14	$ 30.8	NTP issued: May
Peabody	1340	$ 92.6	4/8/14	6/17/14	$ 75.1	NTP issued: June
Greater Lawrence RVTSD	1400	$ 5.2	4/8/14	5/29/14	$ 4.4	NTP issued: June
Lynn	1100	$ 92.0	8/23/14	10/21/14	$ 67.7	GMP targeted: October
Athol-Royalston RSD	545	$ 43.9	8/23/14	11/10/14	$ 35.2	NTP targeted: November
Newton	465	$ 37.5	9/8/14	10/21/14	$ 26.2	GMP targeted: October
Lunenburg	820	$ 72.9	9/15/14	11/24/14	$ 59.6	GMP targeted: November
Winchester	1370	$ 129.9	10/6/14	11/26/14	$ 100.9	GMP targeted: November
Gloucester	355	$ 39.6	10/20/14	12/17/14	$ 30.0	GMP targeted: December
Milford	985	$ 60.9	11/3/14	1/15/15	$ 48.4	GMP targeted: January
Total	**14,345**	**$ 935.4**			**$ 731.9**	

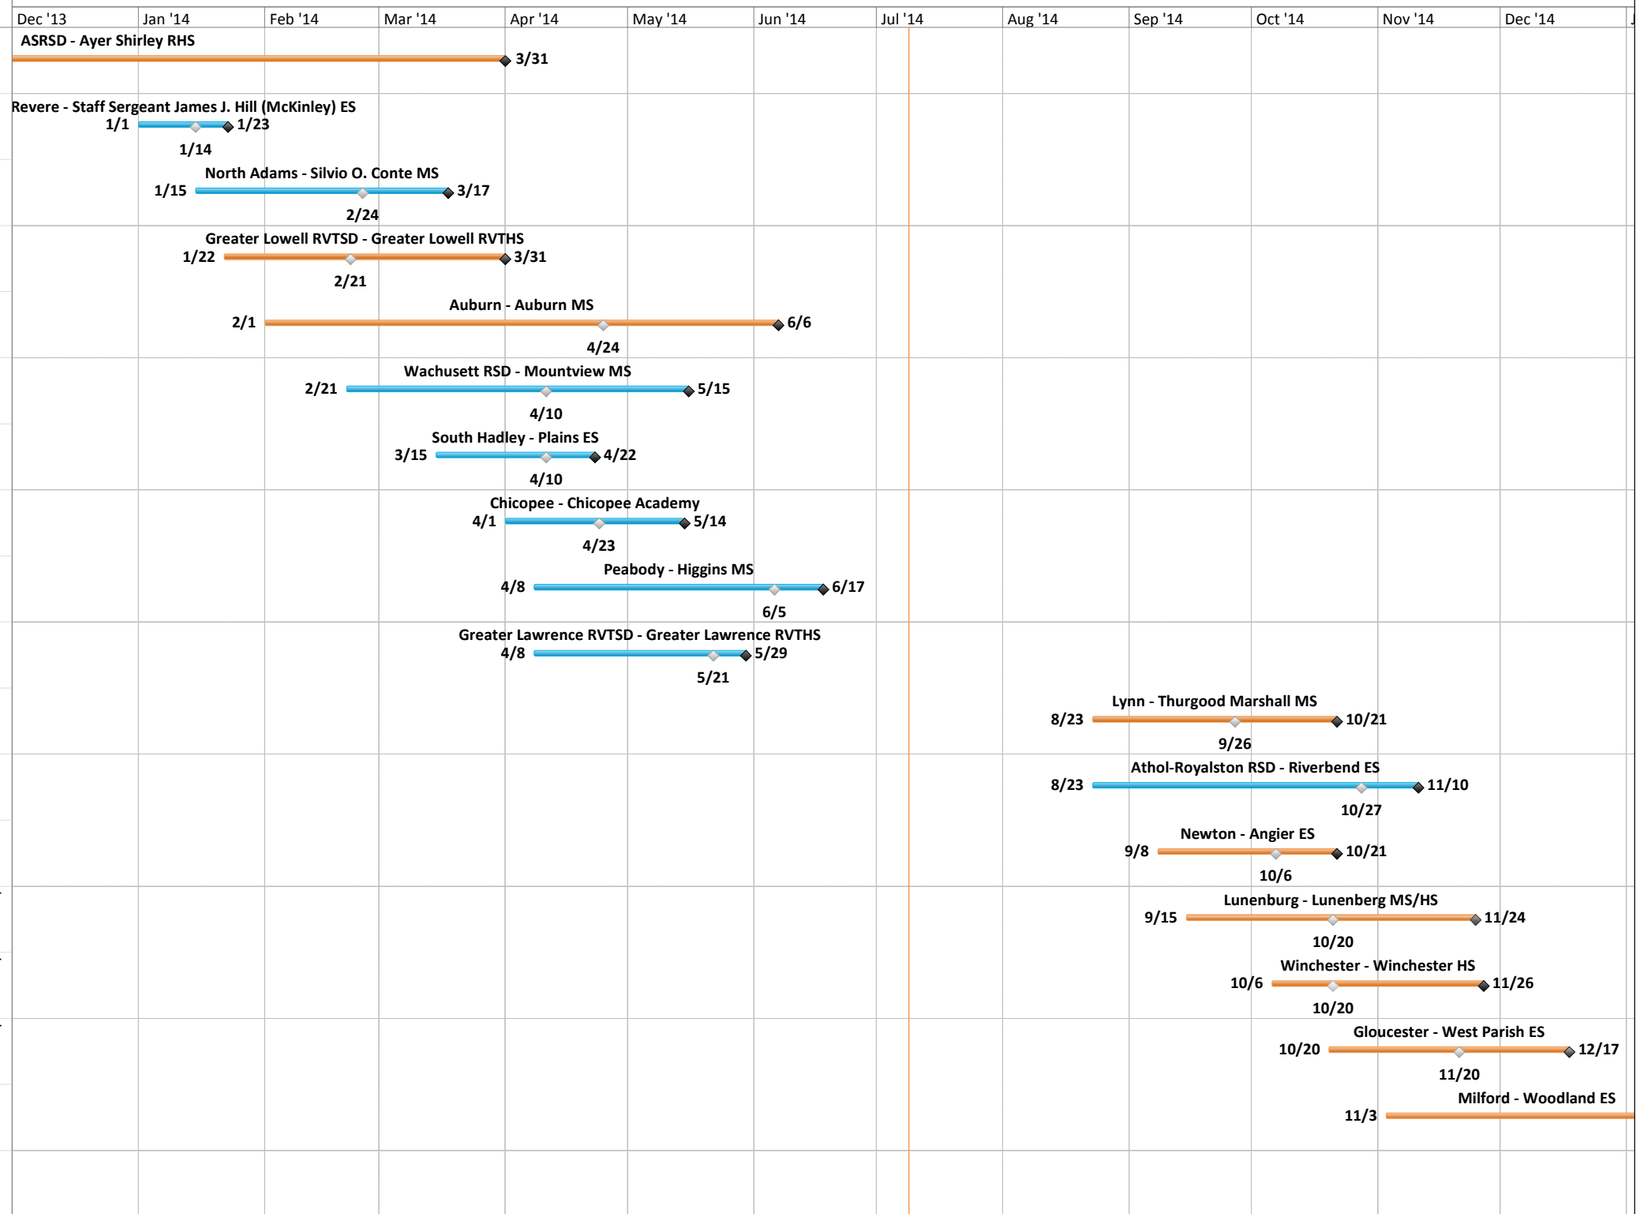

Note: Budget values are in millions.
The project start date represents the Filed-Sub bid solicitation date, gray diamond Filed-Sub bid date, and the black diamond GC Bids / GMP Execution.




7/9/2014

2015 ESTIMATED BID DATES

Note bid dates are Estimates ONLY. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

District	Enrollment	Project Budget	Start	Finish	Construction Budget	Notes
Winthrop	970	$ 80.2	2/2/15	4/15/15	$ 61.9	GMP targeted: April
Northborough	270	$ 25.5	2/2/15	4/1/15	$ 18.2	NTP targeted: April
Georgetown	720	$ 7.8	2/23/15	4/14/15	$ 5.9	NTP targeted: April
North Middlesex RSD	870	$ 89.0	3/16/15	5/14/15	$ 68.8	NTP targeted: May
Total	**2,830**	**$ 203.0**			**$ 154.8**	

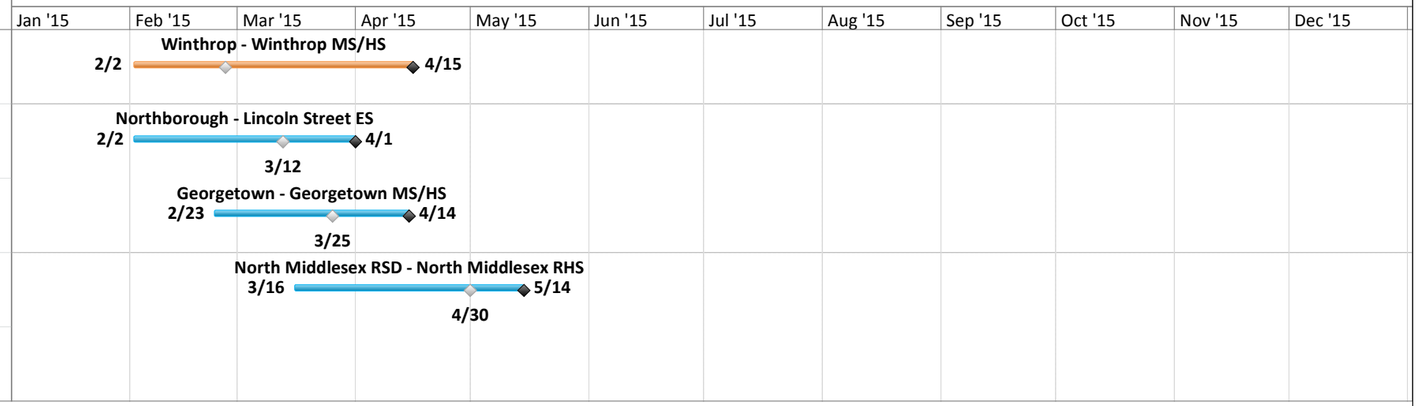


Note: Budget values are in millions.
The project start date represents the Filed-Sub bid solicitation date, gray diamond Filed-Sub bid date, and the black diamond GC Bids / GMP Execution.

7/9/2014



DBB Project



CMR Project

Projects in Construction
MSBA Grant Basis and Maximum Grant Amount
Data Reported as of July 9, 2014

Core Program and Waitlist Totals			$2,776,819,810														*Includes Alternates	$1,768,006,814
Project	**Grade**	**Contractor**	**Total Construction Cost***	**Projected Enrollment**	**PFA or Bid Data**	**Proposed Sq.Ft.**	**Construction Cost/Sq.Ft.**	**Building Cost**	**Building Cost/Sq.Ft.**	**Procurement Type**	**Construction Start Date**	**Substantial Completion**	**Schedule Variance (days)**	**Physical Progress**	**Change Orders**	**Change Orders %**	**Construction Status**	**Max Total Facilities Grant**
CAPITAL PIPELINE PROJECTS IN CONSTRUCTION																		
Core Program Totals			**$2,742,073,912**				**$17,528**		**$13,153**									**$1,731,926,230**
Arlington Thompson	Elementary School	G & R Construction, Inc.	$15,340,026	380	Bid	57,614	$266	$12,403,811	$215	Design/Bid/Build	07-Apr-12	21-Aug-13	0	100%	$473,244	3.085%	The new school building is in service. Site work is complete and final acceptance inspection of landscaping work is planned for the Fall of 2014.	$8,996,284
Assabet Valley Assabet Valley Voc H S	Vocational / Technical	CTA Construction Co., Inc.	$46,764,740	963	Bid	367,565	$127	$41,523,764	$113	Design/Bid/Build	01-Apr-13	01-Aug-15	0	46%	$371,205	0.794%	This is a (10) phase project. Phase 1 ,2 ,3 and 4 are complete. Punch list items in Phase 2, 3 and 4 are complete. Work includes demolition of ceiling tiles, demolition of the Mechanical Room, HVAC work and abatement, MEP work, windows, roofing, flooring and painting for these areas. Certificate of Occupancy for Phase 2 was received which allowed students and staff back into the building in that location. Phase 5 was completed on June 30, 2014. Punch list for Phase 5 will continue through the summer. Phase 6 began on July 1,2014.	$28,790,301
Berlin-Boylston Tahanto Reg High	High School	CTA Construction Co., Inc.	$32,162,000	560	Bid	126,100	$255	$24,629,999	$195	Design/Bid/Build	10-May-11	01-Jul-13	0	99%	$1,026,723	3.282%	The new school building is in service. The District has bid and awarded a contract for installation of a ceramic tile rain screen which is scheduled to be substantially complete by August 25, 2014. Discussions between the District and contractor are continuing in an attempt to resolve open issues associated with remaining change orders that the contractor has not signed; the added cost of the new rain screen that is being installed to replace the failed blue stone; and, grading/poor drainage at the baseball field.	$18,717,193
Chicopee Chicopee Academy	Elementary School	Fontaine Brothers, Inc.	$30,776,990	825	PFA	176,425	$174	$22,116,660	$125	Design/Bid/Build	01-Jul-14	11-Aug-15	0	0%	$0	0.000%	The District has recently issued a Notice to Proceed to the contractor.	$28,500,581
Danvers Danvers High	High School	Bacon Construction Co, Inc.	$53,834,164	1,000	Bid	246,251	$219	$43,710,809	$178	Design/Bid/Build	14-Nov-10	10-Jul-13	0	100%	$1,717,573	3.191%	All work has been completed. Litigation is ongoing to resolve a dispute over the bleacher/floor issue.	$34,409,979
Douglas Douglas Elementary	Elementary School	CTA Construction Co., Inc.	$24,275,111	552	Bid	83,100	$292	$19,026,763	$229	Design/Bid/Build	02-Mar-12	26-Aug-13	0	99%	$343,494	1.440%	Punch list work is ongoing.	$15,297,961
Dracut Dracut Senior High	High School	CTA Construction Co., Inc.	$45,900,000	1,160	Bid	226,844	$202	$38,377,028	$169	Design/Bid/Build	27-Aug-12	26-Aug-14	0	85%	$177,659	0.387%	Work in progress includes finishes in the D wing, E wing Admin area, and C Upper Level. Site work in progress includes installation of the ball field retaining wall, infiltration basin, site utilities, and courtyard tree removal. Current schedule indicates that the project team intends to declare Substantial Completion August 26, 2014, with the exception of some site work, and the auditorium, which is anticipated to be completed in October 2014.	$34,137,202
East Bridgewater East Bridgewater High	High School	Fontaine Brothers, Inc.	$65,409,000	950	Bid	213,544	$306	$47,684,117	$223	Design/Bid/Build	10-Aug-11	25-Jun-13	0	96%	$2,247,610	3.681%	Demolition of the existing building is complete. Site crew working on bringing the site up to grade to complete the remaining ball fields and parking. Overall project completion will be delayed until September to coincide with the planting season. Work continues over the summer months on outstanding items regarding the HVAC units and Commissioning associated with the units.	$40,164,584
Easthampton Easthampton High	High School	Fontaine Brothers, Inc.	$30,934,000	510	Bid	110,400	$280	$24,511,000	$222	Design/Bid/Build	16-May-11	19-Feb-13	0	99%	$1,000,308	3.285%	The contractor continues to work on remaining open punchlist and warranty items along with remaining open change order items.	$22,859,504
Fairhaven Rogers	Elementary School	CTA Construction Co., Inc.	$19,099,606	370	Bid	77,871	$245	$14,996,521	$193	Design/Bid/Build	21-May-12	26-Jun-13	0	100%	$267,798	1.402%	The new school building is in service. All punch list and commissioning consultant action items are complete. Site work is complete and final acceptance inspection of landscaping work is planned for the Fall 2014.	$13,431,486
Franklin Franklin High	High School	Bacon-Agostini Construction Joint Venture	$86,778,700	1,650	Bid	306,543	$283	$73,191,801	$239	Design/Bid/Build	16-Oct-12	25-Jul-14	0	92%	$948,337	1.093%	Academic floors 2 and 3 are complete and the first floor is nearing completion. The Gym floor has been sanded and sealing is underway. Auditorium millwork is nearing completion but carpet installation remains. Kitchen equipment installation is underway. Plantings have been installed in the courtyard and around the new building. Furniture deliveries will proceed through July. Abatement of the existing building will also begin in July.	$54,558,408
Georgetown Penn Brook	Elementary School	Brait Builders Corp.	$32,875,975	770	Bid	98,000	$335	$26,976,145	$275	Design/Bid/Build	26-Sep-13	20-May-16	15 ahead	38%	$2,143,372	6.520%	The project is ahead of schedule and the quality of work is excellent. Steel erection is complete and the septic system is installed. The soil issues had been resolved and air monitoring continues. A change order is expected as a result of an agreement with an abutter pertaining to property lines, driveway and use of the newly installed access road.	$18,864,538
Greater Lawrence RVT Gr Lawrence Reg Voc Tech	Vocational / Technical	E. Amanti & Sons, Inc.	$4,361,641	1,340	PFA	360,000	$12	$3,551,593	$10	Design/Bid/Build	04-Jun-14	12-Dec-14	0	0%	$0	0.000%	Notice To Proceed was issued on June 4, 2014 and work commenced on June 23, 2014.	$3,126,998
Greater New Bedford Gr New Bedford Voc Tech	Vocational / Technical	Agostini Construction Co., Inc.	$12,181,500	2,060	Bid	464,300	$26	$10,757,696	$23	Design/Bid/Build	13-Sep-13	19-Dec-14	0	40%	$159,933	1.313%	The Phase 1 new addition is on schedule for September 2014 completion and occupancy. Structural steel erection, slab placements, and exterior precast panel installations are complete. Wall framing is nearly complete. MEP rough-in, drywall installation, and window installation are progressing on schedule.	$12,736,352
Hingham Hingham Middle School	Middle School	Brait Builders Corp.	$48,436,000	1,020	Bid	176,385	$275	$41,227,552	$234	Design/Bid/Build	07-Jun-12	01-May-14	0	98%	$452,657	0.945%	FF&E deliveries and installation are underway. Site work for the bus loop is remaining. Demolition of the existing building to be performed over the summer months.	$22,503,315
Hudson John F Kennedy	Middle School	Bacon-Agostini Construction Joint Venture	$35,102,573	715	Bid	118,846	$295	$28,373,294	$239	Design/Bid/Build	28-Sep-11	22-Jun-13	0	99%	$1,025,731	2.922%	The new school building is in service. Closeout of Commissioning is in process. Final site work is complete.	$22,932,938
Lynnfield Lynnfield High	High School	E.A. Colangeli Construction Co. Inc	$3,110,346	740	Bid	10,950	$284	$2,322,687	$212	Design/Bid/Build	25-Jun-12	28-Jun-13	0	99%	$259,285	8.981%	Minor punch list work remaining.	$1,743,071
Marblehead Glover	Elementary School	G & R Construction, Inc.	$20,868,000	425	Bid	79,108	$264	$16,977,513	$215	Design/Bid/Build	25-Jun-12	20-Dec-13	0	99%	$767,120	3.676%	The new school building is complete and in service. Site work is complete and final acceptance inspection of landscaping work is planned for the Fall 2014.	$8,759,441
Marshfield Marshfield High	High School	Brait Builders Ventures	$84,980,000	1,310	Bid	267,469	$318	$64,604,850	$242	Design/Bid/Build	16-Aug-12	25-Jul-14	30 ahead	90%	$734,870	0.923%	The academic areas, and the gym and auditorium have been completed to the punch list stage. Elevators have been inspected and approved for use. Furniture delivery and installation has been completed. Gym flooring was completed with all required markings and coats of sealant. Kitchen equipment has been installed and tested. Technology checkout and coordination is underway. Courtyard plantings were set. Moving materials from the old High School to the new building is underway.	$46,550,599
Maynard Maynard High	High School	CTA Construction Co., Inc.	$36,650,000	410	Bid	121,520	$302	$30,630,013	$252	Design/Bid/Build	18-Aug-11	13-Dec-13	0	100%	$541,428	1.477%	Exterior landscaping work is being finalized and project closeout is in process.	$22,095,036
Monomoy Monomoy Regional High School	High School	Fontaine Brothers, Inc.	$49,374,000	700	Bid	168,000	$294	$41,433,695	$247	Design/Bid/Build	11-Feb-13	30-Jun-14	31 behind	87%	$363,501	0.757%	Interior finish work continues throughout the building. Flooring installations are progressing. Final cleaning has commenced in the 2nd floor academic areas.	$27,654,507
Newburyport Francis T Bresnahan Elem	Elementary School	CTA Construction Co., Inc.	$28,190,000	660	Bid	112,517	$251	$20,841,757	$185	Design/Bid/Build	14-Mar-13	30-Jun-14	42 behind	93%	$71,537	0.261%	Building envelope is complete. Metal stud, drywall and MEP rough-ins are complete. Interior finishes are nearly complete. MEP finishes are nearing completion. Gym flooring ongoing. Kitchen equipment underway. The elevator is complete. Abatement and demolition of the existing building has begun and is scheduled to be completed by the end of July. Site work is ongoing and is approximately 75% complete.	$15,676,427
Norfolk County Agriculture Norfolk County Agr	Vocational / Technical	Brait Builders Corp.	$21,508,952	550	Bid	114,816	$187	$15,546,739	$135	Design/Bid/Build	29-Mar-12	09-May-14	90 behind	85%	$741,281	3.601%	Phase 1: Animal Science Building, Agricultural Mechanical Building, Equine Center, and Equipment Garage are substantially complete. Phase 3: Site work is substantially complete. Phase 2: Replacement General Contractor, Brait Builders, is completing renovation and site Phase 2 work. OPM reports that Phase 2 completion is estimated for early August 2014. Surety continues to negotiate contract agreement with Brait Builders for completion of project. Brait Builder's is responsible for all work in Phase 2 and punchlist work for Phases 1 and 3.	$13,493,272
North Adams Silvio O Conte Middle	Middle School	PDS Engineering and Construction, Inc.	$21,853,267	310	PFA	78,119	$280	$14,521,110	$186	Design/Bid/Build	28-Apr-14	17-Jul-15	0	0%	$0	0.000%	The contractor has mobilized to the site. Initial site preparation has begun consisting of silt fence and hay bale installation. Abatement and demolition of the portable classroom, and gymnasium is pending with exterior restoration work to proceed through the summer. Interior abatement and demolition will also proceed through the summer.	$20,632,054
Oxford Oxford Middle	Middle School	J.J. Cardosi, Inc.	$5,085,217	652	PFA	117,000	$43	$5,085,217	$43	Design/Bid/Build	01-Jun-12	22-Aug-14	0	79%	$139,512	2.744%	Roof replacement completed in the Summer of 2012. Window project completed in the Summer of 2013. HVAC/ADA General Contractor is completing renovation during the Summer of 2014.	$3,369,847
Peabody J Henry Higgins Middle	Middle School	Agostini Construction Co., Inc.	$76,735,661	1,340	PFA	221,518	$346	$47,562,204	$215	Design/Bid/Build	10-Mar-14	31-May-16	0	3%	$0	0.000%	Early site package has been under construction and nearing completion. This work consisted of stripping the topsoil at the site of the future school and parking area, excavation to subgrade, and installation of underdrain piping and backfill material.	$41,311,831
Quincy Central Middle	Middle School	H.V. Collins Co., Inc.	$32,540,712	620	Bid	114,975	$283	$27,057,118	$235	Design/Bid/Build	18-Jun-12	18-Oct-13	0	99%	$828,830	2.547%	Commissioning and punch list work nearing completion.	$28,962,549

Projects in Construction
MSBA Grant Basis and Maximum Grant Amount
Data Reported as of July 9, 2014

Core Program and Waitlist Totals			$2,776,819,810														*Includes Alternates	$1,768,006,814
Project	**Grade**	**Contractor**	**Total Construction Cost***	**Projected Enrollment**	**PFA or Bid Data**	**Proposed Sq.Ft.**	**Construction Cost/Sq.Ft.**	**Building Cost**	**Building Cost/Sq.Ft.**	**Procurement Type**	**Construction Start Date**	**Substantial Completion**	**Schedule Variance (days)**	**Physical Progress**	**Change Orders**	**Change Orders %**	**Construction Status**	**Max Total Facilities Grant**
CAPITAL PIPELINE PROJECTS IN CONSTRUCTION																		
Core Program Totals			**$2,742,073,912**				**$17,528**		**$13,153**									**$1,731,926,230**
Revere Staff Sergeant James J. Hill School	Elementary School	CTA Construction Co., Inc.	$33,897,336	690	PFA	103,650	$327	$24,309,968	$235	Design/Bid/Build	25-Mar-14	16-Jun-15	0	12%	$428,348	1.264%	Preliminary site work and demolition have been completed. Foundations has been poured throughout the building. Structural steel is ongoing.	$28,099,048
Somerset-Berkley Somerset-Berkley High	High School	Bacon-Agostini Construction Joint Venture	$69,407,000	1,000	Bid	222,826	$311	$52,553,676	$236	Design/Bid/Build	16-Jul-12	20-Jun-14	0	90%	$594,110	0.903%	Building finishes progressed through June with the majority of work remaining for completion to be on the first floor including ceramic tile installation, floor surfaces and carpet installation. Commissioning activities continued on mechanical/electrical/plumbing trade work.	$46,363,361
South Hadley Plains Elementary	Elementary School	Fontaine Brothers, Inc.	$21,563,821	270	PFA	63,377	$340	$14,664,281	$231	Design/Bid/Build	08-May-14	15-Jul-15	0	0%	$0	0.000%	The general contractor has recently mobilized.	$13,874,014
Southwick-Tolland Powder Mill	Middle School	PDS Engineering and Construction, Inc.	$13,556,194	545	Bid	95,775	$142	$11,289,029	$118	Design/Bid/Build	07-Jun-13	14-Aug-15	0	33%	($7,627)	-0.056%	Phase 2 (East Wing) renovation is underway. Window installations are ongoing. MEP trades continue rough-ins. Summer renovations to be completed by August 15, 2014.	$8,437,002
Southwick-Tolland Southwick-Tolland Regional High	High School	Fontaine Brothers, Inc.	$25,307,990	790	Bid	165,995	$152	$19,838,420	$120	Design/Bid/Build	05-Aug-13	18-Sep-15	0	40%	$488,225	1.970%	Phase 1 (additions) continues. Interior and exterior masonry as well as window installations have been completed. MEP rough-ins are complete at the Middle School wing and are ongoing at the High School wing. Phase 2 (existing building) renovations are underway. Window installations and roof replacement are ongoing. MEP trades continue rough-ins. Phase 2 Summer renovations to be completed by August 20, 2014. Excavation of drainage and underground utilities as well as new parking lot paving will be completed in Summer of 2014.	$19,572,669
Southwick-Tolland Woodland Elementary	Elementary School	PDS Engineering and Construction, Inc.	$7,172,052	400	Bid	67,800	$106	$6,077,790	$90	Design/Bid/Build	07-Jun-13	14-Aug-15	0	68%	$104,665	1.459%	Phase 3 (West Wing) is substantially complete. Phase 4 (East Wing) work has begun with MEP rough-ins and roof installation. Phase 4 renovations to be completed by August 15, 2014.	$4,620,410
Sturbridge Burgess Elementary	Elementary School	Fontaine Brothers, Inc.	$22,946,000	860	Bid	131,630	$174	$17,591,000	$134	Design/Bid/Build	10-Aug-10	30-Oct-10	0	100%	$1,966,295	8.575%	The new school building addition and renovations are complete and in service. An investigation of a rubber floor tile adhesion failure in the Cafeteria and Band Room in the renovated building has been completed. Floor replacement in these areas is being planned for the Summer of 2014. A report of the results of investigations in other areas revealed no additional areas need replacement.	$14,764,380
Sutton Sutton Middle School	Middle School	Brait Builders Corp.	$41,230,800	840	Bid	179,040	$230	$32,998,403	$184	Design/Bid/Build	01-Jul-11	23-Feb-15	35 ahead	77%	$1,099,286	2.736%	Selective demolition work is complete. Concrete foundations and footings are complete. Underground utility work is ongoing. Fire protection installations are underway. Roofing work at the high school building has started.	$25,646,928
Wachusett Mountview Middle	Middle School	CTA Construction Co., Inc.	$43,122,257	800	PFA	126,200	$342	$28,959,805	$229	Design/Bid/Build	21-May-14	19-Apr-16	0	0%	$0	0.000%	Contractor has mobilized to the project site. Erosion control has been installed. Tree clearing has been completed and stripping of loam has begun. Installation of temporary power has begun.	$25,445,463
Webster Park Avenue Elementary	Elementary School	CTA Construction Co., Inc.	$32,370,001	720	Bid	109,597	$295	$24,190,915	$221	Design/Bid/Build	08-Jul-13	12-Dec-14	0	55%	$268,374	0.848%	The Gymnasium and Auditorium slabs have been poured and construction work continues in those spaces as well as the remaining portions of the school building. Work includes installations of rough mechanical, electrical, plumbing and fire protection systems, exterior wall and roof systems and installation of interior gypsum board walls. Window, storefront and curtain wall installations are also underway. Brick veneer is approximately 70% complete, flat roofs are approximately 70% complete and sloped metal roofs are approximately 50% complete. Installation of underground utilities is well underway.	$28,102,666
West Bridgewater West Bridgewater Jr-Sr	High School	CTA Construction Co., Inc.	$46,267,000	625	Bid	141,250	$328	$34,404,274	$244	Design/Bid/Build	01-Oct-13	15-Jun-15	40 behind	18%	$18,647	0.041%	Demolition of the existing athletic fields and courts are complete. Top soil is stockpiled on site. Structural steel and masonry are complete. Underslab piping and slabs are complete. Steel stairs are nearing completion. Metal studs and mechanical/electrical rough-ins are underway. Site work and site utilities are ongoing.	$26,384,658
West Springfield West Springfield High	High School	Fontaine Brothers, Inc.	$85,006,020	1,270	Bid	257,525	$330	$56,875,181	$221	Design/Bid/Build	22-Nov-11	31-Dec-13	0	95%	$2,552,562	3.623%	Abatement of the existing building is complete and demolition of the existing building is nearly complete. Minor punch list work remains within the new building and is scheduled to be completed over the summer months.	$60,722,795
Westfield Abner Gibbs	Elementary School	Fontaine Brothers, Inc.	$25,578,000	600	Bid	95,573	$268	$21,444,000	$224	Design/Bid/Build	24-Aug-12	25-Mar-14	0	0%	$0	0.000%	Work stoppage regarding Article 97 "Protected Land". The City still does not have approval. General Contractor has demobilized from the site.	$20,004,642
Weston Field Elem School	Elementary School	Colantonio, Inc.	$24,537,966	355	Bid	65,390	$375	$19,872,289	$304	Design/Bid/Build	21-Dec-12	19-Jun-14	43 behind	95%	$959,054	3.908%	A temporary certificate of occupancy was issued on June 19, 2014 with the understanding that the 25 (base contract) items will be completed by August 1st. If all items are found to be complete at the August 1st walk through with the Building Inspector and Designer, a final certificate of occupancy will be issued and the building will be deemed substantially complete.	$8,004,886
Williamsburg Anne T Dunphy	Elementary School	Enfield Builders, Inc.	$8,990,457	170	Bid	37,859	$237	$7,625,327	$201	Design/Bid/Build	05-Apr-13	15-May-14	52 behind	94%	$337,811	3.757%	The building envelope is complete. Metal studs, drywall and MEP/FP rough-ins are complete. Interior finishes and MEP/FP finish work is nearing completion. FF & E is underway. Earth work, underground utilities and the retaining wall construction are nearing completion.	$6,808,088
Winchester Vinson-Owen	Elementary School	CTA Construction Co., Inc.	$21,289,999	420	Bid	74,820	$285	$17,586,598	$235	Design/Bid/Build	17-Feb-12	26-Jul-13	0	100%	$182,522	0.867%	Punch list work is nearing completion.	$9,091,823
Andover Bancroft Elementary	Elementary School	Skanska USA Building, Inc.	$40,077,007	680	Bid	106,904	$375	$27,101,717	$254	CM-at-Risk	14-May-12	23-Jun-14	0	99%	$267,843	0.668%	FF&E installation is nearly complete. Temporary fire pump was installed to obtain a Temporary Certificate of Occupancy permit. Domestic water pump and permanent water pump to be installed and complete by August 15th. Site work is ongoing over the next several months and demolition of the existing building to begin in July.	$15,731,353
Ashburnham-Westminster Briggs Elem	Elementary School	Consigli Construction Company, Inc.	$24,780,000	520	Bid	87,085	$285	$18,202,478	$209	CM-at-Risk	09-Mar-12	30-Aug-13	0	100%	$44,103	0.178%	The new school building is in service. Potential change orders related to extending boiler breaching and installation of a water leak detection system for the RTUs in the attic is under review. Site work is complete and final acceptance inspection of landscaping work is planned for the Fall 2014.	$16,187,237
Auburn Auburn Middle	Middle School	Fontaine Brothers, Inc.	$36,412,806	560	PFA	100,395	$363	$23,350,958	$233	CM-at-Risk	27-Feb-14	05-Jun-15	0	17%	$0	0.000%	Site work has continued to progress with site drainage and sanitary installations well underway. Underground plumbing and electrical installations have begun. Forming and placing of concrete foundations progressed through May and June. Delivery and erection of structural steel is pending.	$19,763,951
Ayer-Shirley Ayer-Shirley Regional Middle/High School	High School	Consigli Construction Company, Inc.	$44,516,576	495	PFA	144,072	$309	$32,082,505	$223	CM-at-Risk	19-Feb-13	26-Aug-15	14 behind	37%	$150,196	0.339%	This project is a 6-Phase Add/Reno that is currently 37% complete at Phase 3. There are two general classroom sections that are scheduled to be turned over to the District in September that will require premium time from now until it is complete. Work includes site, HVAC, electrical, roof, fire protection, plumbing, masonry, windows, etc.	$34,926,694
Concord-Carlisle Concord Carlisle High	High School	Turner Construction Company	$76,143,704	1,225	Bid	219,871	$346	$53,607,000	$244	CM-at-Risk	20-Feb-13	15-Mar-15	10 ahead	59%	$345,490	0.454%	All concrete slabs have been placed. Exterior envelope is complete (masonry, roofing, curtain wall and metal panels). Drywall is nearing completion. Paint, flooring, millwork and ceiling grid installation are ongoing. Plumbing, fire protection, HVAC and electrical finish are underway. RTU start up has been performed. Permanent power has been brought to the site. Site Work for Phase I is nearly complete. Site Work for Phase II and Demolition of existing school is scheduled to begin after the new building is occupied in March/April 2015.	$26,795,748
Duxbury Duxbury High	High School	Dimeo Construction Company	$105,475,520	1,735	Bid	322,105	$327	$73,368,123	$228	CM-at-Risk	12-Sep-12	09-Jun-14	0	88%	$2,233,671	2.243%	The building is substantially complete. Commissioning and punchlist activities are ongoing. Furniture and equipment deliveries are underway.	$48,141,830
Essex Agr Tech Essex Agr and Tech Inst	Vocational / Technical	Gilbane Building Company	$110,217,451	1,440	Bid	337,000	$327	$79,334,889	$235	CM-at-Risk	07-May-12	30-Jun-14	0	92%	$1,762,649	1.599%	Phase I Farmstead: Punch list work remains to be completed. Phase II Farmstead: Agr. Storage Bldg (Hoop House) has been erected and MEP equipment has been installed. Site work is ongoing for the Danvers playing fields. Academy: Auto Tech & Collision fit-out nearly complete. Epoxy floors and lifts to be installed. Landscape/Mason Bldg metal panel system and slabs complete. Rough installations are nearly complete. Main Academy: Painting and final cleaning are ongoing as well as punch list work. The Gym floor and second floor track are complete. The contractor is on schedule to its contractual substantial completion date of August 1, 2014.	$72,471,233
Greater Lowell Voc Tec Gr Lowell Reg Voc Tech	Vocational / Technical	Consigli Construction Company, Inc.	$52,472,010	1,990	PFA	505,766	$104	$38,997,643	$77	CM-at-Risk	04-Nov-13	31-Aug-15	0	10%	$0	0.000%	Building Addition: Foundations and structural steel complete. Underslab piping and slab are complete. Roofing is underway. Mechanical piping is underway. Renovations to the existing school began in late June 2014 at the close of the school year. Abatement of the existing school is ongoing.	$46,002,209
Greenfield Greenfield High	High School	Shawmut Design and Construction	$53,507,787	585	Bid	160,649	$333	$37,812,150	$235	CM-at-Risk	27-Mar-13	15-Dec-15	0	46%	$292,990	0.548%	The Phase 1 new school building work is on schedule for July 31, 2014 Substantial Completion with occupancy in September of 2014. The building exterior is complete except minor finish work. Access roadway and parking area are ready for final paving. Sidewalks are complete and final landscaping is in process. Interior construction is progressing on schedule. MEPs and flooring work is nearly complete and millwork installation is progressing, Interior walls are primed and finish painting is in process.	$42,194,483
Leominster Leominster Senior High	High School	S.O.M. Construction Ent,, Inc.	$33,794,797	1,825	Bid	295,859	$114	$25,382,707	$86	CM-at-Risk	01-Jul-11	30-Aug-13	0	100%	$2,478,803	7.335%	Remaining punch list work is being completed and project closeout is in process.	$27,337,956

Projects in Construction
MSBA Grant Basis and Maximum Grant Amount
Data Reported as of July 9, 2014

Project	Grade	Contractor	Total Construction Cost*	Projected Enrollment	PFA or Bid Data	Proposed Sq.Ft.	Construction Cost/Sq.Ft.	Building Cost	Building Cost/Sq.Ft.	Procurement Type	Construction Start Date	Substantial Completion	Schedule Variance (days)	Physical Progress	Change Orders	Change Orders %	Construction Status	Max Total Facilities Grant
Core Program and Waitlist Totals			**$2,776,819,810**														*Includes Alternates	**$1,768,006,814**
CAPITAL PIPELINE PROJECTS IN CONSTRUCTION																		
Core Program Totals			**$2,742,073,912**				**$17,528**		**$13,153**									**$1,731,926,230**
Lexington Joseph Estabrook	Elementary School	Shawmut Design and Construction	$32,792,348	540	Bid	91,840	$357	$22,795,606	$248	CM-at-Risk	12-Jun-12	27-Jan-14	0	95%	$842,093	2.568%	The new building is occupied. Demolition and abatement of existing building is complete. Site work is ongoing.	$12,148,491
Longmeadow Longmeadow High	High School	Gilbane Building Company	$63,685,998	1,000	Bid	236,985	$269	$46,573,364	$197	CM-at-Risk	01-Nov-10	01-Nov-13	0	99%	$1,577,729	2.508%	Remaining punch list work is being completed and project closeout is in process.	$31,297,686
Lynn Thurgood Marshall Mid	Middle School	Walsh Brothers, Inc.	$71,225,244	1,100	PFA	181,847	$392	$49,913,764	$274	CM-at-Risk	27-Jun-14	06-Jun-16	0	7%	$18,530,760	27.362%	Interim Guaranteed Maximum Price (IGMP) No. 1 has been executed and includes site work, foundations, concrete, structural steel, underground electrical and underground plumbing work. Ongoing work includes installation of construction gates, fencing, gravel site exits, and dust control. Site trailers are set up and temporary power, water and internet services are established. Erosion control and soil stabilization measures are in place. Underground storage tanks have been removed and 3 structures have been abated and demolished. Grubbing and clearing operations are complete. Culvert parameters have been established and a bridge assembly built to accommodate construction vehicle travel. Existing foundation structures have been removed and processing of the material for backfill is underway. Vibration monitoring of all activities on site is ongoing for seismic reporting. Cut and capped all sewer and water lines to property and all drain lines to culvert.	$49,690,902
Methuen Methuen High	High School	Consigli Construction Company, Inc.	$74,749,773	2,075	Bid	324,424	$230	$58,040,776	$179	CM-at-Risk	12-Jul-11	26-Jun-14	0	95%	$3,144,973	4.207%	Phase II construction has received a temporary Certificate of Occupancy on June 23rd. Phase I punchlist has been monetized and much substantial work was completed during the April vacation. A few items remain to be completed during the summer months.	$61,544,094
Newburyport Rupert A Nock Middle	Middle School	Gilbane Building Company	$20,877,414	845	Bid	161,500	$129	$14,924,391	$92	CM-at-Risk	18-Mar-13	21-Aug-14	0	75%	$827,178	3.962%	Full time day summer schedule is in operation. Punch list and commissioning work continue on Phases 1-3. Phase 4 work continues and includes mechanical, electrical, plumbing, fire protection, ceiling tile, flooring, lighting and casework installations. Construction activity continues in the Boys' and Girls' Locker Rooms and the Auditorium. Installation of the new roof system and related PV panel removal and reinstallation work has begun and continues on a full time summer schedule. Commissioning work is ongoing.	$12,785,667
North Reading North Reading High	High School	Gilbane Building Company	$101,328,353	1,370	Bid	267,939	$378	$66,726,592	$249	CM-at-Risk	15-Jan-13	31-Aug-15	0	66%	$1,501,515	1.482%	Installation of finishes has progressed to near completion in the High School academic building and the High School/Middle School shared areas including the Auditorium, Gym, Kitchen, and administrative spaces. Furniture and equipment have been moved into the building. Trades continue Saturday work schedule to advance progress. Exterior work has progressed on Route 62 intersection along with access road and sidewalks.	$47,071,882
Norton Norton High	High School	W. T. Rich Company Inc.	$27,023,541	700	Bid	162,405	$166	$20,590,559	$127	CM-at-Risk	12-Mar-12	31-Jan-14	0	100%	$1,366,532	5.131%	Punch list work is 100% complete. An extension has been granted for temp. occupancy of the Auditorium through May 11, 2014. RTU noise issue and a floor finish issue are being resolved.	$20,634,829
Shrewsbury Sherwood Middle School	Middle School	Gilbane Building Company	$33,986,286	900	Bid	129,378	$263	$22,823,030	$176	CM-at-Risk	07-Mar-11	31-Oct-12	0	100%	($1,033,847)	-3.061%	The new school building is in service. Site work is complete and final acceptance inspection of landscaping work is planned for the Fall of 2014.	$20,964,674
Southern Worcester Cty VT Bay Path Reg Voc Tech H S	Vocational / Technical	Consigli Construction Company, Inc.	$57,024,455	1,110	Bid	249,521	$229	$41,468,049	$166	CM-at-Risk	02-Aug-13	01-Sep-15	0	27%	$357,291	0.631%	The project is currently in Phase 1 of an 11-Phase project. Phase 1 is the addition of the new Media Center, Science Classrooms and Typical Classrooms. Phase 1 is approx. 70% complete. Phase 1 is scheduled to be turned over to the District on September 1, 2014. Scope in additional phases 2-11 include the replacement of multiple building systems throughout the building as well as site work.	$44,420,530
Springfield Dryden Memorial	Elementary School	Morganti/Aquadro & Cerruti	$11,476,091	280	Bid	40,900	$281	$8,276,912	$202	CM-at-Risk	28-Jun-12	01-Nov-13	0	99%	$271,991	2.370%	Remaining site punch list and commissioning work is being completed and project closeout is in process.	$10,344,789
Springfield Elias Brookings	Elementary School	Morganti/Aquadro & Cerruti	$22,733,394	320	Bid	64,800	$351	$18,337,328	$283	CM-at-Risk	01-Jul-13	20-Jan-15	35 behind	33%	($256,355)	-1.128%	Building steel erection is complete. MEP rough-in work is proceeding in the south classroom portion of the building. Under slab utilities are placed and ready for slabs to be poured. Roofing, interior partition wall framing and exterior wall framing are underway.	$25,563,992
Stoneham Stoneham Middle School	Middle School	Shawmut Design and Construction	$33,086,864	775	Bid	136,410	$243	$23,430,771	$172	CM-at-Risk	01-Nov-12	08-Aug-14	0	87%	$380,966	1.151%	The new school building's exterior is complete except some roof trim. Roofing is complete with nine RTUs installed. Interior work is progressing with drywall complete, MEP finishes progressing on schedule, wall tile 85% complete, painting and ceiling grid placement close to 60% complete, floor tile installation 65% complete, and the elevator is complete. Commissioning Consultant inspections are ongoing.	$21,346,937
Wakefield Galvin Middle School	Middle School	Bond Brothers, Inc.	$59,756,584	1,070	Bid	187,722	$318	$44,899,853	$239	CM-at-Risk	18-Mar-13	30-Jun-15	0	54%	$1,448,896	2.425%	The new school building is being completed in three phases (A, B & C) working from upper to lower floors. Phase A exterior and interior construction is nearing completion. Framing of walls in Phase B is progressing and MEP rough-ins have started. Phase C slab placement has been completed. Permanent power, boilers, water heaters, and switchgear have been installed.	$32,631,618
Wilmington Wilmington High	High School	Gilbane Building Company	$67,558,835	960	Bid	192,443	$351	$48,060,314	$250	CM-at-Risk	30-Apr-13	13-Feb-15	0	45%	$481,543	0.745%	Structural steel work overall is 95% complete. All MEP rough-ins are well underway. Site work continues including utility work and the installation of the drainage system.	$35,708,354
Waitlist Totals			**$34,745,898**				**$234**		**$176**									**$36,080,584**
Springfield Forest Park Middle	Middle School	Consigli Construction Company, Inc.	$34,745,898	660	Bid	148,800	$234	$26,209,932	$176	CM-at-Risk	26-Mar-12	26-Aug-13	0	99%	$1,048,807	3.019%	Punch list work is ongoing.	$36,080,584
